

**County /City Stormwater Management Plan (SWMP / CSWMP)  
Rock Island Trail  
Waynoka Pl to Constitution Ave  
Capital Project  
Colorado Springs, Colorado**

Permittee:  
City of Colorado Springs  
Parks, Recreation and Cultural Services  
1401 Recreation Way  
Colorado Springs, CO 80905  
(719) 385-6951

GEC Administrator and Qualified Stormwater Manager  
Emily Duncan 719-385-6951  
City of Colorado Springs  
Parks, Recreation and Cultural Services  
1401 Recreation Way  
Colorado Springs, CO 80905  
[Emily.Duncan@coloradosprings.gov](mailto:Emily.Duncan@coloradosprings.gov)

Contractor:

Company Name:

SWMP Point of Contact Name:

Phone:

Address:

CSWMP /SWMP Preparing Engineer:



1604 South 21st Street  
Colorado Springs, Colorado 80904  
(719) 630-7342

Contact: Todd Cartwright, P.E.

Kiowa Project No. 16028  
Project Dox: STM-REV24-0296  
EPC Project Number: CDR193

November 22, 2024

**Engineer's Statement**

This SWMP / CSWMP was prepared under my direction and supervision and is correct to the best of my knowledge and belief. If such work is performed in accordance with the SWMP / CSWMP, the work will not become a hazard to life and limb, endanger property, or adversely affect the safety, use, or stability of a public way, drainage channel, or other property.

Printed Name: Todd Cartwright, PE Date: \_\_\_\_\_

Phone Number: (719) 694-0012

Seal



**City Project Manager's Statement**

I hereby certify that the drainage, grading, and erosion control for Rock Island Trail - Constitution Avenue to Sand Creek shall be constructed according to the design presented in this SWMP / CSWMP. I further understand that field changes must be reviewed by the SWENT Review Engineer to ensure conformance with the original design intent. I am employed by and perform engineering services solely for the City of Colorado Springs, and therefore am exempt from Colorado Revised Statute Title 12, Article 25, Part 1 according to § 12-25-103(1), C.R.S.

Name of City Project Manager: Emily Duncan

Signature: [Handwritten Signature] Date: 11/13/2024

**Contractor's Statement**

I will comply with the requirements of the Grading and Erosion Control Plan SWMP / CSWMP including Construction Control Measure inspection requirements and final stabilization requirements. I acknowledge the responsibility to determine whether the construction activities on these plans require Colorado Discharge Permit System (CDPS) permitting for stormwater discharges associated with construction activity.

Name of Contractor: \_\_\_\_\_

Authorized Signature: \_\_\_\_\_ Date: \_\_\_\_\_

Title: \_\_\_\_\_

Phone Number: \_\_\_\_\_

Address: \_\_\_\_\_

Email Address: \_\_\_\_\_

**City of Colorado Springs Grading and Erosion Control Review**

This SWMP / CSWMP is filed in accordance with the City Code. This plan is reviewed in accordance with the Stormwater Construction Manual; latest revisions.

Date:

For the SWENT Manager

Notes: \_\_\_\_\_

\_\_\_\_\_

## TABLE OF CONTENTS

|   |           |
|---|-----------|
| <b>Table of Contents</b> .....  | <b>i</b>  |
| <b>State Stormwater Discharge Permit Requirements</b> .....             | <b>ii</b> |
| <b>I. Stormwater Management Plan Objectives</b> .....                   | <b>1</b>  |
| A. State Permit Applicant.....  | 2         |
| B. SWMP / CSWMP Terms.....  | 2         |
| C. Contractor Required Items.....                                       | 3         |
| <b>II. Site Description</b> .....                                       | <b>3</b>  |
| A. Nature of the Construction Activity.....                             | 3         |
| B. Sequence of Major Activities.....                                    | 4         |
| C. Estimate of Area and Volume Disturbed.....                           | 5         |
| D. Soil Data.....   | 5         |
| E. Existing Vegetation and Ground Cover.....                            | 5         |
| F. Potential Pollution Sources.....                                     | 5         |
| G. Non-stormwater Discharges.....                                       | 6         |
| H. Receiving Waters.....  | 6         |
| <b>III. SWMP / CSWMP Site Map Contents</b> .....                        | <b>6</b>  |
| <b>IV. Stormwater Management Controls</b> .....                         | <b>7</b>  |
| A. GEC Administrator.....   | 7         |
| B. Identification of Potential Pollutant Sources:.....                  | 7         |
| C. Construction Control Measures (CCMs) for Pollution Prevention.....   | 8         |
| <b>V. Final Stabilization and LONG-TERM Stormwater Management</b> ..... | <b>12</b> |
| <b>VI. Recommended Inspection and Maintenance Procedures</b> .....      | <b>13</b> |
| A. Minimum Inspection Schedule.....                                     | 13        |
| B. CCM Operation and Maintenance.....                                   | 15        |
| <b>VII. References</b> .....  | <b>15</b> |
| <b>Appendix Table of Contents</b> .....                                 | <b>16</b> |

## STATE STORMWATER DISCHARGE PERMIT REQUIREMENTS

At least ten days prior to the anticipated start of construction activities (i.e. the initial disturbance of soils associated with clearing, grading, excavation activities, installation of structural Construction Control Measures, or other activities), for projects that will disturb one (1.0) acre or more, the owner or operator of the construction activity must submit an application as provided by the Colorado Department of Public Health and Environment, Water Quality Control Division (Division). This form may be reproduced and is also available from the Division's web site. Applications received by the Division are processed and a permit certification and other relevant materials will be sent to the attention of the legally responsible person. The application contains certification of completion of a storm water management plan (SWMP / CSWMP). Do not include a copy of the Stormwater Management Plan, unless requested by the Division.

For information or application materials contact:

Colorado Department of Public Health and Environment  
Water Quality Control Division  
WQCD-P-B2  
4300 Cherry Creek Drive South  
Denver, Colorado 80246-1530  
<https://www.colorado.gov/pacific/cdphe/wq-construction-general-permits>

Electronic Application – CDPHE website:

<https://www.colorado.gov/pacific/cdphe/WQ%20permits%20construction%20electronic%20application>

## I. STORMWATER MANAGEMENT PLAN OBJECTIVES

The objective of the Stormwater Management Plan (SWMP / CSWMP) is “to identify possible pollutant sources that may contribute pollutants to stormwater and identify Construction Control Measures (CCMs) that, when implemented, will reduce or eliminate any possible water quality impacts. The SWMP / CSWMP must be completed and implemented at the time the project breaks ground and revised as construction proceeds, to accurately reflect the conditions and practices at the site (CDPHE *Stormwater Management Plan Preparation Guidance*)”. A general schedule or phasing of CCMs will be determined by construction schedule and ground disturbances necessitating required erosion control methods/CCMs. The SWMP / CSWMP shall be implemented until expiration or inactivation of permit coverage. Evaluations of and modifications to this plan may be necessary during the length of the construction project until the site is finally stabilized.

SWMP / CSWMP Plan Availability: A copy of the Stormwater Discharge Permit from the State of Colorado, SWMP / CSWMP Report, SWMP / CSWMP Site Map, SWMP / CSWMP Notes and Details; and inspection reports shall be kept on site by the GEC Administrator at all times, as to be available for use by the operator/ GEC Administrator and to be available for inspection by federal, state and local agencies. If an office location is not available at the site, the SWMP / CSWMP must be managed so that it is available at the site when construction activities are occurring (for example: by keeping the SWMP / CSWMP in the superintendent’s vehicle). The permittee shall retain copies of the SWMP / CSWMP and all reports required by the Permit and records of all data used to complete the Permit application for three (3) years minimum after expiration or inactivation of permit coverage, unless the community requires a longer period.

This SWMP / CSWMP should be viewed as a “living document” that is continuously being reviewed and modified as a part of the overall process of evaluating and managing stormwater quality issues at the site. The GEC Administrator shall amend the SWMP / CSWMP when there is a change in design, construction, operation or maintenance of the site which would require the implementation of new or revised CCMs or if the SWMP / CSWMP proves to be ineffective in achieving the general objectives of controlling pollutants in stormwater discharges associated with construction activity or when CCMs are no longer necessary and are removed. If the GEC Administrator feels that modifications to the CCMs shown on the SWMP / CSWMP are necessary to provide for a more effective plan, the process will include: 1) Evaluate pollutant sources, 2) Select CCMs, 3) Document CCMs, 4) Implement CCMs.

SWMP / CSWMP revisions must be made prior to changes in the site conditions, except for “Responsive SWMP / CSWMP Changes” as follows:

- SWMP / CSWMP revision must be made immediately after changes are made in the field to address CCM installation and/or implementation issues; or
- SWMP / CSWMP revisions must be made as soon as practicable, but in no case more than 72 hours, after change(s) in CCM installation and/or implementation occur at the site that require development of materials to modify the SWMP / CSWMP
  - ◊ A notation must be included in the SWMP / CSWMP prior to the site change(s) that includes the time and date of the change(s) in the field, and identification of the CCM(s) removed or added and the location(s) of the CCM(s). Modifications to the SWMP / CSWMP shall be submitted to the City within seven days.

An El Paso County Erosion and Stormwater Quality Control Permit (ESQCP) is required along with a Colorado Discharge Permit System (CDPS), Stormwater Discharge Associated with Construction Activities Permit from the Colorado Department of Public Health and Environment for this project. The general conditions associated with the permits must be followed through the duration of the

land disturbing activities at the site. For additional details or more specific information on the CDPS permit, consult the CDPS General Permit No. COR-030000.

#### **A. State Permit Applicant**

The State Permit applicant (also referred to as the Permittee) must be a legal entity that meets the definition of the owner and/or operator of the construction site, in order for this application to legally cover the activities occurring at the site. The applicant must have day-to-day supervision and control over activities at the site and implementation of the SWMP / CSWMP. Although it is acceptable for the applicant to meet this requirement through the actions of a contractor, as discussed in the examples below, the applicant remains liable for violations resulting from the actions of their contractor and/or subcontractors. Examples of acceptable applicants include:

Owner or Developer - An owner or developer who is operating as the site manager or otherwise has supervision and control over the site, either directly or through a contract with an entity such as those listed below.

General Contractor or Subcontractor - A contractor with contractual responsibility and operational control (including SWMP / CSWMP implementation) to address the impacts construction activities may have on stormwater quality.

Other Designated Agents/Contractors - Other agents, such as a consultant acting as construction manager under contract with the owner or developer, with contractual responsibility and operational control (including SWMP / CSWMP implementation) to address the impacts construction activities may have on stormwater quality.

Refer to the CDPHE, *Stormwater Management Plan Preparation Guidance* for additional information.

The Permittee shall be legally responsible for compliance with the State Permit.

#### **B. SWMP / CSWMP Terms**

Construction Control Measures (CCMs): CCMs encompass a wide range of erosion and sediment control practices, both structural and non-structural in nature, that are intended to reduce or eliminate any possible water quality impacts from stormwater leaving a construction site. The individual CCMs appropriate for a particular construction site are largely dependent of the types of potential pollutant sources present, the nature of the construction activity, and specific-site conditions.

Nonstructural CCMs, such as preserving natural vegetation, preventive maintenance and spill response procedures, schedules of activities, prohibition of specific practices, education, and other management practices are mainly operational or managerial techniques.

Structural CCMs include treatment processes and practices ranging from diversion structures and silt fences, to retention ponds and inlet protection.

Construction Start Date: This is the day when ground disturbing activities are expected to begin, including grubbing, stockpiling, excavating, demolition, and grading activities.

Disturbance Area Determination: Aside from clearing, grading and excavation activities, disturbed areas also include areas receiving overburden (e.g., stockpiles), demolition areas,

and areas with heavy equipment/vehicle traffic and storage that disturb existing vegetative cover.

**Final Stabilization Date:** In terms of permit coverage, this is when the site is finally stabilized. This means that all ground surface disturbing activities at the site have been completed, and all disturbed areas have been either built on, paved, or a uniform vegetative cover has been established with an individual plant density of at least 70 percent of pre-disturbance levels (refer to Final Stabilization Section). Permit coverage must be maintained until the site has reached Final Stabilization. Even if only one part of the project is being done, the estimated final stabilization date must be for the overall project. If permit coverage is still required once your part is completed, the permit certification may be transferred or reassigned to a new responsible entity(s).

**SWMP / CSWMP Drawings:** Also known as the SWMP / CSWMP Site Map.

### **C. Contractor Required Items**

The Contractor shall include and/or provide the following items prior to beginning land disturbing activities:

- Add the GEC Administrator and Alternate with phone numbers to this plan.
- Construction Dates – Verify the construction dates indicated in this report. Update as necessary to reflect the planned schedule.
- Material Handling and Spill Prevention procedures – See Section IV-4. Review and modify as necessary.

## **II. SITE DESCRIPTION**

### **A. Nature of the Construction Activity**

The proposed project will construct approximately 10,900 linear feet of concrete trail. In the final disposition of the project, the City of Colorado Springs will own and maintain the installation.

#### **i. Site Description**

Rock Island Trail is comprised of 36.8 acres, located in southeast Colorado Springs, Colorado between Sand Creek and Constitution Ave. The property is bordered multiple commercial and residential lots and city property. The project is anticipated disturb 18.2 Acres.

The property is located in Sections 5 and 6, Township 14, Range 65 of the 6th Principal Meridian, in Colorado Springs, El Paso County, Colorado. The vegetation in the site consists of native grasses. A vicinity map showing the general location of the site is presented in Appendix A.

The project consists of 10,907 feet of paved trail from 8 to 12 feet wide. The trail includes a 210 foot bridge over Sand Creek. The trail runs from Waynoka on the west to Constitution on the east primarily along the Rock Island Railroad grade.

The property is primarily the abandoned Rock Island Railroad alignment. And is now an almost 2 mile long narrow strip of land that is city owned open space. The total disturbed area associated with this project is approximately 18.2 acres. The total construction site is 22.8 acres. There is no proposed development within any streamside buffer zone or in any designated floodplain, as indicated on FEMA panel 08041C0752G. A FEMA firmette for the



site is located in Appendix A. The site has about 50% vegetative ground cover based on site visit field observation.

The sites ultimate receiving waters is Sand Creek. Because the site will remain primarily open space there will be little runoff. Because of the long narrow shape of the site the runoff leaves the site in a variety of paths. The majority of the runoff will use these paths; directly to Sand Creek, to an existing onsite concrete channel, sheet flow to adjacent residential lots, drain onto Constitution Ave.

The project and the trail include the erection of a 210 long single span pedestrian bridge over Sand Creek. The Bridge and abutments are intended to be above and outside the 100-year flood plain.

The project schedule is as follows:

- begin 01/01/2025
- Initial erosion control measures 01/01/2025
- Interim erosion control measures 02/01/2025
- complete 10/01/2025
- final stabilization 10/01/2025
- There are no utilities or vertical construction with this project so interim and final are the same

**ii. Adjacent Areas**

The proposed trail is surrounded by parks, residential and commercial properties.

**B. Sequence of Major Activities**

Prior to the commencement of the majority of clearing and grubbing activities, minimal clearing and grubbing may be necessary to install initial erosion control devices such as silt fencing and vehicle tracking control, clearing and grubbing will commence, and grading will proceed as shown on the SWMP / CSWMP Site Plan. When the finished grades are attained, the concrete pavement will begin. In general, the GEC Administrator will identify the precise schedule.

The major construction activities associated with this project are shown in the table below along with an approximate timing of the sequence. In general, the GEC Administrator and the Contractor will identify the precise schedule to be used during the term of this project and modify this schedule as needed. Minimal clearing and grubbing may be necessary to install the initial erosion control features.

Approximate Sequence of Major Construction Activities:

|   |                          |
|---|--------------------------|
| Installation of initial CCMs                                      | Oct 1, 2024              |
| Clearing, grubbing and earthworks                                 | December 1, 2024         |
| Site work   | December 2024- June 2025 |
| End Construction (refer to <i>Final Stabilization...</i> section) | September 2025           |

The temporary erosion control measures can be removed when Final Stabilization has occurred. Refer to the Final Stabilization section for a description of the requirements.

### **C. Estimate of Area and Volume Disturbed**

The total site area associated with the project is approximately 36.2 acres. The estimated area of disturbance is 18.2 acres. The estimated area of disturbance corresponds to that necessary to construct the concrete trails as shown on the SWMP / CSWMP Site Maps. Most of the existing trails will be restored to vegetative areas. All other areas are to remain undisturbed.

Earthwork cut and fill operations will be roughly 605 cubic yards of Cut and 2,777 cubic yards of Fill.

### **D. Soil Data**

Soils within the property are classified to be within Hydrologic Soils Group A and B as shown in the El Paso County Soils Survey. The soil type is identified as Ellicott Soils and Blakeland Loamy which is a somewhat excessively drained loamy coarse sand of floodplains and terraces. Both series has a moderate to high erosion hazard. The other native soil found on site is the Blendon soils which is a well-drained soil of fans and terraces. The Blendon soil has a moderate erosion hazard.

### **E. Existing Vegetation and Ground Cover**

A survey including a general description of existing vegetation shall be conducted by the GEC Administrator for Construction prior to any ground disturbance on the project. The manager shall photo document existing vegetation where all work will be occurring. The manager shall also perform the vegetation survey transect(s) including photo documentation as outlined in Chapter 4. 11.2 of CDOT's Erosion Control and Stormwater Quality Guide. The overall existing vegetative cover is estimated at about 50% by field observation.

It is recommended that the contractor take pictures of the existing vegetative cover prior to construction and any calculations they feel necessary to make the Final Stabilization comparison (refer to Final Stabilization section for additional information). The contractor will be responsible for providing the documentation to make this comparison to the City and the State of Colorado, Water Quality Control Division.

### **F. Potential Pollution Sources**

The potential pollution sources for the site that may have an impact to stormwater include the following items:

1. Concrete washouts – Concrete, slurry
2. Construction Dewatering – Sediment
3. Ground disturbing activities and grading - Sediment
4. Haul routes – Sediment, fuel, oil
5. Landscaping – Fertilizers, sediment, over-watering, pesticides
6. Loading and unloading operations
7. Management of contaminated soils
8. Off-site vehicle tracking - Sediment
9. Outdoor storage activities
10. Portolet – Chemicals, human waste
11. Significant dust or particulate generating processes

12. Soil, aggregate and sand stockpiling – Sediment
13. Storage of disposal items – Sediment
14. Storage of fertilizers, materials or chemicals - Chemicals
15. Vehicle maintenance or fueling – Fuel, oil, chemicals

#### **G. Non-stormwater Discharges**

In the existing condition there are no known non-stormwater discharges from the project site, such as springs and landscape irrigation return flows. During construction, the following non-stormwater discharges from the project site could occur.

1. Release of concrete washout water – Not anticipated. The washout water should be contained within the concrete washout CCM.
2. Runoff from water used for dust control – Not anticipated. The contractor should limit the amount of water used for dust control to an amount less than would result in runoff. Perimeter control CCMs are planned to filter water that may runoff.

If any other non-stormwater discharges from the site become apparent during the term of construction, the occurrence and mitigation shall be addressed by the GEC Administrator.

#### **H. Receiving Waters**

The Rock Island Trail, Constitution Avenue to Waynoka Tl discharges directly to Sand Creek by overland flow in both the existing condition and proposed condition. The project spans Sand Creek and the 100 year flood plain with a 210 foot pedestrian bridge.

Immediate Receiving water(s): Sand Creek

Ultimate Receiving Water(s): Fountain Creek

The site is located within FEMA flood zone X based on FEMA maps 08041C0752G effective December 7, 2018. The site is within the 100-year flood plain.

### **III. SWMP / CSWMP SITE MAP CONTENTS**

The SWMP / CSWMP Site Map and SWMP / CSWMP Drawings are considered a part of this plan. It identifies the following:

1. Construction site boundaries;
2. All areas of ground disturbance;
3. Existing and proposed topography;
4. Areas used for storage of building materials, equipment, soil, stockpiles or waste;
5. Locations of all structural CCMs;
6. Locations of non-structural CCMs where applicable;
7. Locations of springs, streams, wetlands, detention basins, roadside ditches and other surface waters.

The SWMP / CSWMP Site Map must be updated and or red-lined by the GEC Administrator on a regular basis to reflect current conditions of the site at all times. The SWMP / CSWMP site maps are contained at the rear of this report.

**IV. STORMWATER MANAGEMENT CONTROLS**

**A. GEC Administrator**

The Permittee shall designate the GEC Administrator. The GEC Administrator is typically the Contractor or his/her designated representative and is responsible for developing, implementing, maintaining and revising the SWMP / CSWMP. The GEC Administrator is the contact person with the City and State for all matter pertaining to the SWMP / CSWMP. The GEC Administrator is the person responsible for the SWMP / CSWMP accuracy, completeness and implementation. Therefore, the GEC Administrator should be a person with authority to adequately manage and direct day to day stormwater quality management activities at the site. The GEC Administrator shall have the authority to act on behalf of the Permittee(s) to ensure the site remains in compliance with the CDPS Stormwater Discharge Associated with Construction Activities Permit and the City’s Grading Permit. An Alternate GEC Administrator who is able to serve in the same capacity as the GEC Administrator shall also be selected.

The GEC Administrator shall be present at the project site a majority of the time and (along with the Alternate GEC Administrator) shall provide the City with a 24-hour emergency contact number.

If the GEC Administrator or Alternate changes for any reason, it shall be noted/redlined on this Plan. The City shall be notified in writing of any change.

GEC Administrator: Emily Duncan

Phone: (719) 385-6951

Alternate GEC Administrator: \_\_\_\_\_

Phone: \_\_\_\_\_

**B. Identification of Potential Pollutant Sources:**

At a minimum, the following sources and activities shall be evaluated for the potential to contribute pollutants to stormwater discharges and identified in the SWMP / CSWMP if found to have such potential. The sources of any potential pollutants must be controlled through CCM selection and implementation. Each pollutant source recognized through this process as having the potential to contribute pollutants to stormwater, must be identified in the SWMP / CSWMP along with the specific stormwater management control (CCMs) that will be implemented to adequately control the source. (Note: the actual evaluation of the potential pollutant sources does NOT need to be included in the SWMP / CSWMP – just the resultant pollutant sources and their associated CCMs.). The GEC Administrator shall determine the need for and locations of each of the following potential pollutant sources during the course of the construction project.

| Could it Contribute? | Potential Pollutant Source     | CCM Implemented to Control Source                             |
|----------------------|--------------------------------|---|
| Yes                  | All disturbed and stored soils | Silt fence, sediment control logs, rock socks, seed and mulch |
| Yes                  | Vehicle tracking of sediments  | Vehicle tracking control, street sweeping                     |

|              |  |   |
|--------------|--|---|
| No           | Management of contaminated soils   |   |
| Yes          | Loading and unloading operations   | Stabilized staging area, materials storage area, vehicle tracking control, silt fence |
| Yes          | Outdoor storage activities (building materials, fertilizers, chemicals, etc.)                              | Stabilized staging area, materials storage area, silt fence                           |
| Yes          | Vehicle and equipment maintenance and fueling  | Stabilized staging area, materials storage area, silt fence                           |
| Not expected | Significant dust or particulate generating processes   | Control by sprinkling with water and other appropriate means.                         |
| Yes          | Routine maintenance activities involving fertilizers, pesticides, detergents, fuels, solvents, oils, etc   | Use as recommended by manufacturer and in areas specified, silt fence                 |
| Yes          | On-site waste management practices (waste piles, liquid wastes, dumpsters, etc)                            | Stabilized staging area, silt fence, non-structural CCMs                              |
| Yes          | Concrete truck/equipment washing, including the concrete truck chute and associated fixtures and equipment | Concrete washout area, stabilized staging area, vehicle tracking control, silt fence  |
| No           | Dedicated asphalt and concrete batch plants  |   |
| Yes          | Non-industrial waste sources such as worker trash and portable toilets                                     | Stabilized staging area, construction fence, non-structural CCMs                      |
| Yes          | Other areas or procedures where potential spills can occur   | Non-structural CCMs, construction fence   |

### C. Construction Control Measures (CCMs) for Pollution Prevention

1. A list of the Structural CCMs for erosion and sediment control implemented on the site to minimize erosion and sediment are as follows. Refer to the GEC Plan for Installation and Maintenance requirements for each structural CCM and refer to the GEC Plan for the location of the CCMs.
  - a) Concrete Washout Area (CWA): An approved portable concrete washout system, or a shallow excavation with a small perimeter berm to isolate concrete truck washout operations.
  - b) Inlet protection (IP): Installed at appropriate inlets.
  - c) Erosion Control Blanket (ECB): At selected areas steeper than 3-to-1 as indicated on the plans shall be protected with an erosion control blanket.
  - d) Seeding and Mulching (SM): Temporary seeding and mulching can be used to stabilize disturbed areas that will be inactive for an extended period of time. Permanent seeding should be used to stabilize areas at final grade that will not otherwise be stabilized.
  - e) Silt Fence (SF): A temporary sediment barrier constructed of woven fabric stretched across supporting posts.
  - f) Stabilized Staging Area (SSA): Consists of stripping topsoil and spreading a layer of granular material in the area to be used for a trailer, parking, storage, unloading and loading.
  - g) Temporary Stockpile Areas (SP): Temporary stockpiles of excess excavated material and stockpiles for imported materials shall be shown

on the SWMP / CSWMP drawings. Slopes shall not be steeper than 3H to 1V. Temporary soil stockpile areas will require approved erosion protection such as silt fence or sediment control logs.

- h) Vehicle Tracking Control (VTC): Consists of a rock pad that is intended to help strip mud from tires prior to vehicles leaving the construction site. Installed at all entrance/exit points to the site. The number of access points shall be minimized.

Minimal clearing and grubbing may be necessary prior to installing the initial erosion control features.

- 2. Non-structural practices for erosion and sediment control to be used to minimize erosion and sediment transport are:

Seeding and mulching in areas that will not be hard surfaced. Minimize the amount of existing vegetation to be removed during construction, leaving native vegetation in place when possible. Only the existing vegetation that is specified or requiring removal shall be disturbed or removed. If possible, leave existing ground cover in place or remove just prior to grading to minimize the length of soil exposure.

- 3. Phased CCM Implementation:

The GEC Administrator shall update the CCM Implementation if necessary to meet and/or address the Contractor's schedule. The SWMP / CSWMP shall be updated as necessary to reflect the CCMs installed.

- a) Installation of Initial CCMs.

Prior to any construction activities, erosion control facilities shall be installed. Minimal clearing and grubbing may be necessary prior to installing the initial erosion control features. Stabilization of cleared or grubbed areas to be completed the same day if possible. The "initial" CCMs include, but may not be limited to, construction fence, silt fence, vehicle tracking control, stabilized staging area, materials storage area, concrete washout area, and inlet protection. Designate areas for construction trailer (if used), trash container, portolets, vehicle and equipment parking and material storage. If these areas are not indicated on the plan, the contractor must "red line" the plan with the locations. Provide a confined area for maintenance and fueling of equipment from which runoff will be contained and filtered. CCM / Erosion Control facility waste shall be disposed of properly.

- b) Clearing, grubbing and earthworks

The measures included in the previous sequence shall be maintained and continue. The removed cleared and grubbed items, soil, storm sewer pipe and fence shall be disposed of properly. If a soil stockpile area is needed, the area shall be protected as shown in the Details and the stockpile area shall be redlined onto the plan. Existing vegetation to remain shall be protected with construction fence. Wind erosion shall be controlled on the site by sprinkling and other appropriate means.

- c) Site Grading, Retaining Walls, Utility Infrastructure, and Stormwater Facility Construction

The measures included in the previous sequence shall be maintained and continue. This phase includes overall site work. Other than dewatering for surface runoff, it is not expected that a subsurface dewatering system will be required to complete the work shown on the plans. A CDPHE construction dewatering permit is required prior to performing the dewatering activities. Materials site and building construction shall be stored in the designated areas delineated on the plan. If an area is not delineated on the plan, the contractor shall "red line" the plan to show the location. Material waste from the detention basin construction shall be disposed of properly. Solvents, paints and chemicals shall be stored and disposed properly.

d) Building construction.

The measures included in the previous sequence shall be maintained and continue, unless the work requiring the measure is completed.

e) Seeding and mulching.

The measures included in the previous sequence shall be maintained and continue, unless the work requiring the measure is completed. Seeding, mulching and blanketing shall be installed. Avoid excess watering and placing of fertilizers and chemicals.

f) Final Stabilization.

The necessary erosion control measures included in the previous sequence shall continue until Final Stabilization is reached. Refer to Final Stabilization section for requirements.

The GEC Administrator shall amend the SWMP / CSWMP if necessary and as required, refer to Section I.

4. Materials handling and spill prevention:

The GEC Administrator will inspect daily to ensure proper use and disposal of materials on-site including solvents, fertilizers, chemicals, waste materials and equipment maintenance or fueling procedures. All materials stored on-site will be stored in a neat and orderly manner in the original containers with the original manufacturer's label, and if possible under a roof or other enclosure to prevent contact with stormwater. Chemicals should be stored within berms or other secondary containment devices to prevent leaks and spills from contacting stormwater runoff. Before disposing of the container, all of a product will be used up whenever possible and manufacturer's recommendations for proper disposal will be followed according to state and local regulations.

Material and equipment necessary for spill cleanup will be kept in the material storage area on-site. Manufacturer's recommendations for spill cleanup will be posted and site personnel will be made aware of the procedures along with the location of the information and cleanup supplies.

The contractor shall have spill prevention and response procedures that include the following:

- a) Notification procedures to be used in the event of an accident. At the very least, the GEC Administrator should be notified. Depending on the nature of the spill and the material involved, the Colorado Department of Public

Health and Environment (24-hour spill reporting line – 877-518-5608), downstream water users or other agencies may also need to be notified.

- b) Instructions for clean-up procedures and identification of spill kit location(s).
- c) Provisions for absorbents to be made available for use in fuel areas and for containers to be available for used absorbents.
- d) Procedures for properly washing out concrete truck chutes and other equipment in a manner and location so that the materials and wash water cannot discharge from the site and never into a storm drain system or stream.

5. Dedicated concrete or asphalt batch plants:

No dedicated concrete or asphalt batch plants will be used.

6. Vehicle tracking control:

Off-site vehicle tracking of sediment shall be minimized and is as shown on the SWMP / CSWMP Site Map. Vehicle Tracking Control shall be installed at the construction access points. The contractor shall minimize the number of construction access points to reduce the amount of sediment tracked from the site. Streets shall be kept clean and free of mud, soil and construction waste. Street sweeping or other acceptable methods shall be used to prevent sediment from being washed from the project site. Streets shall not be washed down with water. Street cleaning operations shall occur if necessary or as directed by the City.

7. Waste management and disposal including concrete washout:

A concrete washout area is specified on the SWMP / CSWMP. Concrete wash water shall not be discharged to state waters, to storm sewer systems or from the site as surface runoff. The washout area shall be an approved portable concrete washout system or a shallow excavation with a small perimeter berm to isolate concrete truck washout operations. At the end of construction, all concrete shall be removed from the site and disposed of at an approved waste site. Signs shall be placed at the washout to clearly indicate the concrete washout area to operators of concrete trucks and pump rigs. Refer to the standard detail for requirements.

All construction site waste both liquid and solid must be contained in approved waste containers and disposed of off-site according to state and local regulations. Portable sanitary facilities shall be provided at the site throughout the construction phase and must comply with state and local sanitary or septic system.

Waste disposal bins will be inspected daily for leaks and capacity. The bins will be placed on a surface that would indicate if there were a leak in the bin and prevent the leak from infiltrating the ground. If a leak is identified the bin will be repaired or replaced within 24 hours. No leakage will be allowed into the ground. Bins will be inspected for capacity by marking the bins with a level line at 80% of the internal height at the lowest rim. When any debris exceeds the 80% line, The bin will be closed or covered and no more debris will be inserted and the bin will be emptied with in 48 hours. No debris will be allowed to extend past the rim of the container.

Portable toilets will be located a minimum of 10ft from stormwater inlets and 50ft from state waters. They will be secured at all four corners to prevent overturning and cleaned on a weekly basis. They will be inspected daily for spills.



8. Groundwater and stormwater dewatering:

Groundwater dewatering is not anticipated on the site work or building construction. Locations and practices to be implemented to control stormwater pollution from excavations, etc. must be noted on the SWMP / CSWMP. A separate CDPHE construction discharge (dewatering) permit will be required for groundwater dewatering and shall be obtained by the GEC Administrator. Construction dewatering water cannot be discharged to surface water or to storm sewer systems without separate permit coverage. The discharge of Construction Dewatering water to the ground, under specific conditions, may be allowed by the Stormwater Construction Permit when appropriate CCMs are implemented. Refer to USDCM Volume III (UDFCD) for City acceptable means of dewatering.

9. Control Measures Owner and Operator.

This project relies on control measures owned or operated by the contractor.

## V. FINAL STABILIZATION AND LONG-TERM STORMWATER MANAGEMENT

“Final stabilization is reached when all ground surface disturbing activities at the site have been completed and uniform vegetative cover has been established with an individual plant density of at least 70 percent of pre-disturbance levels, or equivalent permanent, physical erosion reduction methods have been employed.” When vegetation is used to achieve final stabilization, the 70% vegetation requirement applies to a uniform plant density, which means that all areas of the site that rely on a vegetative cover to achieve stabilization must be uniformly vegetated. Noxious weeds are not to be counted toward the 70% requirement. The contractor will be responsible for providing the documentation to make this comparison to the City and the State of Colorado, Water Quality Control Division. The stormwater permit allows the permittee to use alternatives to vegetation to achieve final stabilization. All alternatives to vegetation must meet specific criteria to be considered equivalent to vegetation, specifically: stabilization must be permanent, all disturbed areas must be stabilized, and alternatives must follow good practices as described in the CDPHE Memo, dated March 5, 2013 (see References).

Temporary seeding for the project site shall include seeding and mulching. For the application methods, soil preparation and seeding and mulching requirements, refer to SWMP / CSWMP Drawings. All slopes of three-to-one (3:1) or steeper must be covered with an erosion control blanket.

Management of storm water after completion of construction will be accomplished by utilizing the practices listed below.

- Upon completion of construction, the site shall be inspected to ensure that all equipment, waste materials and debris have been removed.
- The site will be inspected to make certain that all graded surfaces have been landscaped or seeded with an appropriate ground cover.
- All silt fence, rock socks, etc. and all other control practices and measures that are to remain after completion of construction will be inspected to ensure their proper functioning.
- The contractor shall remove erosion control measures that are not required to remain.

After all construction activities are completed on the site, but final stabilization has not been achieved, the contractor shall make a thorough inspection of the stormwater management system at least once every month.

The contractor shall be responsible for maintaining the CCMs and stormwater controls in good working order and shall also be responsible for the costs incurred until final stabilization is reached. Once final stabilization has been achieved the contractor shall be responsible for removal of the erosion control measures.

Should any of the erosion control facilities (CCMs) become in disrepair prior to the establishment of the native or natural erosion control measures, the Contractor is responsible for the cost of such maintenance. The Contractor is also responsible for the clean-up of offsite areas affected by any sediment that may leave the site. Control of erosion from areas disturbed by project construction will be the responsibility of the respective contractor. All erosion control measures shown on the plan shall be installed and maintained in accordance with Construction Control Measures.

Inactivation of permit coverage: Coverage under the Stormwater Construction Permit may be inactivated by the permittee when the site has attained final stabilization, all temporary erosion and sediment control measures have been removed, and all components of the SWMP / CSWMP are complete.

## **VI. RECOMMENDED INSPECTION AND MAINTENANCE PROCEDURES**

### **A. Minimum Inspection Schedule**

1. Frequency. Contractor should inspect and document Construction CCM's at the following times and intervals.
  - a) After installation of any Construction CCM;
  - b) At least once every 14 days, but a more frequent inspection schedule may be necessary to ensure that CCMs continue to operate as needed to comply with the permit.
  - c) Within 24 hours after a precipitation or snowmelt event that produces runoff or causes surface erosion.
2. Consult State Permit No. COR-030000 for alternate inspection requirements at temporarily idle sites, at completed sites, or for winter conditions.
3. Refer to the Standard Details for the maintenance procedures associated with each CCM.
4. Inspection Procedures. The inspection must include observation of:
  - a) The construction site perimeter and discharge points (including discharges into a storm sewer system);
  - b) All disturbed areas;
  - c) Areas used for material/waste storage that are exposed to precipitation
  - d) Other areas determined to have a significant potential for stormwater pollution, such as concrete washout locations, or locations where vehicles enter or leave the site;
  - e) Erosion and sediment control measures identified in the SWMP / CSWMP; and any other structural CCMs that may require maintenance, such as secondary containment around fuel tanks, or the condition of spill response kits.

The inspection must determine if there is evidence of, or the potential for, pollutants entering the drainage system. CCMs should be reviewed to determine if they still meet the design and operational criteria in the SWMP / CSWMP, and if they continue to adequately control pollutants at the site. Any CCMs not operating in accordance with the SWMP / CSWMP

must be addressed as soon as possible, immediately in most cases, to minimize the discharge of pollutants, and the SWMP / CSWMP must be updated as described.

5. Record Keeping and Documenting Inspections: Keeping accurate and complete records serves several functions. First, keeping records of spills, leaks, inspections, etc. is a requirement of the State Stormwater Construction Permit; therefore, enforcement action, including fines, could result if records are not adequate. Second, by keeping accurate and detailed records, you will have documentation of events which could prove invaluable should complications arise concerning the permit, lawsuits, etc.
6. Inspection Checklist/Report. The Permittee must document inspection results and maintain a record of the results for a period of 3 years following expiration or inactivation of permit coverage. These records must be made available to CDPHE, the City or EPA upon request. The GEC Administrator should record the inspection results on a site-specific standardized inspection report or City Inspection Checklist to be maintained and kept on the construction site. An example template for the inspection report format is included in Appendix. The GEC Administrator should develop a site-specific inspection report that itemizes the selected Construction CCMs for their site. At a minimum the following information from each inspection should be recorded on the site-specific report. This report should be located within 8 feet of the main entrance to job site trailer and within sight of the entrance. If within a cabinet or drawer, there needs to be a sign on the enclosure with a minimum of ½ inch tall letters indicating “SWMP /CSWMP Inspection Report Inside”:
  - a) Date of inspection,
  - b) Name and title of inspector,
  - c) Signature of inspector,
  - d) Location(s) of discharges of sediment or other pollutants from the site,
  - e) Location(s) of CCMs that need to be maintained,
  - f) Location(s) of CCMs that failed to operate as designed or proved inadequate for a particular location,
  - g) Location(s) where additional CCMs are needed that were not in place at the time of inspection,
  - h) Deviations from the minimum inspection schedule as provided in the permit,
  - i) Descriptions of corrective actions for any item above, date(s) of corrective actions taken, and measures taken to prevent future violations, including requisite changes to the SWMP / CSWMP, as necessary and
  - j) After adequate corrective action(s) has been taken, or where a report does not identify any incidents requiring corrective actions, the report shall contain a signed statement indicating the site is in compliance with the permit to the best of the signer’s knowledge and belief.
7. Inspection Checklists/Reports to City: Completed Inspection Checklists will be submitted electronically to the assigned City Engineering inspector within 5 business days of the inspection. The inspections checklists must also be kept on-site.

8. GEC Administrator to perform self-inspections at a minimum once every 14 calendar days, and within 24 hours of storm events or snowmelt event that causes surface erosion. The GEC Administrator must complete and submit self-inspection form within 5 business days of the self-inspections.

#### **B. CCM Operation and Maintenance.**

The GEC Administrator is responsible for operation and maintenance of construction CCMs. The GEC Administrator will inspect the site per inspection and monitoring protocol outlined above and will make any necessary repairs to construction CCMs immediately after a defect or other need for repair is discovered. The project site and the adjacent streets impacted by the construction shall be kept neat, clean and free of debris. The erosion control measures and facilities will be maintained in good working order until final stabilization. Any items that are not functioning properly or are inadequate will be promptly repaired or upgraded. Records of inspections must be kept and be available for review by the State of Colorado Water Quality Control Division or the City.

### **VII. REFERENCES**

- 1) CDPS General Permit: Stormwater Discharges Associated with Construction Activity Permit No. COR-030000, Colorado Department of Public Health and Environment, dated July 1, 2007. Administratively continued effective July 1, 2012.
- 2) CDPHE, Stormwater Discharges Associated with Construction Activity, Stormwater Management Plan Preparation Guidance, prepared by CDPHE, dated April 2011.
- 3) CDPHE Memorandum, Final Stabilization requirements for stormwater construction permit termination, Alternatives to the 70% plant density re-vegetation requirement, prepared by CDPHE, dated March 5, 2013.
- 4) Volume 1 and 2, City of Colorado Springs, Drainage Criteria Manual, by City of Colorado Springs, current edition.
- 5) Volume 3, Urban Storm Drainage Criteria Manual, by Urban Drainage and Flood Control District, current edition.
- 6) El Paso County Area Soil Survey, prepared by the Natural Resources Conservation Service.
- 7) City of Colorado Springs and El Paso County Flood Insurance Study, prepared by the Federal Emergency Management Agency, dated March 1997.

## **APPENDIX TABLE OF CONTENTS**

### **APPENDIX A**

Vicinity Map

Soil Survey Map

Flood Insurance Rate Map

### **APPENDIX B**

Example – Exhibit A: Erosion and Sediment Control Field Inspection Report

Example – Exhibit B: Corrective Action Report

### **APPENDIX C**

Stormwater Certificate

### **APPENDIX D**

CCM Details

### **APPENDIX E**

SWMP Plan (GEC Plan)

**APPENDIX A**  
**Vicinity Map**  
**Soil Survey Map**  
**Flood Insurance Rate Map**

**NOTES TO USERS**

This map is for use in administering the National Flood Insurance Program. It does not necessarily identify all areas subject to flooding, particularly from local drainage sources of small size. The community map repository should be consulted for possible updated or additional flood hazard information.

To obtain more detailed information in areas where **Base Flood Elevations (BFEs)** and/or **floodways** have been determined, users are encouraged to consult the Flood Profiles and Floodway Data and/or Summary of Stillwater Elevations tables contained within the Flood Insurance Study (FIS) report that accompanies this FIRM. Users should be aware that BFEs shown on the FIRM represent rounded whole-foot elevations. These BFEs are intended for flood insurance rating purposes only and should not be used as the sole source of flood elevation information. Accordingly, flood elevation data presented in the FIS report should be utilized in conjunction with the FIRM for purposes of construction and/or floodplain management.

**Coastal Base Flood Elevations** shown on this map apply only landward of 0.0' North American Vertical Datum of 1988 (NAVD88). Users of this FIRM should be aware that coastal flood elevations are also provided in the Summary of Stillwater Elevations table in the Flood Insurance Study report for this jurisdiction. Elevations shown in the Summary of Stillwater Elevations table should be used for construction and/or floodplain management purposes when they are higher than the elevations shown on this FIRM.

Boundaries of the **floodways** were computed at cross sections and interpolated between cross sections. The floodways were based on hydraulic considerations with regard to requirements of the National Flood Insurance Program. Floodway widths and other pertinent floodway data are provided in the Flood Insurance Study report for this jurisdiction.

Certain areas not in Special Flood Hazard Areas may be protected by **flood control structures**. Refer to section 2.4 "Flood Protection Measures" of the Flood Insurance Study report for information on flood control structures for this jurisdiction.

The **projection** used in the preparation of this map was Universal Transverse Mercator (UTM) zone 13. The **horizontal datum** was NAD83, GRS80 spheroid. Differences in datum, spheroid, projection or UTM zones zones used in the production of FIRMs for adjacent jurisdictions may result in slight positional differences in map features across jurisdiction boundaries. These differences do not affect the accuracy of this FIRM.

Flood elevations on this map are referenced to the **North American Vertical Datum of 1988 (NAVD88)**. These flood elevations must be compared to structure and ground elevations referenced to the same **vertical datum**. For information regarding conversion between the National Geodetic Vertical Datum of 1929 and the North American Vertical Datum of 1988, visit the National Geodetic Survey website at <http://www.ngs.noaa.gov/> or contact the National Geodetic Survey at the following address:

NGS Information Services  
NOAA, NIMS12  
National Geodetic Survey  
SSMC-3, #9202  
1315 East-West Highway  
Silver Spring, MD 20910-3282

To obtain current elevation, description, and/or location information for **bench marks** shown on this map, please contact the Information Services Branch of the National Geodetic Survey at (301) 713-3242 or visit its website at <http://www.ngs.noaa.gov/>.

**Base Map** information shown on this FIRM was provided in digital format by El Paso County, Colorado Springs Utilities, City of Fountain, Bureau of Land Management, National Oceanic and Atmospheric Administration, United States Geological Survey, and Anderson Consulting Engineers, Inc. These data are current as of 2006.

This map reflects more detailed and up-to-date **stream channel configurations** and **floodplain delineations** than those shown on the previous FIRM for this jurisdiction. The floodplains and floodways that were transferred from the previous FIRM may have been adjusted to conform to these new stream channel configurations. As a result, the Flood Profiles and Floodway Data tables in the Flood Insurance Study Report (which contains authoritative hydraulic data) may reflect stream channel distances that differ from what is shown on this map. The profile baselines depicted on this map represent the hydraulic modeling baselines that match the flood profiles and Floodway Data Tables if applicable, in the FIS report. As a result, the profile baselines may deviate significantly from the new base map channel representation and may appear outside of the floodplain.

**Corporate limits** shown on this map are based on the best data available at the time of publication. Because changes due to annexations or de-annexations may have occurred after this map was published, map users should contact appropriate community officials to verify current corporate limit locations.


Please refer to the separately printed **Map Index** for an overview map of the county showing the layout of map panels; community map repository addresses; and a Listing of Communities table containing National Flood Insurance Program dates for each community as well as a listing of the panels on which each community is located.

Contact **FEMA Map Service Center (MSC)** via the FEMA Map Information eXchange (FMIX) 1-877-336-2627 for information on available products associated with this FIRM. Available products may include previously issued Letters of Map Change, a Flood Insurance Study Report, and/or digital versions of this map. The MSC may also be reached by Fax at 1-800-358-9620 and its website at <http://www.msc.fema.gov/>.

If you have **questions about this map** or questions concerning the National Flood Insurance Program in general, please call 1-877-FEMA MAP (1-877-336-2627) or visit the FEMA website at <http://www.fema.gov/business/nfp>.

| El Paso County Vertical Datum Offset Table  |                            |
|---|----------------------------|
| Flooding Source   | Vertical Datum Offset (ft) |
| REFER TO SECTION 3.3 OF THE EL PASO COUNTY FLOOD INSURANCE STUDY FOR STREAM BY STREAM VERTICAL DATUM CONVERSION INFORMATION |                            |


**Panel Location Map**

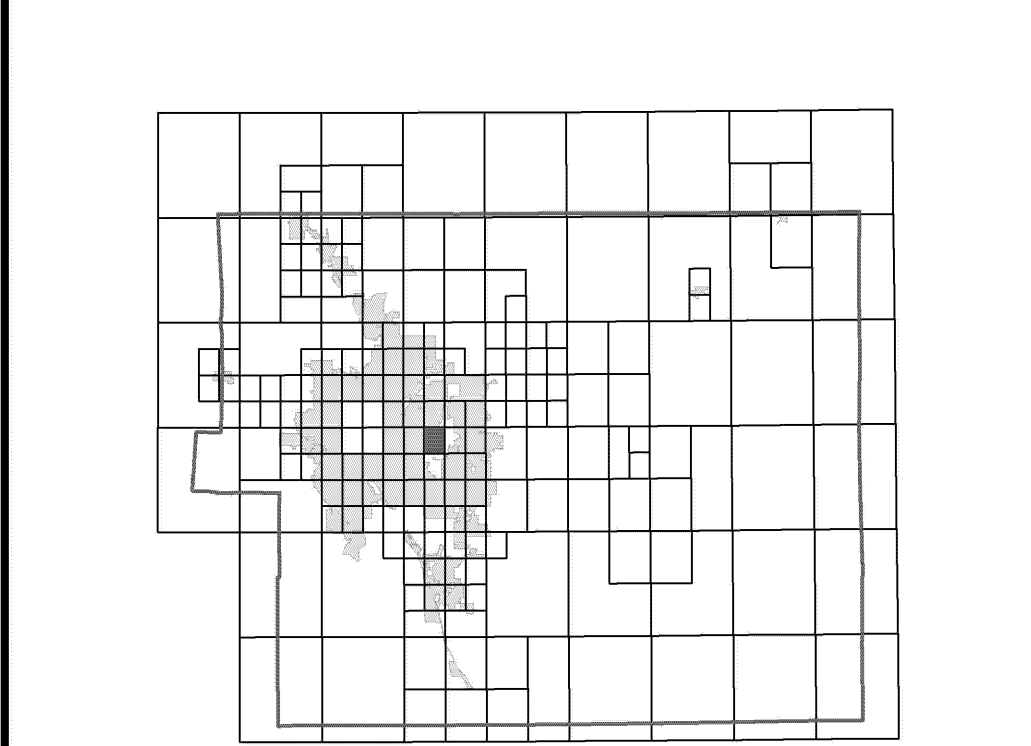

This Digital Flood Insurance Rate Map (DFIRM) was produced through a Cooperating Technical Partner (CTP) agreement between the State of Colorado Water Conservation Board (CWCB) and the Federal Emergency Management Agency (FEMA).



Additional Flood Hazard information and resources are available from local communities and the Colorado Water Conservation Board.

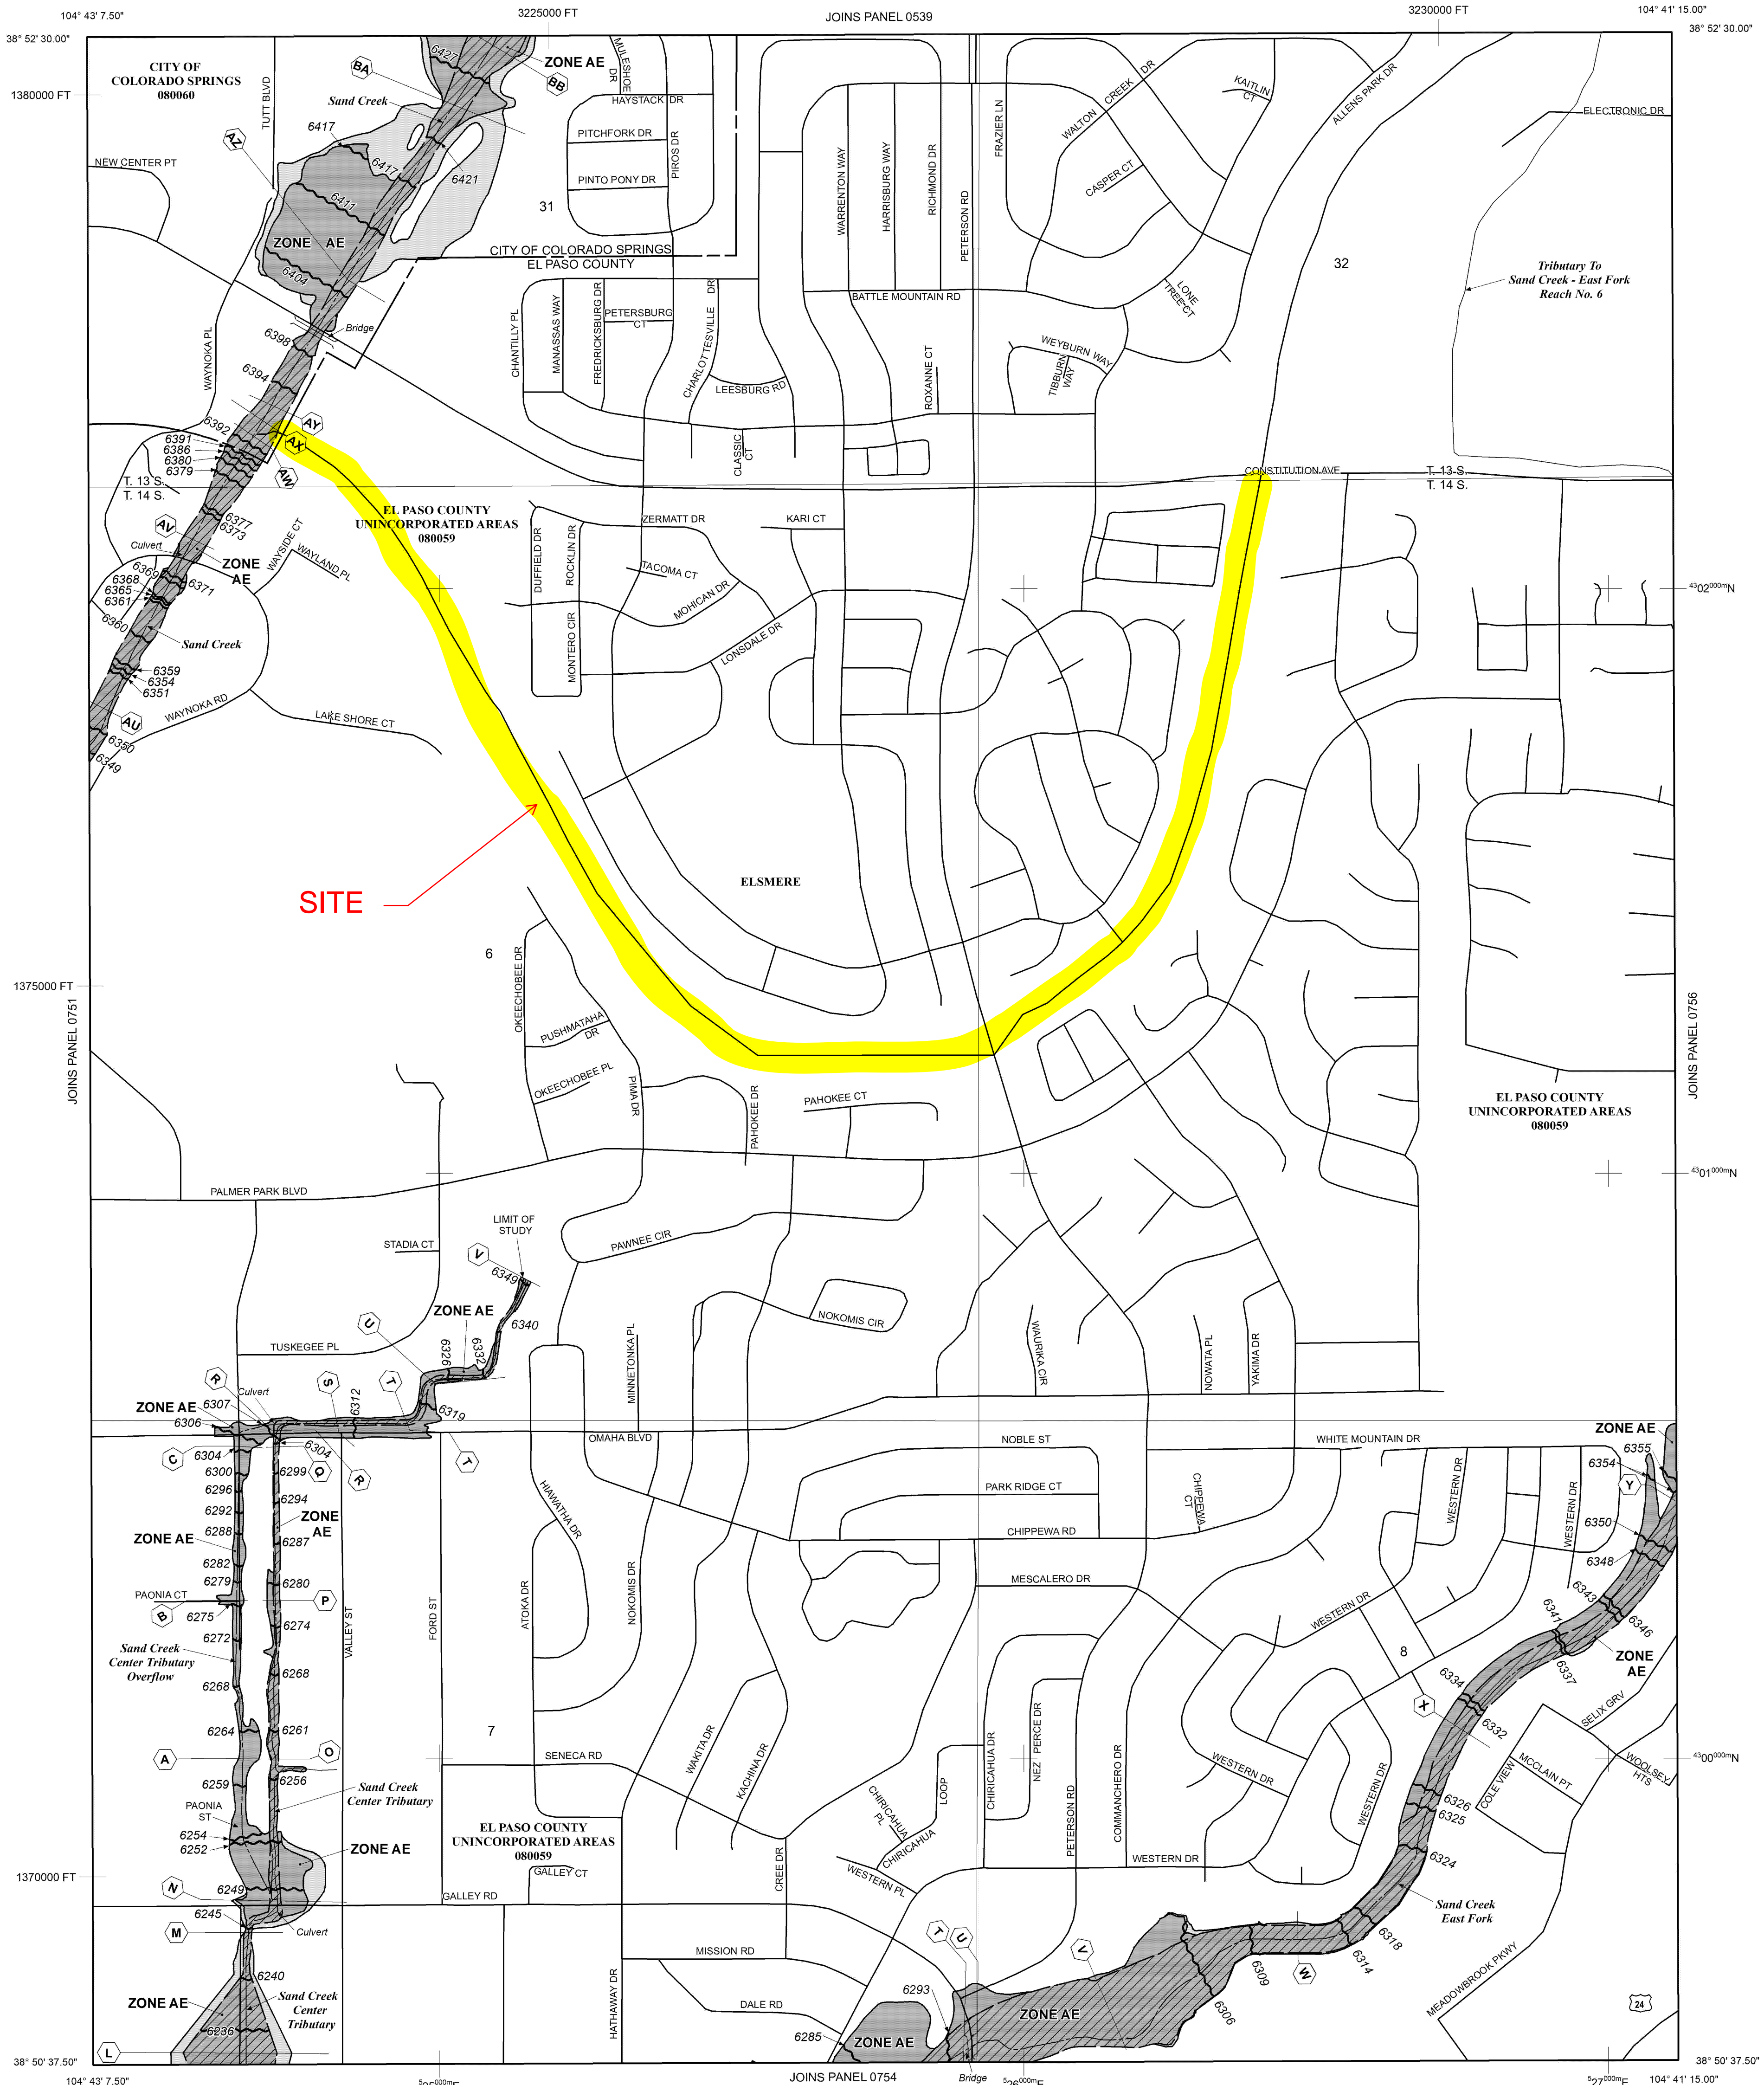

NOTE: MAP AREA SHOWN ON THIS PANEL IS LOCATED WITHIN TOWNSHIP 13 SOUTH, RANGE 65 WEST, AND TOWNSHIP 14 SOUTH, RANGE 65 WEST.

**LEGEND**

**SPECIAL FLOOD HAZARD AREAS (SFHAS) SUBJECT TO INUNDATION BY THE 1% ANNUAL CHANCE FLOOD**

The 1% annual chance flood (100-year flood), also known as the base flood, is the flood that has a 1% chance of being equalled or exceeded in any given year. The Special Flood Hazard Area is the area subject to flooding by the 1% annual chance flood. Areas of Special Flood Hazard include Zones A, AE, AH, AO, AR, AV, and VE. The Base Flood Elevation is the water-surface elevation of the 1% annual chance flood.

- ZONE A** No Base Flood Elevations determined.
- ZONE AE** Base Flood Elevations determined.
- ZONE AH** Flood depths of 1 to 3 feet (usually areas of ponding); Base Flood Elevations determined.
- ZONE AO** Flood depths of 1 to 3 feet (usually sheet flow on sloping terrain); average depths determined. For areas of alluvial fan flooding, velocities also determined.
- ZONE AR** Special Flood Hazard Area Formerly protected from the 1% annual chance flood by a flood control system that was subsequently decertified. Zone AR indicates that the former flood control system is being restored to provide protection from the 1% annual chance or greater flood.
- ZONE A99** Area to be protected from 1% annual chance flood by a Federal flood protection system under construction; no Base Flood Elevations determined.
- ZONE V** Coastal flood zone with velocity hazard (wave action); no Base Flood Elevations determined.
- ZONE VE** Coastal flood zone with velocity hazard (wave action); Base Flood Elevations determined.

**FLOODWAY AREAS IN ZONE AE**

The floodway is the channel of a stream plus any adjacent floodplain areas that must be kept free of encroachment so that the 1% annual chance flood can be carried without substantial increases in flood heights.

**OTHER FLOOD AREAS**

**ZONE X** Areas of 0.2% annual chance flood; areas of 1% annual chance flood with average depths of less than 1 foot, or with drainage areas less than 1 square mile; and areas protected by levees from 1% annual chance flood.

**OTHER AREAS**

**ZONE X** Areas determined to be outside the 0.2% annual chance floodplain.

**ZONE D** Areas in which flood hazards are undetermined, but possible.

**COASTAL BARRIER RESOURCES SYSTEM (CBRS) AREAS**

**OTHERWISE PROTECTED AREAS (OPAs)**

CBRS areas and OPAs are normally located within or adjacent to Special Flood Hazard Areas.

- Floodplain boundary
- Floodway boundary
- Zone D Boundary
- CBRS and OPA boundary
- Boundary dividing Special Flood Hazard Areas of different Base Flood Elevations, flood depths or flood velocities.
- Base Flood Elevation line and value; elevation in feet\* (EL 987)
- Base Flood Elevation value where uniform within zone; elevation in feet\*

\* Referenced to the North American Vertical Datum of 1988 (NAVD 88)

**A** Cross section line

**23** Transsect line

97° 07' 30.00" 32° 22' 30.00" Geographic coordinates referenced to the North American Datum of 1983 (NAD 83)

4250000N 1000-meter Universal Transverse Mercator grid ticks, zone 13

6000000 FT 5000-foot grid ticks; Colorado State Plane coordinate system, central zone (FIPSZONE 0502), Lambert Conformal Conic Projection

DX5510 Bench mark (see explanation in Notes to Users section of this FIRM panel)

M1.5 River Mile

MAP REPOSITORIES Refer to Map Repositories list on Map Index

EFFECTIVE DATE OF COUNTYWIDE FLOOD INSURANCE RATE MAP MARCH 17, 1997


EFFECTIVE DATE(S) OF REVISION(S) TO THIS PANEL

DECEMBER 7, 2018 to update corporate limits, to change Base Flood Elevations and Special Flood Hazard Areas, to update map format, to add roads and road names, and to incorporate previously issued Letters of Map Revision

For community map revision history prior to countywide mapping, refer to the Community Map History Table located in the Flood Insurance Study report for this jurisdiction.

To determine if flood insurance is available in this community, contact your insurance agent or call the National Flood Insurance Program at 1-800-638-6620.

MAP SCALE 1" = 500'

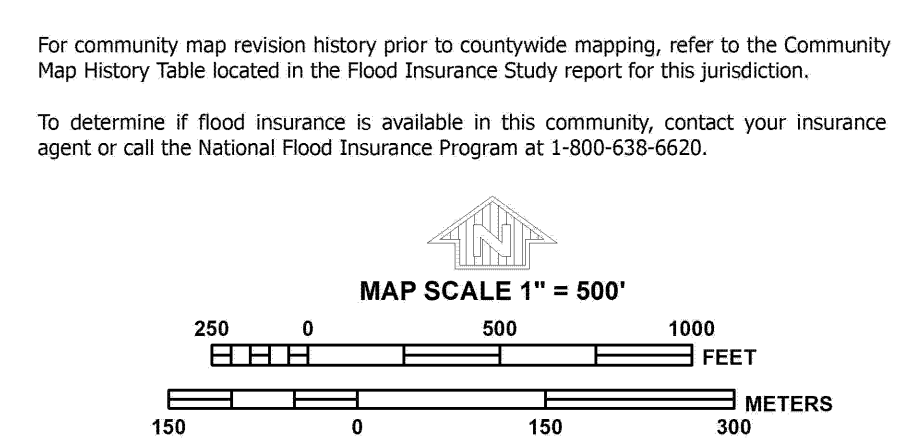

**NFIP**

**PANEL 0752G**

---

**FIRM**

**FLOOD INSURANCE RATE MAP**

**EL PASO COUNTY, COLORADO AND INCORPORATED AREAS**

**PANEL 752 OF 1300**

(SEE MAP INDEX FOR FIRM PANEL LAYOUT)

| CONTAINS: | COMMUNITY                 | NUMBER | PANEL | SUFFIX |
|-----------|---------------------------|--------|-------|--------|
|           | COLORADO SPRINGS, CITY OF | 08060  | 0752  | G      |
|           | EL PASO COUNTY            | 08059  | 0752  | G      |

Notice: This map was released on 06/15/2020 to make a correction. This version replaces any previous versions. See the Notice to User Letter that accompanied this correction for details.

Notice to User: The Map Number shown below should be used when placing map orders. The Community Number shown above should be used on insurance applications for the subject community.

**MAP NUMBER**  
**08041C0752G**

**MAP REVISED**  
**DECEMBER 7, 2018**

Federal Emergency Management Agency




United States  
Department of  
Agriculture

**NRCS**

Natural  
Resources  
Conservation  
Service

A product of the National  
Cooperative Soil Survey,  
a joint effort of the United  
States Department of  
Agriculture and other  
Federal agencies, State  
agencies including the  
Agricultural Experiment  
Stations, and local  
participants

# Custom Soil Resource Report for El Paso County Area, Colorado

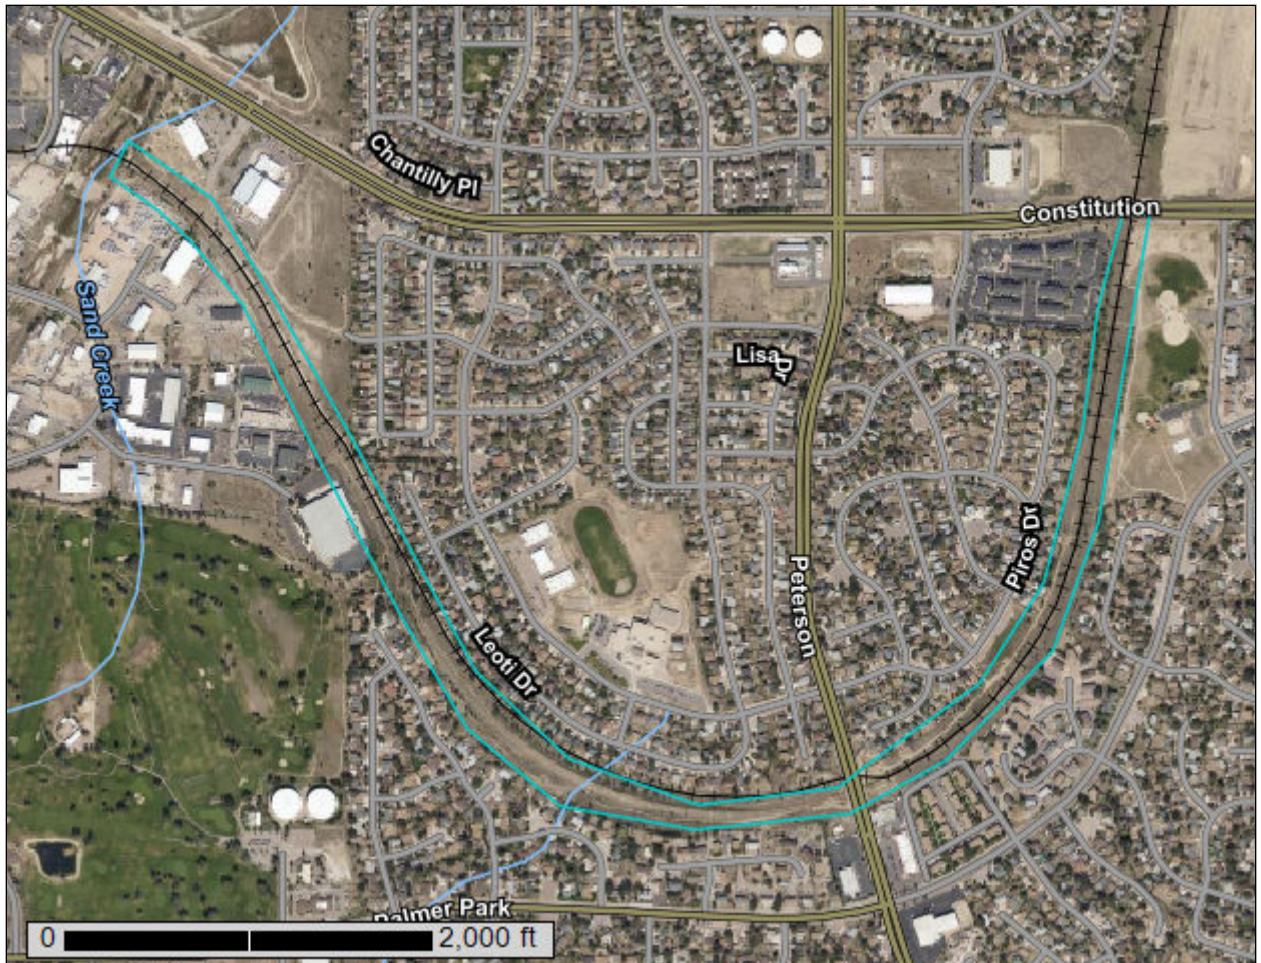




# Custom Soil Resource Report Soil Map




Map Scale: 1:9,580 if printed on A landscape (11" x 8.5") sheet.



Map projection: Web Mercator Corner coordinates: WGS84 Edge tics: UTM Zone 13N WGS84

### MAP LEGEND

**Area of Interest (AOI)**

 Area of Interest (AOI)


**Soils**


 Soil Map Unit Polygons


 Soil Map Unit Lines


 Soil Map Unit Points

**Special Point Features**

 Blowout

 Borrow Pit


 Clay Spot


 Closed Depression

 Gravel Pit

 Gravelly Spot


 Landfill

 Lava Flow

 Marsh or swamp

 Mine or Quarry

 Miscellaneous Water


 Perennial Water

 Rock Outcrop


 Saline Spot

 Sandy Spot

 Severely Eroded Spot


 Sinkhole


 Slide or Slip


 Sodic Spot


 Spoil Area

 Stony Spot


 Very Stony Spot

 Wet Spot

 Other

 Special Line Features

**Water Features**

 Streams and Canals


**Transportation**

 Rails


 Interstate Highways

 US Routes

 Major Roads

 Local Roads

**Background**

 Aerial Photography

### MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:24,000.

Warning: Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service  
 Web Soil Survey URL:  
 Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: El Paso County Area, Colorado  
 Survey Area Data: Version 21, Aug 24, 2023

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Aug 19, 2018—Sep 23, 2018

The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

## Map Unit Legend

| Map Unit Symbol                    | Map Unit Name                                     | Acres in AOI | Percent of AOI |
|------------------------------------|---|--------------|----------------|
| 8                                  | Blakeland loamy sand, 1 to 9 percent slopes       | 41.7         | 98.8%          |
| 28                                 | Ellicott loamy coarse sand, 0 to 5 percent slopes | 0.5          | 1.2%           |
| <b>Totals for Area of Interest</b> |   | <b>42.2</b>  | <b>100.0%</b>  |

## Map Unit Descriptions

The map units delineated on the detailed soil maps in a soil survey represent the soils or miscellaneous areas in the survey area. The map unit descriptions, along with the maps, can be used to determine the composition and properties of a unit.

A map unit delineation on a soil map represents an area dominated by one or more major kinds of soil or miscellaneous areas. A map unit is identified and named according to the taxonomic classification of the dominant soils. Within a taxonomic class there are precisely defined limits for the properties of the soils. On the landscape, however, the soils are natural phenomena, and they have the characteristic variability of all natural phenomena. Thus, the range of some observed properties may extend beyond the limits defined for a taxonomic class. Areas of soils of a single taxonomic class rarely, if ever, can be mapped without including areas of other taxonomic classes. Consequently, every map unit is made up of the soils or miscellaneous areas for which it is named and some minor components that belong to taxonomic classes other than those of the major soils.

Most minor soils have properties similar to those of the dominant soil or soils in the map unit, and thus they do not affect use and management. These are called noncontrasting, or similar, components. They may or may not be mentioned in a particular map unit description. Other minor components, however, have properties and behavioral characteristics divergent enough to affect use or to require different management. These are called contrasting, or dissimilar, components. They generally are in small areas and could not be mapped separately because of the scale used. Some small areas of strongly contrasting soils or miscellaneous areas are identified by a special symbol on the maps. If included in the database for a given area, the contrasting minor components are identified in the map unit descriptions along with some characteristics of each. A few areas of minor components may not have been observed, and consequently they are not mentioned in the descriptions, especially where the pattern was so complex that it was impractical to make enough observations to identify all the soils and miscellaneous areas on the landscape.

The presence of minor components in a map unit in no way diminishes the usefulness or accuracy of the data. The objective of mapping is not to delineate pure taxonomic classes but rather to separate the landscape into landforms or landform segments that have similar use and management requirements. The delineation of such segments on the map provides sufficient information for the development of resource plans. If intensive use of small areas is planned, however,

## El Paso County Area, Colorado

### 8—Blakeland loamy sand, 1 to 9 percent slopes

#### Map Unit Setting

*National map unit symbol:* 369v  
*Elevation:* 4,600 to 5,800 feet  
*Mean annual precipitation:* 14 to 16 inches  
*Mean annual air temperature:* 46 to 48 degrees F  
*Frost-free period:* 125 to 145 days  
*Farmland classification:* Not prime farmland

#### Map Unit Composition

*Blakeland and similar soils:* 98 percent  
*Minor components:* 2 percent  
*Estimates are based on observations, descriptions, and transects of the mapunit.*

#### Description of Blakeland

##### Setting

*Landform:* Hills, flats  
*Landform position (three-dimensional):* Side slope, talf  
*Down-slope shape:* Linear  
*Across-slope shape:* Linear  
*Parent material:* Alluvium derived from sedimentary rock and/or eolian deposits derived from sedimentary rock

##### Typical profile

*A - 0 to 11 inches:* loamy sand  
*AC - 11 to 27 inches:* loamy sand  
*C - 27 to 60 inches:* sand

##### Properties and qualities

*Slope:* 1 to 9 percent  
*Depth to restrictive feature:* More than 80 inches  
*Drainage class:* Somewhat excessively drained  
*Runoff class:* Low  
*Capacity of the most limiting layer to transmit water (Ksat):* High to very high (5.95 to 19.98 in/hr)  
*Depth to water table:* More than 80 inches  
*Frequency of flooding:* None  
*Frequency of ponding:* None  
*Calcium carbonate, maximum content:* 5 percent  
*Available water supply, 0 to 60 inches:* Low (about 4.5 inches)

##### Interpretive groups

*Land capability classification (irrigated):* 3e  
*Land capability classification (nonirrigated):* 6e  
***Hydrologic Soil Group:* A**  
*Ecological site:* R049XB210CO - Sandy Foothill  
*Hydric soil rating:* No

#### Minor Components

##### Other soils

*Percent of map unit:* 1 percent

## Custom Soil Resource Report

*Hydric soil rating:* No

### **Pleasant**

*Percent of map unit:* 1 percent

*Landform:* Depressions

*Hydric soil rating:* Yes

## **28—Ellicott loamy coarse sand, 0 to 5 percent slopes**

### **Map Unit Setting**

*National map unit symbol:* 3680

*Elevation:* 5,500 to 6,500 feet

*Mean annual precipitation:* 13 to 15 inches

*Mean annual air temperature:* 47 to 50 degrees F

*Frost-free period:* 125 to 145 days

*Farmland classification:* Not prime farmland

### **Map Unit Composition**

*Ellicott and similar soils:* 97 percent

*Minor components:* 3 percent

*Estimates are based on observations, descriptions, and transects of the mapunit.*

### **Description of Ellicott**

#### **Setting**

*Landform:* Flood plains, stream terraces

*Landform position (three-dimensional):* Tread

*Down-slope shape:* Linear

*Across-slope shape:* Linear

*Parent material:* Sandy alluvium

#### **Typical profile**

*A - 0 to 4 inches:* loamy coarse sand

*C - 4 to 60 inches:* stratified coarse sand to sandy loam

#### **Properties and qualities**

*Slope:* 0 to 5 percent

*Depth to restrictive feature:* More than 80 inches

*Drainage class:* Somewhat excessively drained

*Runoff class:* Very low

*Capacity of the most limiting layer to transmit water (Ksat):* High to very high (5.95 to 19.98 in/hr)

*Depth to water table:* More than 80 inches

*Frequency of flooding:* Frequent

*Frequency of ponding:* None

*Available water supply, 0 to 60 inches:* Low (about 4.1 inches)

#### **Interpretive groups**

*Land capability classification (irrigated):* None specified

*Land capability classification (nonirrigated):* 7w

**Hydrologic Soil Group: A**

## Custom Soil Resource Report

*Ecological site:* R069XY031CO - Sandy Bottomland

*Other vegetative classification:* SANDY BOTTOMLAND (069AY031CO)

*Hydric soil rating:* No

### **Minor Components**

#### **Fluvaquentic haplaquoll**

*Percent of map unit:* 1 percent

*Landform:* Swales

*Hydric soil rating:* Yes

#### **Other soils**

*Percent of map unit:* 1 percent



*Hydric soil rating:* No

#### **Pleasant**

*Percent of map unit:* 1 percent

*Landform:* Depressions

*Hydric soil rating:* Yes

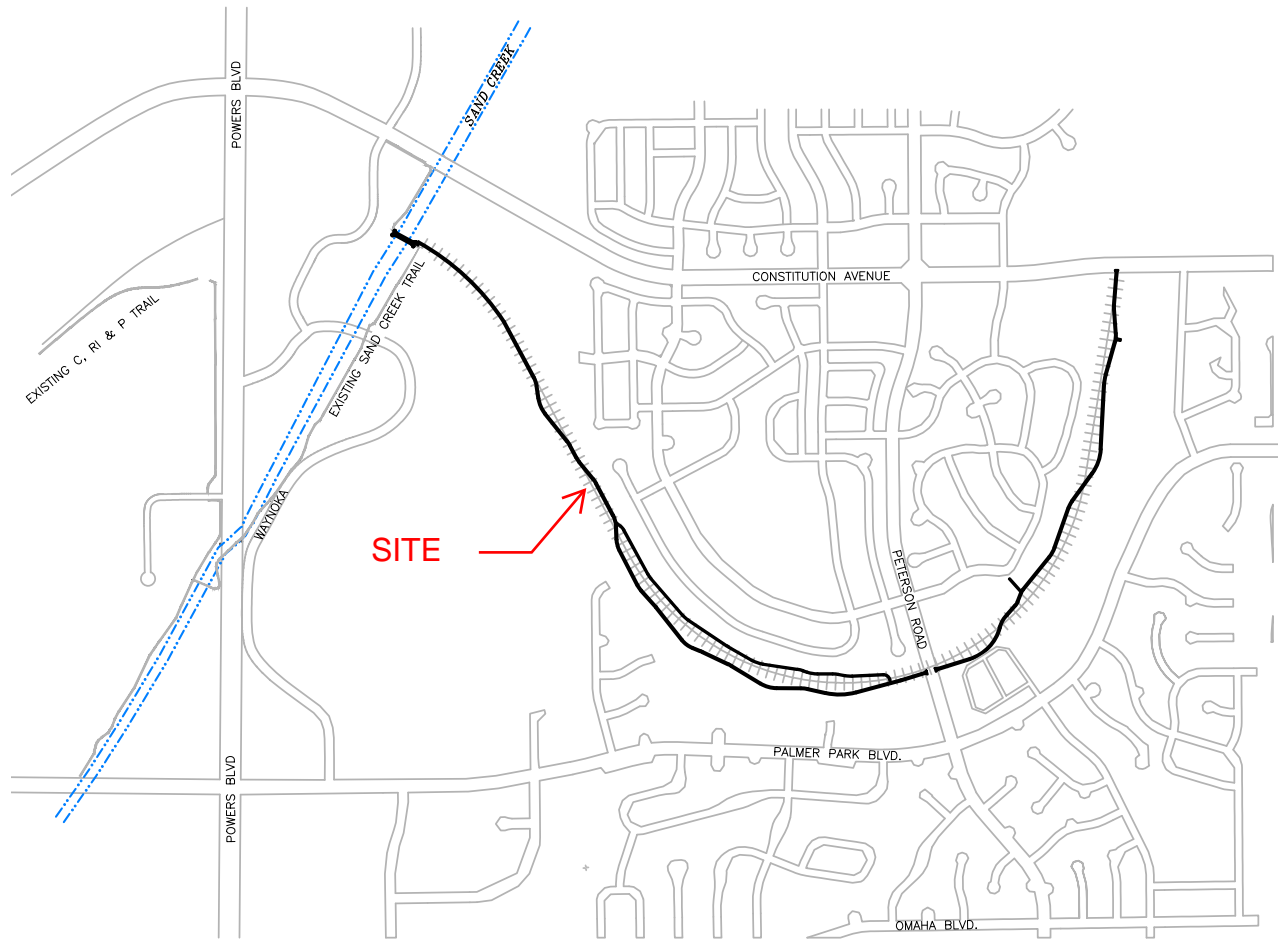

SCALE: 1"=1500'



**FIGURE 1**  
VICINITY MAP  
ROCK ISLAND MULTI-USE TRAIL

## **APPENDIX B**

**Example – Exhibit A: Erosion and Sediment Control Field Inspection Report**

**Example – Exhibit B: Corrective Action Report**



**Exhibit A  
Erosion and Sediment Control Field Inspection Report**

|                           |                     |
|---------------------------|---------------------|
| Project Name:             | Date of Inspection: |
| Project Address/Location: | Time of Inspection: |
| Contractor:               | Name of Inspector:  |

Reason for Inspection:

| BMP for Erosion Control           | Practice Used |    | Maintenance or Sediment Removal Required |    | Explain Required Action |
|-----------------------------------|---------------|----|--|----|-------------------------|
|                                   | Yes           | No | Yes                                      | No |                         |
| Check Dams                        |               |    |  |    |                         |
| Concrete Washout Area             |               |    |  |    |                         |
| Construction Fence                |               |    |  |    |                         |
| Diversion Ditch/Swales/Berms      |               |    |  |    |                         |
| Erosion Control Blankets          |               |    |  |    |                         |
| Inlet Protection                  |               |    |  |    |                         |
| Reinforced Rock Berms             |               |    |  |    |                         |
| Reinforced Rock Berms - Culvert   |               |    |  |    |                         |
| Sediment Basin                    |               |    |  |    |                         |
| Sediment Control Log              |               |    |  |    |                         |
| Seed & Mulch (Temp. or Permanent) |               |    |  |    |                         |
| Silt Fence                        |               |    |  |    |                         |
| Sodding                           |               |    |  |    |                         |
| Stabilized Staging Area           |               |    |  |    |                         |
| Straw Bale Barrier                |               |    |  |    |                         |
| Surface Roughening                |               |    |  |    |                         |
| Vehicle Tracking Control Pad      |               |    |  |    |                         |

Contractor's Comments:

Inspector's Comments:

I certify this Erosion and Sediment Control Field Inspection Report is complete and accurate, to my knowledge and belief.

|                               |              |
|-------------------------------|--------------|
| Inspector Signature and Date: | Reviewed By: |
|-------------------------------|--------------|

**Exhibit B**  
**Corrective Action Report**

Site: \_\_\_\_\_

Inspector: \_\_\_\_\_

Date: \_\_\_\_\_

.....  
Erosion Control Measure/Facility Requiring Attention:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

Recommended Corrective Action:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

Scheduled Completion Date: \_\_\_\_\_ Date Completed: \_\_\_\_\_

.....

Erosion Control Measure/Facility Requiring Attention:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

Recommended Corrective Action:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

Scheduled Completion Date: \_\_\_\_\_ Date Completed: \_\_\_\_\_

.....

Erosion Control Measure/Facility Requiring Attention:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

Recommended Corrective Action:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

Scheduled Completion Date: \_\_\_\_\_ Date Completed: \_\_\_\_\_

**APPENDIX C**  
**Stormwater Certificate**

# Altitude Training Associates

Awards this Certificate of Completion to

**Emily Duncan**

Who on **October 5, 2021** Successfully Completed  
The Following Training Class:

**Stormwater Management and Erosion Control During  
Construction - GEC Administrator**


Certificate Number: 123




Instructor  
Altitude Training Associates




**APPENDIX D**  
**CCM Details**

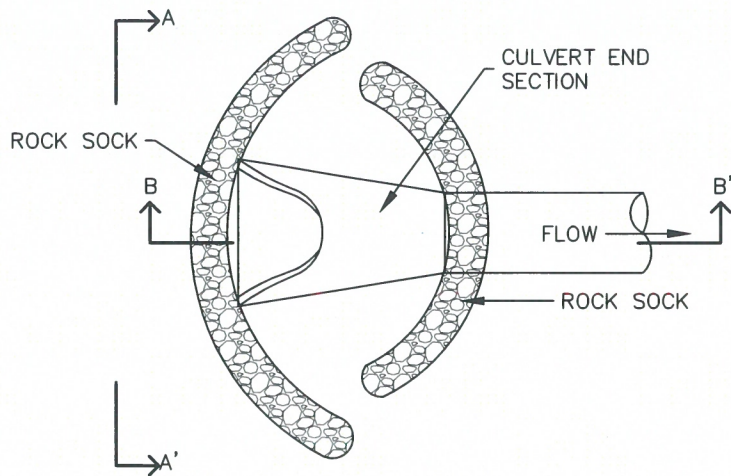

**CULVERT INLET PROTECTION PLAN**



**SECTION A-A'**



**SECTION B-B'**


**INSTALLATION NOTES**


1. SEE ROCK SOCK DETAIL.

**MAINTENANCE NOTES**


1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. ACCUMULATED SEDIMENT UPSTREAM OF THE CULVERT SHALL BE REMOVED WHEN THE SEDIMENT DEPTH IS  $\frac{1}{2}$  HEIGHT OF THE ROCK SOCK.
3. CULVERT INLET PROTECTION SHALL REMAIN UNTIL THE UPSTREAM AREA IS PERMANENTLY STABILIZED.



|   |                       |                        |
|---|-----------------------|------------------------|
| <b>CULVERT INLET PROTECTION</b>   |                       |                        |
| APPROVED:  |                       |                        |
| SWENT MANAGER   |                       |                        |
| ISSUED:<br>10/7/19  | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-CIP |

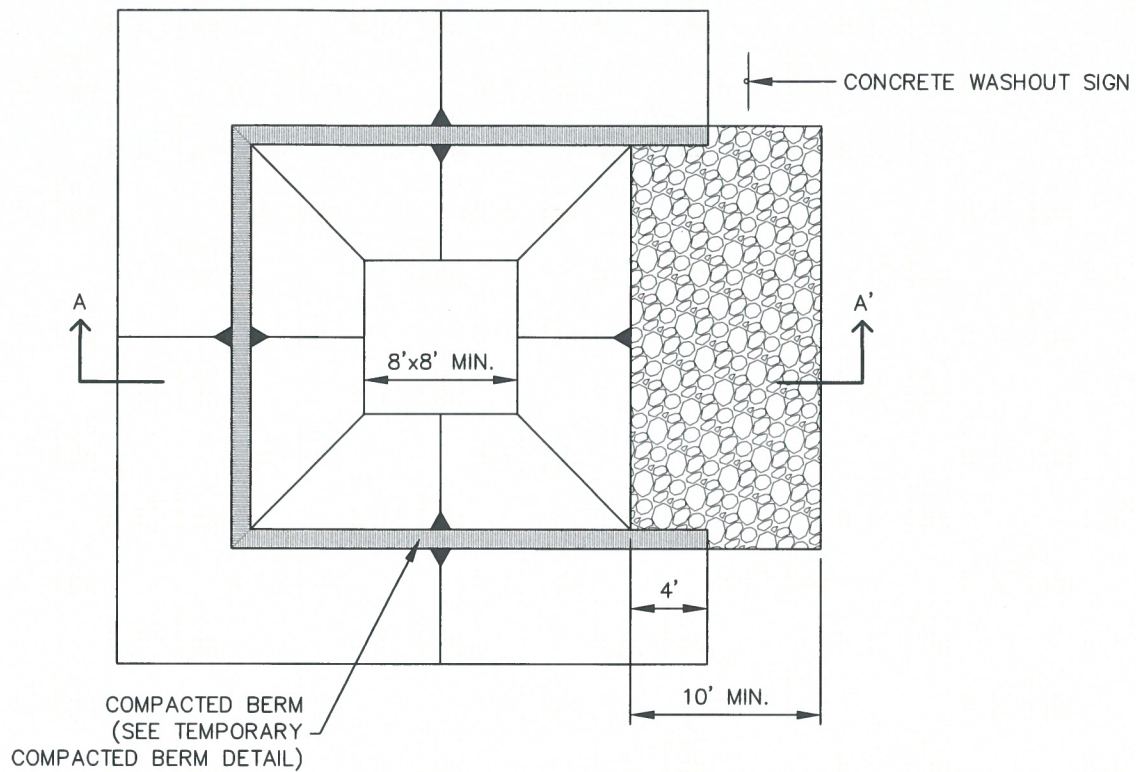

**CONCRETE WASHOUT AREA PLAN**

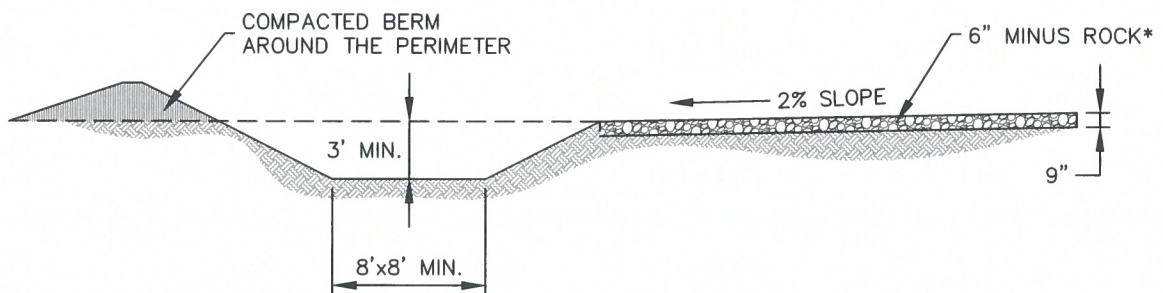

**SECTION A-A'**

\*ROCK REQUIRED BASED ON  
SITE CONDITIONS AT THE  
DISCRETION OF THE GEC  
INSPECTOR



|                                  |                       |                          |
|----------------------------------|-----------------------|--------------------------|
| <b>CONCRETE<br/>WASHOUT AREA</b> |                       |                          |
| APPROVED:                        |                       |                          |
| SWENT MANAGER                    |                       |                          |
| ISSUED:<br>10/7/19               | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-CWA-1 |


INSTALLATION NOTES

1. SEE PLAN VIEW FOR:  
-LOCATION OF CONCRETE WASHOUT AREA
2. LOCATE AT LEAST 50' AWAY FROM STATE WATERS MEASURED HORIZONTALLY.
3. AN IMPERMEABLE LINER (16 MIL. MINIMUM THICKNESS) IS REQUIRED IF CONCRETE WASH AREA IS LOCATED WITHIN 400' OF STATE WATERS OR 1000' OF WELLS OR DRINKING WATER SOURCES.
4. DO NOT LOCATE IN AREAS WHERE SHALLOW GROUNDWATER MAY BE PRESENT.
5. THE CONCRETE WASH AREA SHALL BE INSTALLED PRIOR TO CONCRETE PLACEMENT ON SITE.
6. CONCRETE WASH AREA SHALL INCLUDE A FLAT SUBSURFACE PIT THAT IS AT LEAST 8' BY 8'.
7. BERM SURROUNDING SIDES AND BACK OF CONCRETE WASH AREA SHALL HAVE A MINIMUM HEIGHT OF 2 FEET.
8. CONCRETE WASH AREA ENTRANCE SHALL BE SLOPED 2% TOWARDS THE CONCRETE WASH AREA.
9. SIGNS SHALL BE PLACED AT THE CONCRETE WASH AREA.
10. USE EXCAVATED MATERIAL FOR PERIMETER BERM CONSTRUCTION.


MAINTENANCE NOTES

1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. THE CONCRETE WASH AREA SHALL BE REPAIRED, CLEANED, OR ENLARGED AS NECESSARY TO MAINTAIN CAPACITY FOR CONCRETE WASTE. CONCRETE MATERIALS ACCUMULATED IN THE PIT SHALL BE REMOVED ONCE THE MATERIALS HAVE REACHED A DEPTH OF 2/3 THE HEIGHT OF THE CONCRETE WASH AREA.
3. CONCRETE WASHOUT WATER, WASTED PIECES OF CONCRETE, AND ALL OTHER DEBRIS IN THE SUBSURFACE PIT SHALL BE TRANSPORTED FROM THE JOB SITE IN A WATER-TIGHT CONTAINER AND DISPOSED OF PROPERLY.
4. THE CONCRETE WASH AREA SHALL REMAIN IN PLACE UNTIL ALL CONCRETE FOR THE PROJECT IS PLACED.
5. PERMANENTLY STABILIZE AREA AFTER CONCRETE WASH AREA IS REMOVED.




|                    |   |                          |  |
|--------------------|---|--------------------------|--|
|                    | <b>CONCRETE WASHOUT AREA</b>  |                          |  |
|                    | APPROVED:  |                          |  |
| ISSUED:<br>10/7/19 | REVISED:<br>8/19/2020   | DRAWING NO.<br>900-CWA-2 |  |




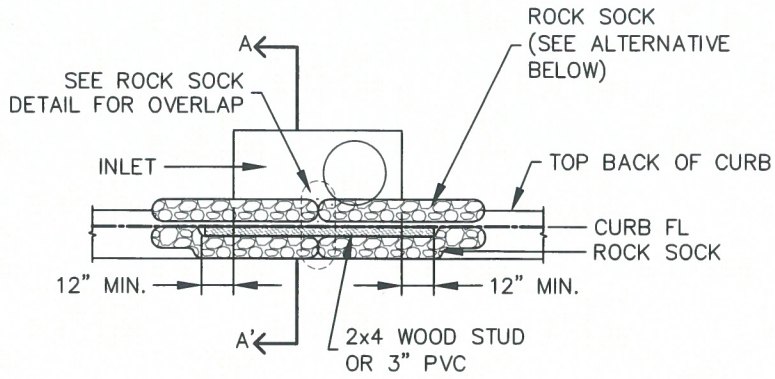

**CURB INLET PROTECTION PLAN**

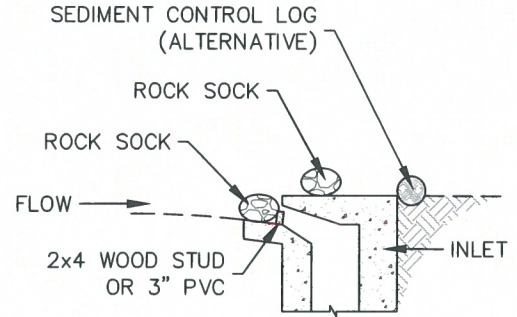

**SECTION A-A'**

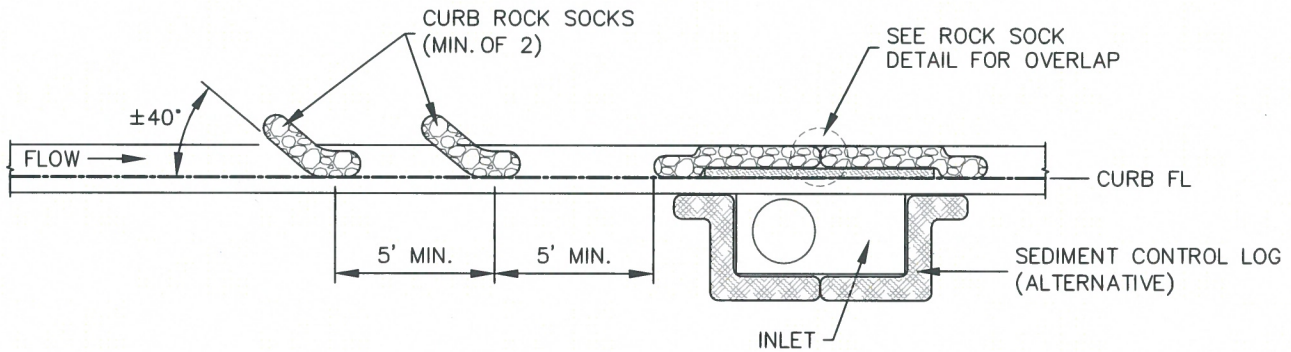

**CURB ROCK SOCKS UPSTREAM OF INLET PROTECTION**

**INSTALLATION NOTES**

1. SEE ROCK SOCK DETAIL FOR INSTALLATION REQUIREMENTS.
2. PLACEMENT OF THE ROCK SOCK SHALL BE APPROXIMATELY 40 DEGREES FROM THE CURB.
3. ROCK SOCKS ARE TO BE FLUSH WITH THE CURB AND SPACED A MINIMUM OF 5' APART.
4. AT LEAST TWO CURB ROCK SOCKS IN SERIES ARE REQUIRED UPSTREAM OF ON-GRADE INLETS.
5. ADDITIONAL ROCK SOCKS MAY BE REQUIRED AT GEC INSPECTOR'S DISCRETION.

**MAINTENANCE NOTES**

1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. ACCUMULATED SEDIMENT MUST BE REMOVED WHEN THE HEIGHT REACHES 1/2 OF THE DESIGN DEPTH OF THE INLET BARRIER.
3. ROCK SOCKS MUST REMAIN UNTIL THE UPSTREAM DISTURBANCE AREA IS STABILIZED.
4. PERMANENTLY STABILIZE AREA BEHIND INLET AFTER ROCK SOCKS ARE REMOVED WHEN REMOVAL IS APPROPRIATE.


IP-1




**ON-GRADE INLET PROTECTION**

APPROVED: *[Signature]*  
SWENT MANAGER

|                    |                       |                         |
|--------------------|-----------------------|-------------------------|
| ISSUED:<br>10/7/19 | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-IP-1 |
|--------------------|-----------------------|-------------------------|

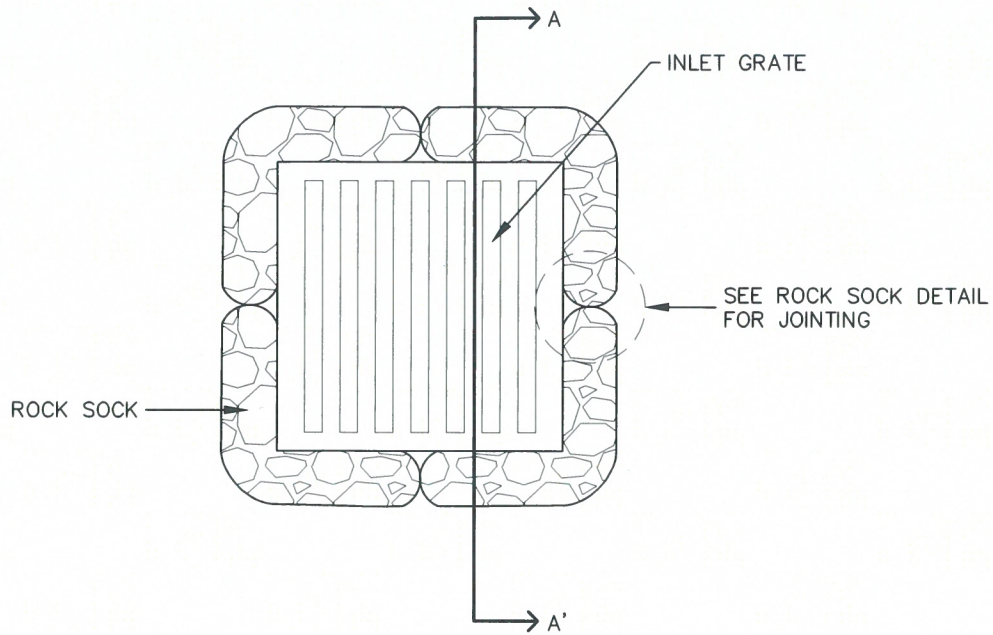

**ROCK SOCK SUMP INLET PROTECTION PLAN**

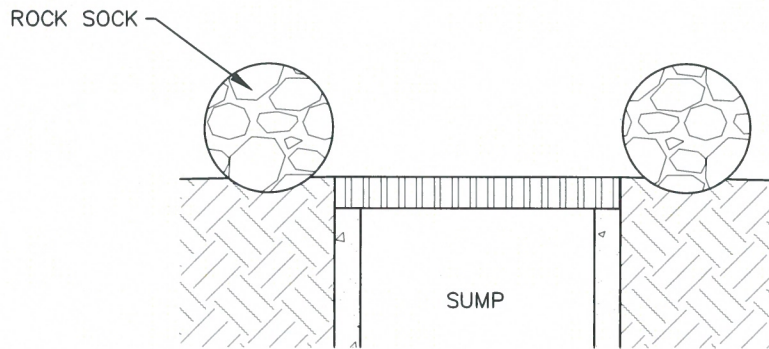

**SECTION A-A'**

**INSTALLATION NOTES**

1. SEE ROCK SOCK DETAIL FOR INSTALLATION REQUIREMENTS.
2. SEDIMENT CONTROL LOGS MAY BE USED IN PLACE OF ROCK SOCKS IN PVIOUS AREAS. INSTALL PER SEDIMENT CONTROL LOG DETAIL
3. CONTROL MEASURES MUST BE WRAPPED AROUND INLET AS TIGHTLY AS POSSIBLE.

**MAINTENANCE NOTES**

1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. ACCUMULATED SEDIMENT MUST BE REMOVED WHEN THE HEIGHT REACHES 1/2 OF THE DESIGN DEPTH OF THE INLET BARRIER.
3. ROCK SOCKS MUST REMAIN UNTIL THE UPSTREAM DISTURBANCE AREA IS STABILIZED.
4. PERMANENTLY STABILIZE AREA AROUND INLET AFTER ROCK SOCKS ARE REMOVED WHEN REMOVAL IS APPROPRIATE.


IP-2




**SUMP INLET PROTECTION**

APPROVED:   
SWENT MANAGER

|                    |                       |                         |
|--------------------|-----------------------|-------------------------|
| ISSUED:<br>10/7/19 | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-IP-2 |
|--------------------|-----------------------|-------------------------|

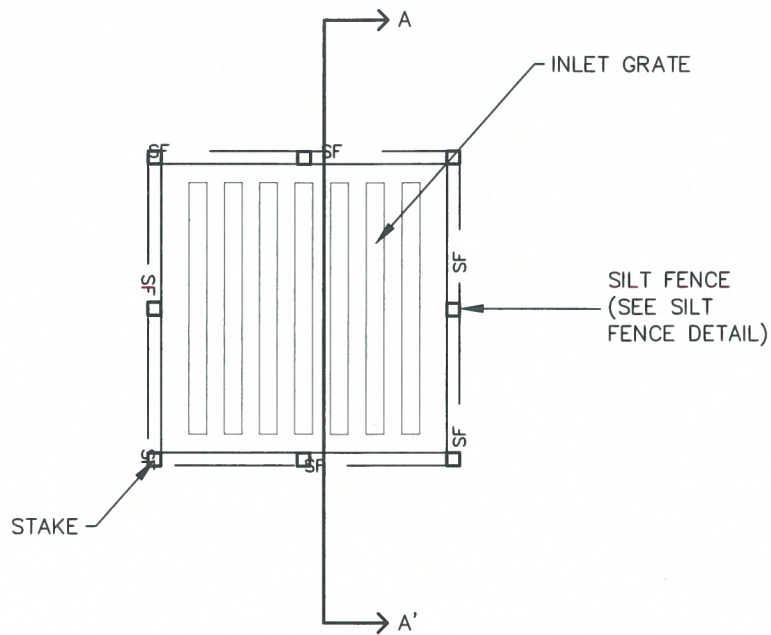

**SILT FENCE SUMP INLET PROTECTION PLAN**

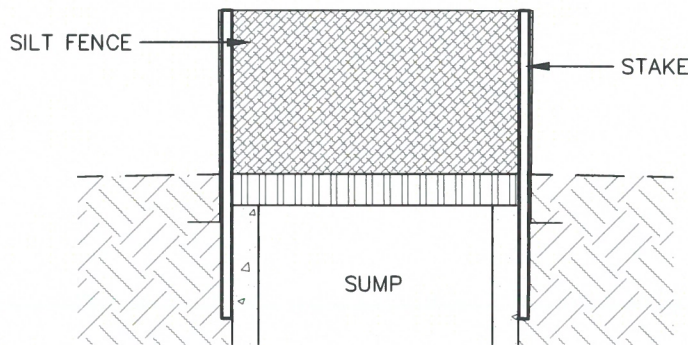

**SECTION A-A'**

**INSTALLATION NOTES**


1. SEE SILT FENCE DETAIL FOR INSTALLATION REQUIREMENTS.
2. POSTS SHALL BE PLACED AT EACH CORNER OF THE INLET AND AROUND THE EDGES AT A MAXIMUM SPACING OF THREE FEET.
3. SILT FENCE FABRIC SHOULD HAVE A FLOW RATE IN EXCESS OF 30 GALLONS PER MINUTE PER SQUARE YARD SO AS TO ALLOW SOME WATER FLOW AND NOT DAM THE WATER. STANDARD, LOW-FLOW SILT FENCE FABRIC WILL NOT BE ALLOWED.

**MAINTENANCE NOTES**


1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. ACCUMULATED SEDIMENT MUST BE REMOVED WHEN THE HEIGHT REACHES 1/2 OF THE DESIGN DEPTH OF THE INLET BARRIER.
3. SILT FENCE MUST REMAIN UNTIL THE UPSTREAM DISTURBANCE AREA IS STABILIZED.
4. PERMANENTLY STABILIZE AREA AROUND INLET AFTER SILT FENCE IS REMOVED WHEN REMOVAL IS APPROPRIATE.

IP-3

|                    |                              |                         |  |
|--------------------|------------------------------|-------------------------|--|
|                    | <b>SUMP INLET PROTECTION</b> |                         |  |
|                    | APPROVED:                    |                         |  |
|                    | SWENT MANAGER                |                         |  |
| ISSUED:<br>10/7/19 | REVISED:<br>8/19/2020        | DRAWING NO.<br>900-IP-3 |  |

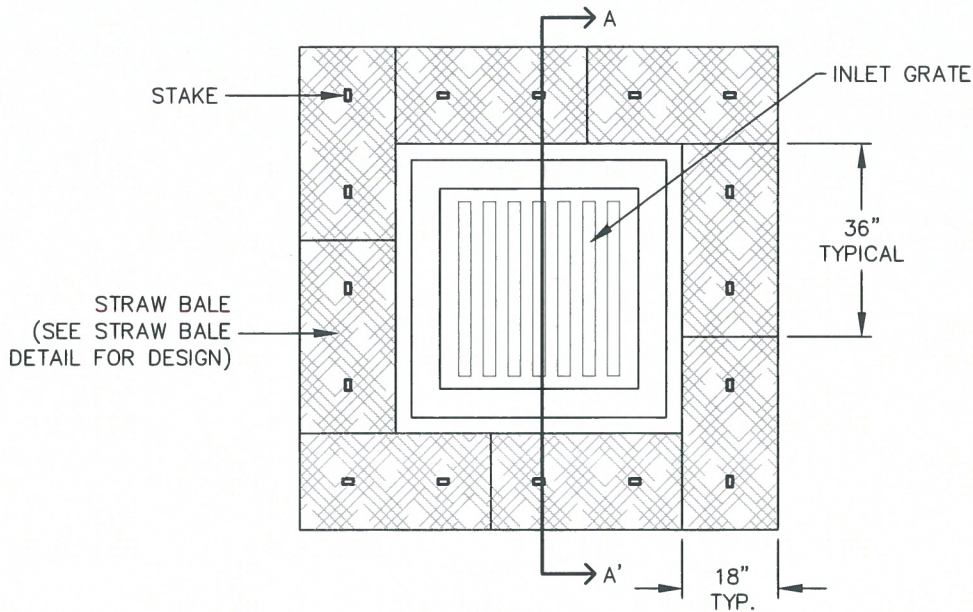

**STRAW BALE SUMP INLET PROTECTION PLAN**

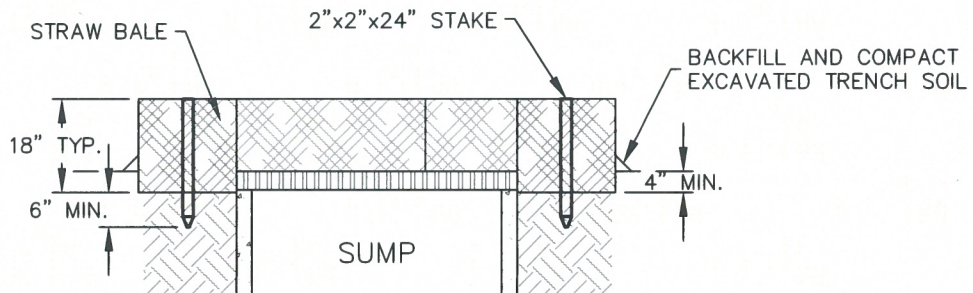

**SECTION A-A'**

**INSTALLATION NOTES**

1. BALES SHALL BE PLACED IN A SINGLE ROW AROUND THE INLET WITH THE ENDS OF THE BALES TIGHTLY ABUTTING ONE ANOTHER.
2. STRAW BALES SHALL CONSIST OF CERTIFIED WEED FREE STRAW OR HAY. LOCAL JURISDICTIONS MAY REQUIRE PROOF THAT BALES ARE WEED FREE.
3. STRAW BALES SHALL CONSIST OF APPROXIMATELY 5 CUBIC FEET OF STRAW OR HAY AND WEIGH NOT LESS THAN 35 POUNDS.
4. STRAW BALE DIMENSIONS SHALL BE APPROXIMATELY 36"x18"x18".
5. A UNIFORM ANCHOR TRENCH SHALL BE EXCAVATED TO A DEPTH OF 4". STRAW BALES SHALL BE PACED SO THAT THE BINDING TWINE IS ENCOMPASSING THE VERTICAL SIDES OF THE BALE(S).
6. TWO (2) WOODEN STAKES SHALL BE USED TO HOLD EACH BALE IN PLACE. WOODEN STAKED SHALL BE 2"x2"x24 (MIN.)". WOODEN STAKES SHALL BE DRIVEN A MINIMUM OF 6" INTO THE GROUND.


**MAINTENANCE NOTES**

1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. ACCUMULATED SEDIMENT MUST BE REMOVED WHEN THE HEIGHT REACHES 1/2 OF THE DESIGN DEPTH OF THE INLET BARRIER.
3. STRAW BALES MUST REMAIN UNTIL THE UPSTREAM DISTURBANCE AREA IS STABILIZED.
4. PERMANENTLY STABILIZE AREA AROUND INLET AFTER STRAW BALES ARE REMOVED WHEN REMOVAL IS APPROPRIATE.
5. STRAW BALES SHALL BE REPLACED IF THEY BECOME HEAVILY SOILED, ROTTEN OR DAMAGED BEYOND REPAIR.

IP-4




**SUMP INLET PROTECTION**

|   |                       |                         |
|---|-----------------------|-------------------------|
| APPROVED:  |                       |                         |
| SWENT MANAGER   |                       |                         |
| ISSUED:<br>10/7/19  | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-IP-4 |


CONTRACTOR SHALL ANCHOR PORTABLE TOILET TO THE GROUND, AT A MINIMUM OF TWO OPPOSING CORNERS (ON A DIAGONAL) USING U-SHAPED REBAR STAKES

TOP BACK OF CURB, ATTACHED SIDEWALK, OR OTHER IMPERVIOUS AREAS

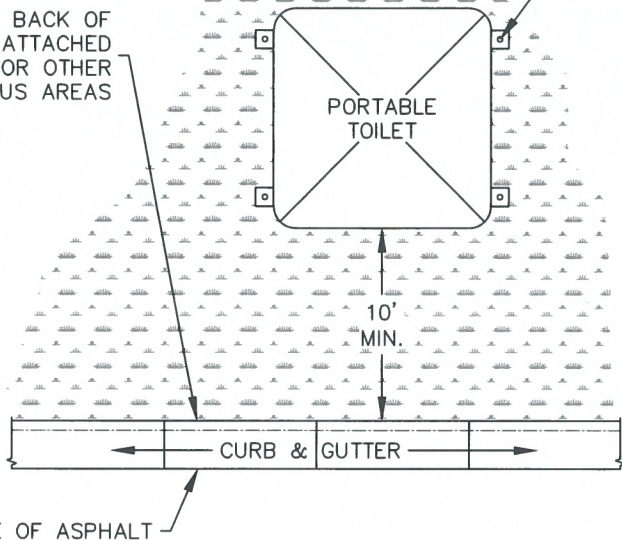

**PORTABLE TOILET PLAN**

PORTABLE TOILET (TYPICAL)

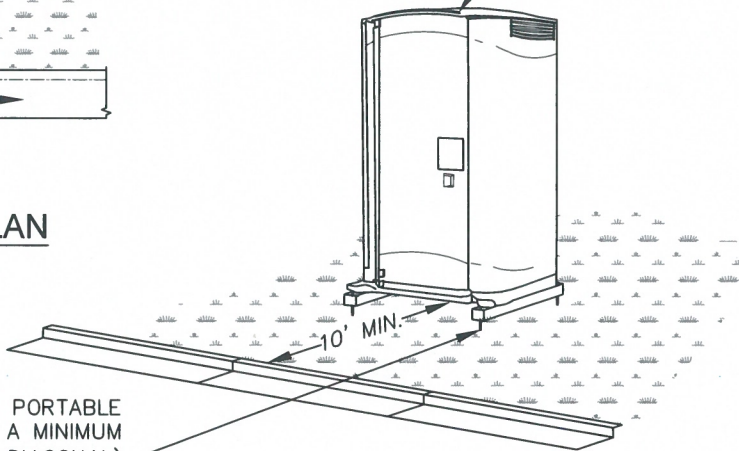

**ISOMETRIC**

CONTRACTOR SHALL ANCHOR PORTABLE TOILET TO THE GROUND, AT A MINIMUM OF TWO OPPOSING CORNERS (ON A DIAGONAL) USING U-SHAPED REBAR STAKES OR OTHER EFFECTIVE ANCHORING


**INSTALLATION NOTES**


1. PORTABLE TOILETS SHALL BE PLACED A MINIMUM OF 10 FEET BEHIND ALL CURBS, SIDEWALKS, AND OTHER IMPERVIOUS AREAS; 50 FEET FROM STORM INLETS, AND 100 FEET FROM WATERWAYS.
2. PORTABLE TOILETS IN THE RIGHT-OF-WAY ARE REQUIRED TO BE PLACED ON MOBILE TRAILERS AND MUST BE ANCHORED OR WEIGHTED DOWN. PORTABLE TOILETS MAY BE INSTALLED IN ACCORDANCE WITH NOTE #1 IN STAGING AREAS/YARDS.
3. PORTABLE TOILETS SHALL BE SECURELY ANCHORED TO THE GROUND USING U-SHAPED REBAR STAKES, OR OTHER EFFECTIVE ANCHORING.
4. ANCHORING SHALL BE POSITIONED ON AT LEAST TWO OPPOSING (DIAGONAL) CORNERS.
5. TOILET CONTAINMENT PANS MAY BE USED IN PLACE OF A TRAILER AT THE GEC INSPECTOR'S DISCRETION. TOILET CONTAINMENT PANS MUST BE ANCHORED IN PLACE AND MUST NOT BE USED WITHIN THE CITY R.O.W.

**MAINTENANCE NOTES**


1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. PORTABLE TOILETS SHALL BE SERVICED AT THE NECESSARY INTERVALS TO ELIMINATE THE POSSIBILITY OF OVERFLOW.
3. WHEN THE PORTABLE TOILETS ARE REMOVED, ANY DISTURBED AREAS ASSOCIATED WITH THE INSTALLATION, MAINTENANCE, AND/OR REMOVAL OF THE TOILETS MUST BE PERMANENTLY STABILIZED.




|   |                       |                        |
|---|-----------------------|------------------------|
| <b>PORTABLE TOILET</b>  |                       |                        |
| APPROVED:  |                       |                        |
| SWENT MANAGER   |                       |                        |
| ISSUED:<br>2/19/19  | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-PTM |

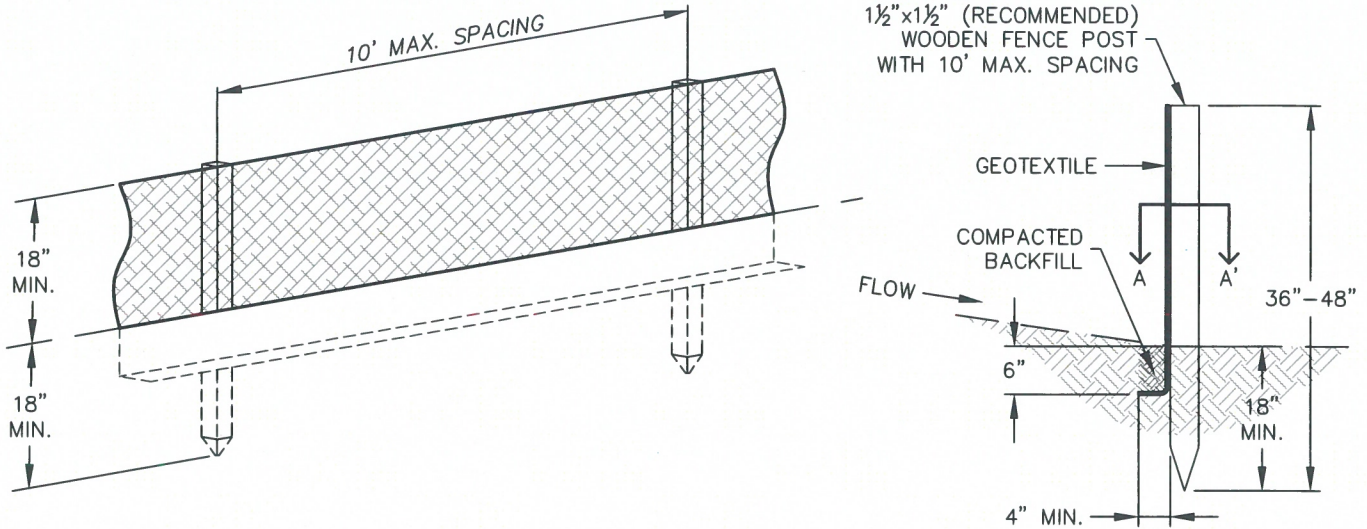

**SILT FENCE**



**J-HOOK INSTALLATION**



**SECTION A-A'**

**INSTALLATION NOTES**


1. SILT FENCE MUST BE PLACED ON A FLAT SURFACE 2'-5' AWAY FROM TOE OF THE SLOPE TO ALLOW FOR PONDING AND DEPOSITION.
2. COMPACT THE TRENCH USING A JUMPING JACK OR WHEEL ROLLING TO THE POINT THAT THE FENCE RESISTS BEING PULLED OUT OF THE GROUND BY HAND.
3. SILT FENCE SHALL BE TAUT WITH NO SAGS AFTER IT HAS BEEN ANCHORED.
4. FABRIC SHALL BE ATTACHED TO POSTS WITH 1" HEAVY DUTY STAPLES OR 1" NAILS. THESE SHOULD BE PLACED VERTICALLY DOWN THE POST, 3" APART.
5. THE PREFERRED INSTALLATION METHOD USES A TRENCHER OR SILT FENCE INSTALLATION DEVICE.
6. INSTALL SILT FENCE ALONG THE CONTOUR OF THE SLOPES OR IN A MANNER TO AVOID CREATING CONCENTRATED FLOW (SUCH AS A "J-HOOK" INSTALLATION).

**MAINTENANCE NOTES**


1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. ACCUMULATED SEDIMENT MUST BE REMOVED WHEN THE HEIGHT REACHES 1/2 OF THE DESIGN HEIGHT OF THE SILT FENCE.
3. SILT FENCE MUST REMAIN UNTIL THE UPSTREAM DISTURBANCE AREA IS STABILIZED.
4. PERMANENTLY STABILIZE AREA AFTER SILT FENCE IS REMOVED.




**SILT FENCE**

APPROVED:   
SWENT MANAGER

|                    |                       |                       |
|--------------------|-----------------------|-----------------------|
| ISSUED:<br>10/7/19 | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-SF |
|--------------------|-----------------------|-----------------------|

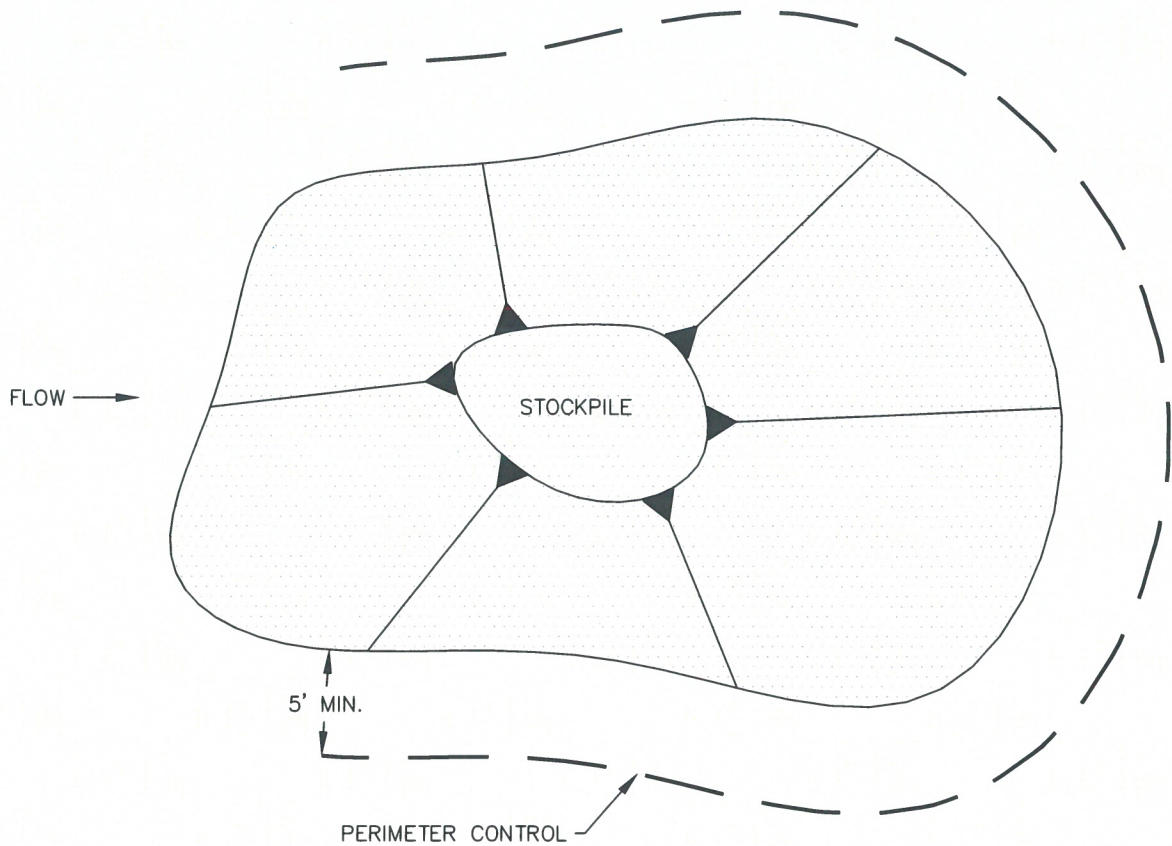

**STOCKPILE PROTECTION PLAN**

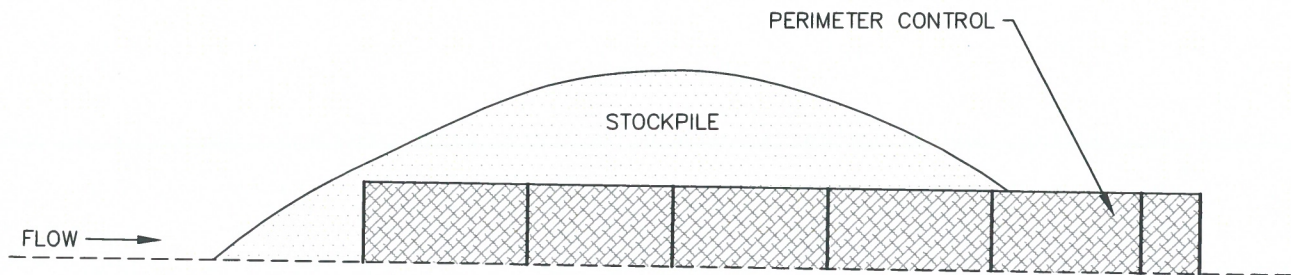

**STOCKPILE PROTECTION ELEVATION**

**INSTALLATION NOTES**


1. INSTALL PERIMETER CONTROL AROUND STOCKPILE ON DOWNGRAIDENT SIDE. PERIMETER CONTROL MUST BE SUITABLE TO SITE CONDITIONS AND INSTALLED ACCORDING TO THE RELEVANT DETAIL.
2. FOR STOCKPILES ON THE INTERIOR PORTION OF A CONSTRUCTION SITE, WHERE OTHER DOWNGRAIDENT CONTROLS INCLUDING PERIMETER CONTROL ARE IN PLACE, STOCKPILE PERIMETER CONTROLS MAY NOT BE REQUIRED.

**MAINTENANCE NOTES**


1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. IF PERIMETER CONTROLS MUST BE MOVED TO ACCESS STOCKPILE, REPLACE PERIMETER CONTROLS BY THE END OF THE WORK DAY.
3. ACCUMULATED SEDIMENT MUST BE REMOVED ACCORDING TO PERIMETER CONTROL DETAIL.




**STOCKPILE PROTECTION**

APPROVED:   
SWENT MANAGER

|                    |                       |                       |
|--------------------|-----------------------|-----------------------|
| ISSUED:<br>10/7/19 | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-SP |
|--------------------|-----------------------|-----------------------|

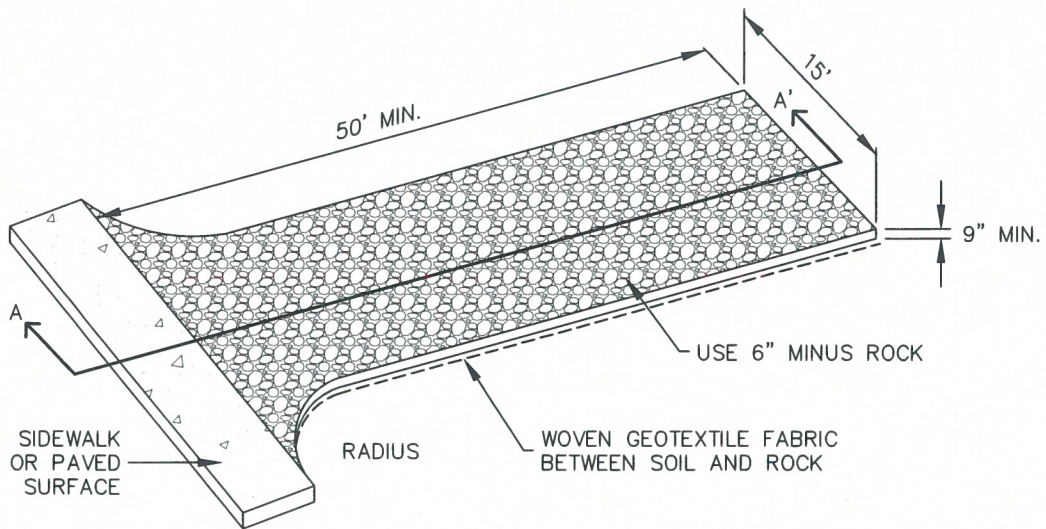

**AGGREGATE VEHICLE TRACKING CONTROL**

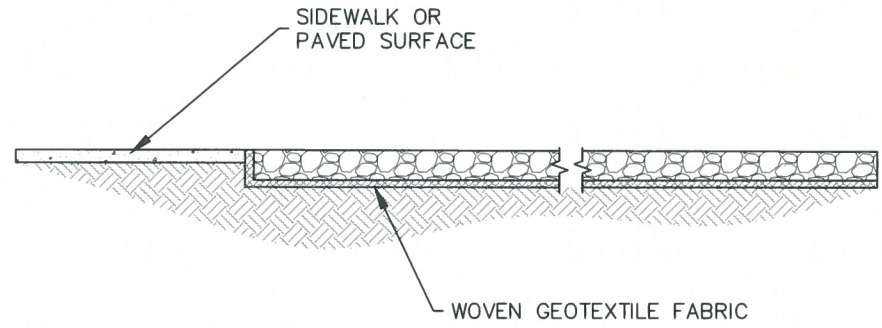

**SECTION A-A'**

INSTALLATION NOTES

1. A STABILIZED CONSTRUCTION ENTRANCE/EXIT SHOULD BE LOCATED AT ALL POINTS WHERE VEHICLES EXIT THE CONSTRUCTION SITE TO ADJACENT ROADWAY.
2. STABILIZED CONSTRUCTION ENTRANCE/EXITS SHALL BE INSTALLED PRIOR TO ANY LAND DISTURBING ACTIVITIES.
3. RADIUS MUST BE ADEQUATE FOR INTENDED CONSTRUCTION VEHICLE TURNING.
4. ROCK SHOULD CONSIST OF 6" MINUS ROCK.
5. INSTALL CONSTRUCTION FENCE ON BOTH SIDES OF VEHICLE TRACKING CONTROL PAD WHEN NEEDED OR REQUIRED BY INSPECTOR.

MAINTENANCE NOTES

1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. SEDIMENT TRACKED ONTO THE ADJACENT ROAD SHALL BE REMOVED DAILY, BY SWEEPING OR SHOVELING, AND NEVER WASHED DOWN STORM DRAINS.
3. ROUGHEN, REPLACE AND/OR ADD ROCK AS NEEDED TO MAINTAIN CONSISTENT DEPTH AND TO PREVENT SEDIMENT TRACKING ONTO ADJACENT STREET.
4. PERMANENTLY STABILIZE AREA AFTER VEHICLE TRACKING CONTROL IS REMOVED.




|   |                       |                        |
|---|-----------------------|------------------------|
| <b>VEHICLE TRACKING CONTROL</b>   |                       |                        |
| APPROVED:  |                       |                        |
| SWENT MANAGER   |                       |                        |
| ISSUED:<br>10/7/19  | REVISED:<br>8/19/2020 | DRAWING NO.<br>900-VTC |



**APPENDIX E**  
**SWMP Plan (GEC Plan)**

STATE OF COLORADO  
DEPARTMENT OF TRANSPORTATION  
CITY OF COLORADO SPRINGS  
Parks, Recreation and Cultural Services Department  
CAPITAL IMPROVEMENT PROJECT  
TRAIL IMPROVEMENT PROGRAM  
COMBINED FEDERAL AID PROJECT No. TAP M240-162, SubAccT. No.20391  
**GRADING AND EROSION CONTROL**  
PLAN of the ROCK ISLAND MULTI-USE TRAIL  
SAND CREEK TO CONSTITUTION AVENUE  
COLORADO SPRINGS & EL PASO COUNTY, COLORADO




| SHEET INDEX |                          |
|-------------|--------------------------|
| G1          | COVER SHEET              |
| G2          | STANDARD NOTES & DETAILS |
| GEC 1       | STA 08+00 TO STA 17+50   |
| GEC 2       | STA 17+50 TO STA 21+50   |
| GEC 3       | STA 21+50 TO STA 47+50   |
| GEC 4       | STA 47+50 TO STA 75+00   |
| GEC 5       | STA 75+00 TO STA 102+00  |
| GEC 6       | STA 102+00 TO STA 117+50 |
| GEC 7       | EROSION CONTROL DETAILS  |
| GEC 8       | EROSION CONTROL DETAILS  |

| TRAIL DATA DESIGN               |                       |
|---------------------------------|-----------------------|
| BEGIN STATION ROCK ISLAND TRAIL | 8+00                  |
| END STATION ROCK ISLAND TRAIL   | 106+15                |
| MAXIMUM GRADE                   | 8.33%                 |
| MINIMUM HORIZONTAL CURVE        | 25'                   |
| MINIMUM WIDTH                   | 8'                    |
| TYPICAL WIDTH                   | 10' (+ 2' Shoulder)   |
| MAXIMUM WIDTH                   | 12' (+ 2' Shoulder)   |
| CROSS-SLOPE                     | 2% (towards drainage) |
| LENGTH SAND CREEK TRAIL         | 10,900 LF             |
| SITE AREA                       | 36.8 ACRES            |
| AREA OF DISTURBANCE             | 18.2 ACRES            |
| CONSTRUCTION AREA               | 18.2 ACRES            |


BENCHMARK: FIMS MONUMENT SR10 IS A 2-INCH DIAMETER ALUMINUM CAP STAMPED "CSU FIMS CONTROL SR10" ON TOP OF THE NORTH CURB OF CONSTITUTION AVENUE AT THE NORTHWEST CORNER OF THE BRIDGE OVER SAND CREEK.

\*A.G.A./A.P.W.A. STANDARD UTILITY MARKING COLOR CODE

|             |        |
|-------------|--------|
| NATURAL GAS | YELLOW |
| ELECTRIC    | RED    |
| WATER       | BLUE   |
| WASTEWATER  | GREEN  |



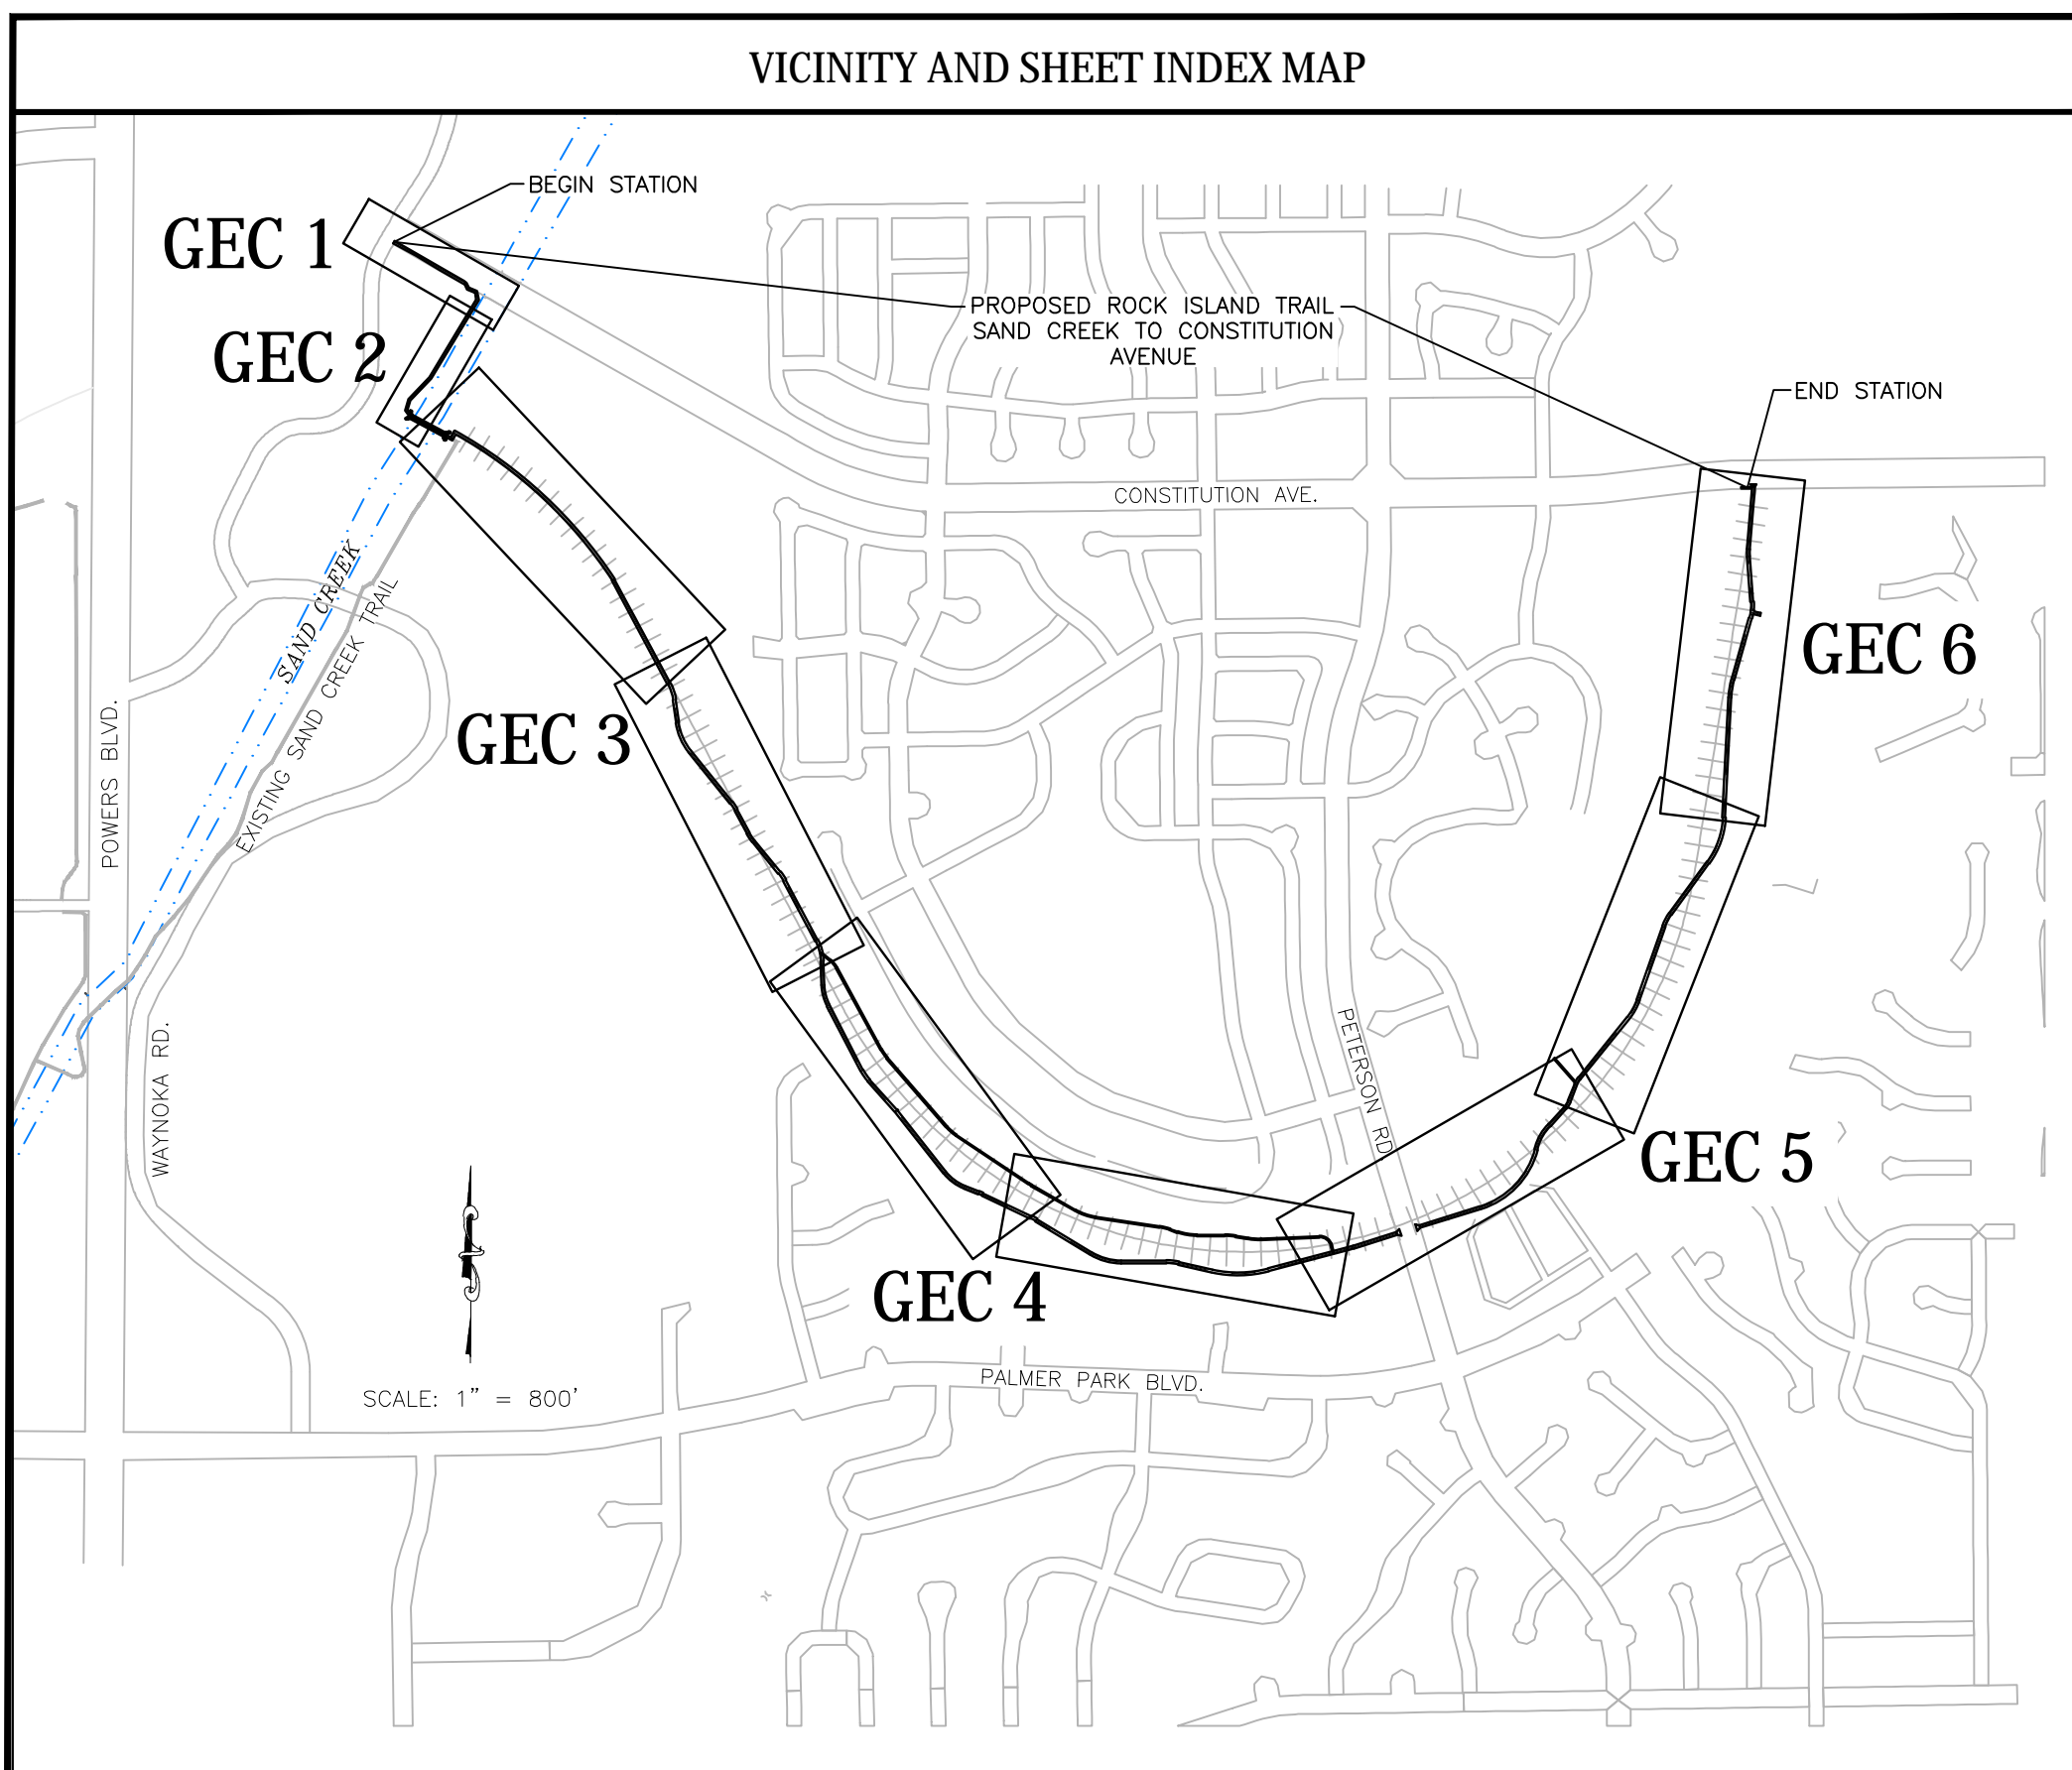


Know what's below.  
Call before you dig.



| APPROVAL SIGNATURES                         |                     |           |       |
|---|---------------------|-----------|-------|
| TITLE                                       | NAME                | SIGNATURE | DATE  |
| DIRECTOR, PARKS, REC. & CULT. SVS PARKS     | BRITT HALEY         | _____     | _____ |
| OPERATION & DEVELOPMENT MANAGER             |                     | _____     | _____ |
| CITY FORESTER                               |                     | _____     | _____ |
| REG. SUPERVISOR, PARKS, TRAILS & OPEN SPACE | SCOTT ABBOTT        | _____     | _____ |
| CONSTRUCTION PROJECT MANAGER                | EMILY DUNCAN        | _____     | _____ |
| COLORADO DEPARTMENT OF TRANSPORTATION       |                     | _____     | _____ |
| EL PASO COUNTY DEPARTMENT OF PUBLIC WORKS   | JENNIFER IRVINE, PE | _____     | _____ |

| STATEMENTS   |            |
|--|------------|
| <b>Engineer's Statement:</b>   |            |
| This Grading and Erosion Control Plan was prepared under my direction and supervision and is correct to the best of my knowledge and belief. Said Plan has been prepared according to the criteria established by the County for Grading and Erosion Control Plans. I accept responsibility for any liability caused by any negligent acts or omissions on my part in preparing this Plan. |            |
| Engineer of Record signature _____   | Date _____ |
| <b>Owner's Statement:</b>  |            |
| I, the owner/developer have read and will comply with the requirements of this Grading and Erosion Control Plan.   |            |
| Signature _____  | Date _____ |
| <b>El Paso County:</b>   |            |
| County Plan review is provided only for general conformance with County Design Criteria. The County is not responsible for the accuracy and adequacy of the design, dimensions, and/or elevations which shall be confirmed at the job site. The County through the approval of this document assumes no responsibility for completeness and/or accuracy of this document.                  |            |
| Filed in accordance with the requirements of the El Paso County Land Development Code, Drainage Criteria Manual Volumes 1 and 2, and Engineering Criteria Manual as amended.   |            |
| In accordance with ECM Section 1.12, these construction documents will be valid for construction for a period of 2 years from the date signed by the El Paso County Engineer. If construction has not started within those 2 years, the Plans will need to be resubmitted for approval, including payment of review fees at the Planning and Community Development Director's discretion.  |            |
| County Engineer/ECM Administrator _____  | Date _____ |

|   |   |   |               |  |  |
|---|---|---|---------------|--|--|
|  |  <p>1604 South 21st Street<br/>Colorado Springs, Colorado 80904<br/>(719) 630-7342</p> | Sheet Revisions   | IFC           | <b>ROCK ISLAND TRAIL</b><br>GRADING AND EROSION CONTROL PLAN<br><b>COVER SHEET</b> | Kiowa Proj. No. 16028                                  |
|   |   |  | No Revisions: |  | Designer: TAC<br>Detailer: JDC/TEG<br>Date: 11/22/2024 |
| For and on Behalf of<br>Kiowa Engineering Corporation Date                          |   |   | Void:         | SubAcct No. 20391  | Sheet Number G1  |

**EL PASO COUNTY STANDARD  
NOTES FOR GRADING & EROSION CONTROL PLANS**

- Stormwater discharges from construction sites shall not cause or threaten to cause pollution, contamination, or degradation of state waters. All work and earth disturbance shall be done in a manner that minimizes pollution of any on-site or off-site waters, including wetlands.
- Notwithstanding anything depicted in these plans in words or graphic representation, all design and construction related to roads, storm drainage and erosion control shall conform to the standards and requirements of the most recent version of the relevant adopted El Paso County standards, including the Land Development Code, the Engineering Criteria Manual, the Drainage Criteria Manual, and the Drainage Criteria Manual Volume 2. Any deviations from regulations and standards must be requested, and approved, in writing.
- A separate Stormwater Management Plan (SMWP) for this project shall be completed and an Erosion and Stormwater Quality Control Permit (ESQCP) issued prior to commencing construction. Management of the SWMP / CSWMP during construction is the responsibility of the designated Qualified Stormwater Manager or Certified Erosion Control Inspector. The SWMP / CSWMP shall be located on-site at all times during construction and shall be kept up to date with work progress and changes in the field.
- Once the ESQCP is approved and a "Notice to Proceed" has been issued, the contractor may install the initial stage erosion and sediment control measures as indicated on the approved GEC. A preconstruction meeting between the contractor, engineer, and El Paso County will be held prior to any construction. It is the responsibility of the applicant to coordinate the meeting time and place with County staff.
- Control measures must be installed prior to commencement of activities that could contribute pollutants to stormwater. Control measures for all slopes, channels, ditches, and disturbed land areas shall be installed immediately upon completion of the disturbance.
- All temporary sediment and erosion control measures shall be maintained and remain in effective operating condition until permanent soil erosion control measures are implemented and final stabilization is established. All persons engaged in land disturbance activities shall assess the adequacy of control measures at the site and identify if changes to those control measures are needed to ensure the continued effective performance of the control measures. All changes to temporary sediment and erosion control measures must be incorporated into the stormwater management plan.
- Temporary stabilization shall be implemented on disturbed areas and stockpiles where ground disturbing construction activity has permanently ceased or temporarily ceased for longer than 14 days.
- Final stabilization must be implemented at all applicable construction sites. Final stabilization is achieved when all ground disturbing activities are complete and all disturbed areas either have a uniform vegetative cover with individual plant density of 70 percent of pre-disturbance levels established or equivalent permanent alternative stabilization method is implemented. All temporary sediment and erosion control measures shall be removed upon final stabilization and before permit closure.
- All permanent stormwater management facilities shall be installed as designed in the approved plans. Any proposed changes that effect the design or function of permanent stormwater management structures must be approved by the ECM Administrator prior to implementation.
- Earth disturbances shall be conducted in such a manner so as to effectively minimize accelerated soil erosion and resulting sedimentation. All disturbances shall be designed, constructed, and completed so that the exposed area of any disturbed land shall be limited to the shortest practical period of time. Pre-existing vegetation shall be protected and maintained within 50 horizontal feet of a Waters of the State unless shown to be infeasible and specifically requested and approved.
- Compaction of soil must be prevented in areas designated for infiltration control measures or where final stabilization will be achieved by vegetative cover. Areas designated for infiltration control measures shall also be protected from sedimentation during construction until final stabilization is achieved. If compaction prevention is not feasible due to site constraints, all areas designated for infiltration and vegetation control measures must be loosened prior to installation of the control measure(s).
- Any temporary or permanent facility designed and constructed for the conveyance of stormwater around, through, or from the earth disturbance area shall be a stabilized conveyance designed to minimize erosion and the discharge of sediment off-site.
- Concrete wash water shall be contained and disposed of in accordance with the SWMP / CSWMP. No wash water shall be discharged to or allowed to enter state waters, including any surface or subsurface storm drainage system or facilities. Concrete washouts shall not be located in an area where shallow groundwater may be present, or within 50 feet of a surface water body, creek or stream.
- During dewatering operations, uncontaminated groundwater may be discharged on-site, but shall not leave the site in the form of surface runoff unless an approved state dewatering permit is in place.
- Erosion control blanketing or other protective covering shall be used on slopes steeper than 3:1.
- Contractor shall be responsible for the removal of all wastes from the construction site for disposal in accordance with local and state regulatory requirements. No construction debris, tree slash, building material wastes or unused building materials shall be buried, dumped, or discharged at the site.
- Waste materials shall not be temporarily placed or stored in the street, alley, or other public way, unless in accordance with an approved Traffic Control Plan. Control measures may be required by El Paso County Engineering if deemed necessary, based on specific conditions and circumstances.
- Tracking of soils and construction debris off-site shall be minimized. Materials tracked off-site shall be cleaned up and properly disposed of immediately.
- The owner/developer shall be responsible for the removal of all construction debris, dirt, trash, rock, sediment, soil, and sand that may accumulate in roads, storm drains and other drainage conveyance systems and stormwater appurtenances as a result of site development.
- The quantity of materials stored on the project site shall be limited, as much as practical, to that quantity required to perform the work in an orderly sequence. All materials stored on-site shall be stored in a neat, orderly manner, in their original containers, with the original manufacturer's labels.

**EL PASO COUNTY STANDARD  
NOTES FOR GRADING & EROSION CONTROL PLANS (cont)**

- No chemical(s) having the potential to be released in stormwater are to be stored or used on-site unless permission for the use of such chemical(s) is granted in writing by the ECM administrator. In granting approval for the use of such chemical(s), special conditions and monitoring may be required.
- Bulk storage of allowed petroleum products or other allowed liquid chemicals in excess of 55 gallons shall require adequate secondary containment protection to contain all spills on-site and to prevent any spilled materials from entering state waters, any surface or subsurface storm drainage system or other facilities.
- No person shall cause the impeding of stormwater flow in the curb and gutter or ditch except with approved sediment control measures.
- Owner/developer and their agents shall comply with the "Colorado Water Quality Control Act" (Title 25, Article 8, CRS), and the "Clean Water Act" (33 USC 1344), in addition to the requirements of the Land Development Code, DCM Volume II and the ECM Appendix I. All appropriate permits must be obtained by the contractor prior to construction (1041, NPDES, Floodplain, 404, fugitive dust, etc.). In the event of conflicts between these requirements and other laws, rules, or regulations of other federal, state, local, or county agencies, the most restrictive laws, rules, or regulations shall apply.
- All construction traffic must enter/exit the site only at approved construction access points.
- Prior to construction the permittee shall verify the location of existing utilities.
- A water source shall be available on-site during earthwork operations and shall be utilized as required to minimize dust from earthwork equipment and wind.
- The soils report for this site has been prepared by Kumar & Assoc., 3/29/11 and shall be considered a part of these plans.
- At least ten (10) days prior to the anticipated start of construction, for projects that will disturb one (1) acre or more, the owner or operator of construction activity shall submit a permit application for stormwater discharge to the Colorado Department of Public Health and Environment, Water Quality Division. The application contains certification of completion of a Stormwater Management Plan (SWMP / CSWMP), of which this Grading And Erosion Control Plan may be a part. For information or application materials contact:

Colorado Department of Public Health and Environment  
Water Quality Control Division  
WQCD - permits  
4300 Cherry Creek Drive South  
Denver, CO 80246-1530  
Attn: permits unit


**PROJECT SPECIFIC NOTES**

- Where El Paso County and Colorado Springs notes contradict, El Paso County notes shall supersede.
- The SWMP and CSWMP are the same document, one document.
- Anticipated start: 10/01/2024
- Anticipated Construction End: 10/31/2025
- Anticipated Stabilization: 8/01/2025
- Receiving water: Sand Creek
- Site is Native Grass and will remain Native Grass.
- There are no on site asphalt or concrete batch plants anticipated.
- There are no "no-build" areas on this site.
- Peterson Road is the primary access for the site. Constitution will only be used to access work on the west side of Sand Creek.

**COLORADO SPRINGS STANDARD  
GRADING & EROSION CONTROL PLAN NOTES**

- No clearing, grading, excavation, or other land disturbing activities shall be allowed (except for work directly related to the installation of Initial Control Measures) until a City GEC Permit has been issued.
- All land disturbing activities must be performed in accordance with and the approved GEC Plan and CSWMP.
- Initial Control Measures shall be installed and inspected prior to any land disturbance activities taking place. An initial site inspection will not be scheduled until a City GEC Permit has been "conditionally approved." Call City Stormwater Inspections, 385-5980, at least 48 hours prior to construction to schedule an initial inspection and obtain full permit approval.
- Individuals shall comply with the "Colorado Water Quality Control Act" (Title 25, Article 8, CRS) and the "Clean Water Act" (33 USC 1344), including regulations promulgated and certifications or permits issued, in addition to the requirements included in the City's MS4 Permit, Stormwater Construction Manual. In the event of conflicts between these requirements and water quality control laws, rules, or regulations of other Federal or State agencies, the more restrictive laws, rules, or regulations shall apply.
- Stormwater discharges from construction sites shall not cause or threaten to cause pollution, contamination, or degradation of State Waters.
- All Construction Control Measures shall be maintained until permanent stabilization measures are implemented. Temporary Construction Control Measures must be removed prior to permit closeout.
- Concrete wash water shall not be discharged to or allowed to runoff to State Waters or any surface or subsurface storm drainage system or facilities.
- Building, construction, excavation, or other waste materials shall not be temporarily placed or stored in the street, alley, or other public way, unless in accordance with an approved Traffic Control Plan. Construction Control Measures may be required by the GEC Inspector if deemed necessary based on specific conditions and circumstances (e.g., estimated time of exposure, season of the year, etc.).
- All wastes composed of building materials must be removed from the construction site for disposal in accordance with local and state regulatory requirements. No building material wastes or unused building materials shall be buried, dumped, or discharged at the site.
- The permittee shall be responsible for the removal of all construction debris, dirt, trash, rock, sediment, and sand that may accumulate in the storm sewer or other drainage conveyance system as a result of construction activities.
- The quantity of materials stored on the project site shall be limited, as much as practical, to that quantity required to perform the work in an orderly sequence. All materials stored on-site shall be stored in a neat, orderly manner, in their original containers, with original manufacturer's labels. Materials shall not be stored in a location where they may be carried by stormwater runoff into the storm sewer system at any time.
- Spill prevention and containment measures shall be used at all storage, equipment fueling, and equipment servicing areas so as to contain all spills and prevent any spilled material from entering the MS4, including any surface or subsurface storm drainage system or facility. Bulk storage structures for petroleum products and other chemicals shall have secondary containment or equivalent adequate protection. All spills shall be cleaned up immediately after discovery, or contained until appropriate cleanup methods can be employed. Manufacturer's recommended methods for spill cleanup shall be followed, along with proper disposal methods.
- Sediment (mud and dirt) transported onto a public road, regardless of the size of the site, shall be cleaned as soon as possible after discovery.
- No chemicals are to be added to the discharge unless permission for the use of a specific chemical is granted by the State. In granting the use of such chemicals, special conditions and monitoring may be required.
- Control Measures for all slopes, channels, ditches, or any disturbed land area shall be completed within fourteen (14) calendar days after final grading or final land disturbance has been completed. Disturbed areas which are not at final grade but will remain dormant for longer than fourteen (14) days shall be roughened, mulched, tackified, or stabilized with tarps within fourteen (14) days after interim grading. An area that is going to remain in an interim state for more than sixty (60) days shall also be seeded, unless an alternative stabilization measure is accepted at the inspector's discretion. All temporary Construction Control Measures shall be maintained until final stabilization is achieved.
- The GEC Plan will be subject to re-review and re-acceptance by the Stormwater Enterprise should any of the following occur: grading does not commence within twelve (12) months of the City's acceptance of the plan, the construction site is idle for twelve (12) consecutive months, a change in property ownership occurs, the planned development changes, or any other major modifications are proposed as defined in the Stormwater Construction Manual.
- It is not permissible for any person to modify the grade of the earth on any utility easement or utility right-of-way without written approval from the utility owner. City acceptance of the GEC Plan and CSWMP does not satisfy this requirement. The plan shall not increase or divert water towards utility facilities. Any changes to existing utility facilities to accommodate the plan must be approved by the affected utility owner prior to implementing the plan. The cost to relocate or protect existing utilities or to provide interim access shall be at the applicant's expense.
- Applicant represents and warrants that they have the legal authority to grade and/or construct improvements on adjacent property. The City has not reviewed the developer's authority to modify adjacent property. An approved GEC Permit does not provide approval for the Applicant to perform work on adjacent property.

NOTE: BLOCK COLOR SHALL BE APPROVED BY THE OWNER PRIOR TO CONSTRUCTION.

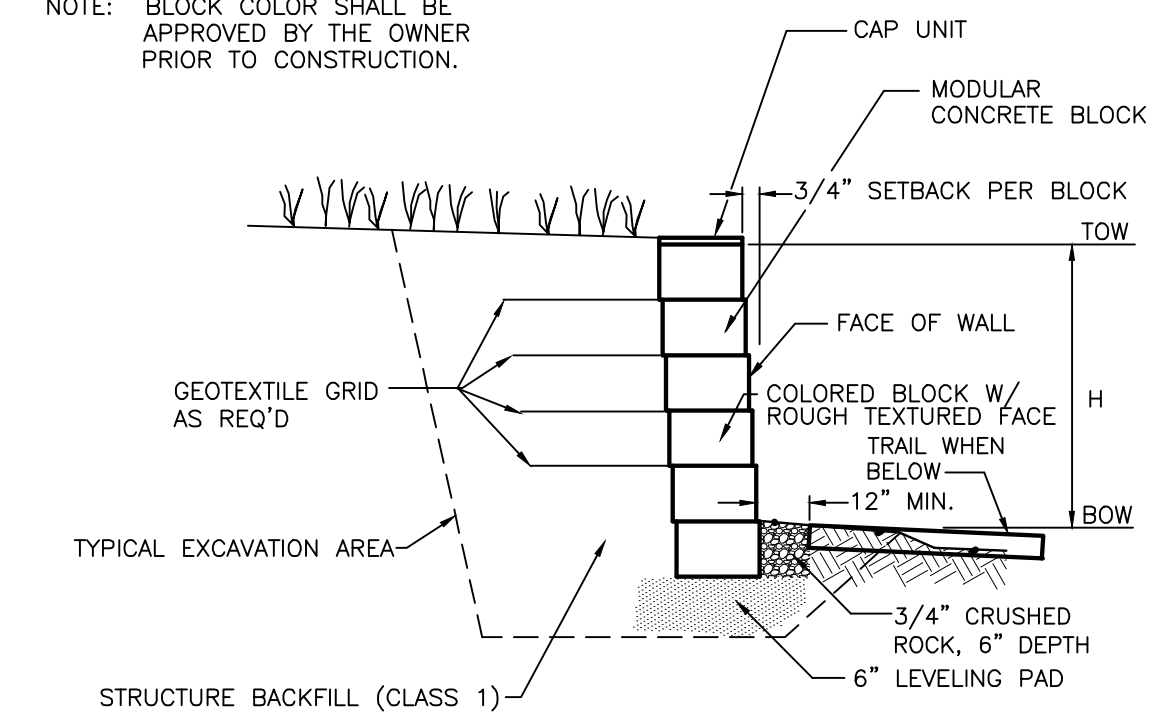

**2 CONCRETE BLOCK FACING MSE WALL CROSS SECTION  
NOT TO SCALE**

**WALL NOTES:**

- SHOP DRAWINGS DEPICTING THE DESIGN OF BLOCK WALL SHALL BE SUBMITTED TO ENGINEER PRIOR TO CONSTRUCTION PER THE PROJECT SPECIFICATIONS. DESIGN SHALL BE COMPLETED UNDER THE DIRECT SUPERVISION OF A PROPERLY REGISTERED PROFESSIONAL ENGINEER WITH THE STATE OF COLORADO. FINAL CONSTRUCTION DRAWINGS SHALL BEAR HIS/HER SEAL AND SIGNATURE.
- BUILDING PERMITS FOR THE INSTALLATION OF THE MSE WALL MAY BE REQUIRED THROUGH THE PIKES PEAK REGIONAL BUILDING DEPARTMENT.
- CONTRACTOR TO OBTAIN EPC-DPW ROAD CUT WORK PERMIT FOR WORK IN RIGHT-OF-WAY.
- CONTRACTOR TO SUPPLY TO EPC-DPW CONSTRUCTION TRAFFIC CONTROL PLAN FOR REVIEW AND APPROVAL PRIOR TO COMMENCING WITH ANY WORK WITHIN THE PETERSON ROAD RIGHT-OF-WAY.

| EROSION CONTROL LEGEND |                          | CONSTRUCTION PHASE       |
|------------------------|--------------------------|--------------------------|
| (CD)                   | CHECK DAM                | FINAL                    |
| (CW)                   | CONCRETE WASHOUT         | INITIAL, INTERIM & FINAL |
| (ECB)                  | EROSION CONTROL BLANKET  | FINAL                    |
| (IP)                   | INLET PROTECTION         | INITIAL, INTERIM & FINAL |
| (SF)                   | SILT FENCE               | INITIAL, INTERIM & FINAL |
| (SM)                   | SEEDING & MULCH          | FINAL                    |
| (SSA)                  | STABILIZED STAGING AREA  | INITIAL, INTERIM & FINAL |
| (VTC)                  | VEHICLE TRACKING CONTROL | INITIAL & INTERIM        |

SEE DETAILS SHEETS GEC 7 & 8

| GENERAL LEGEND |                                      |
|----------------|--------------------------------------|
| ---            | EXISTING PROPERTY LINE               |
| ---            | CONSTRUCTION / LIMITS OF DISTURBANCE |
| ---            | EXISTING MAJOR CONTOUR               |
| ---            | EXISTING MINOR CONTOUR               |
| ---            | PROPOSED MAJOR CONTOUR               |
| ---            | PROPOSED MINOR CONTOUR               |
| →              | DIRECTION OF FLOW                    |



For and on Behalf of  
Kiowa Engineering Corporation Date

**Kiowa**  
Engineering Corporation  
1604 South 21st Street  
Colorado Springs, Colorado 80904  
(719) 630-7342



Sheet Revisions

IFC

No Revisions:

Revised:

Void:

**ROCK ISLAND TRAIL  
GRADING AND EROSION CONTROL PLAN  
STANDARD NOTES & DETAILS**

Designer: TAC

Detailer: JDC/TEG


Date: 11/22/2024

Kiowa Proj. No. 16028

TAP M240-162

SubAcct No. 20391

Sheet Number G2


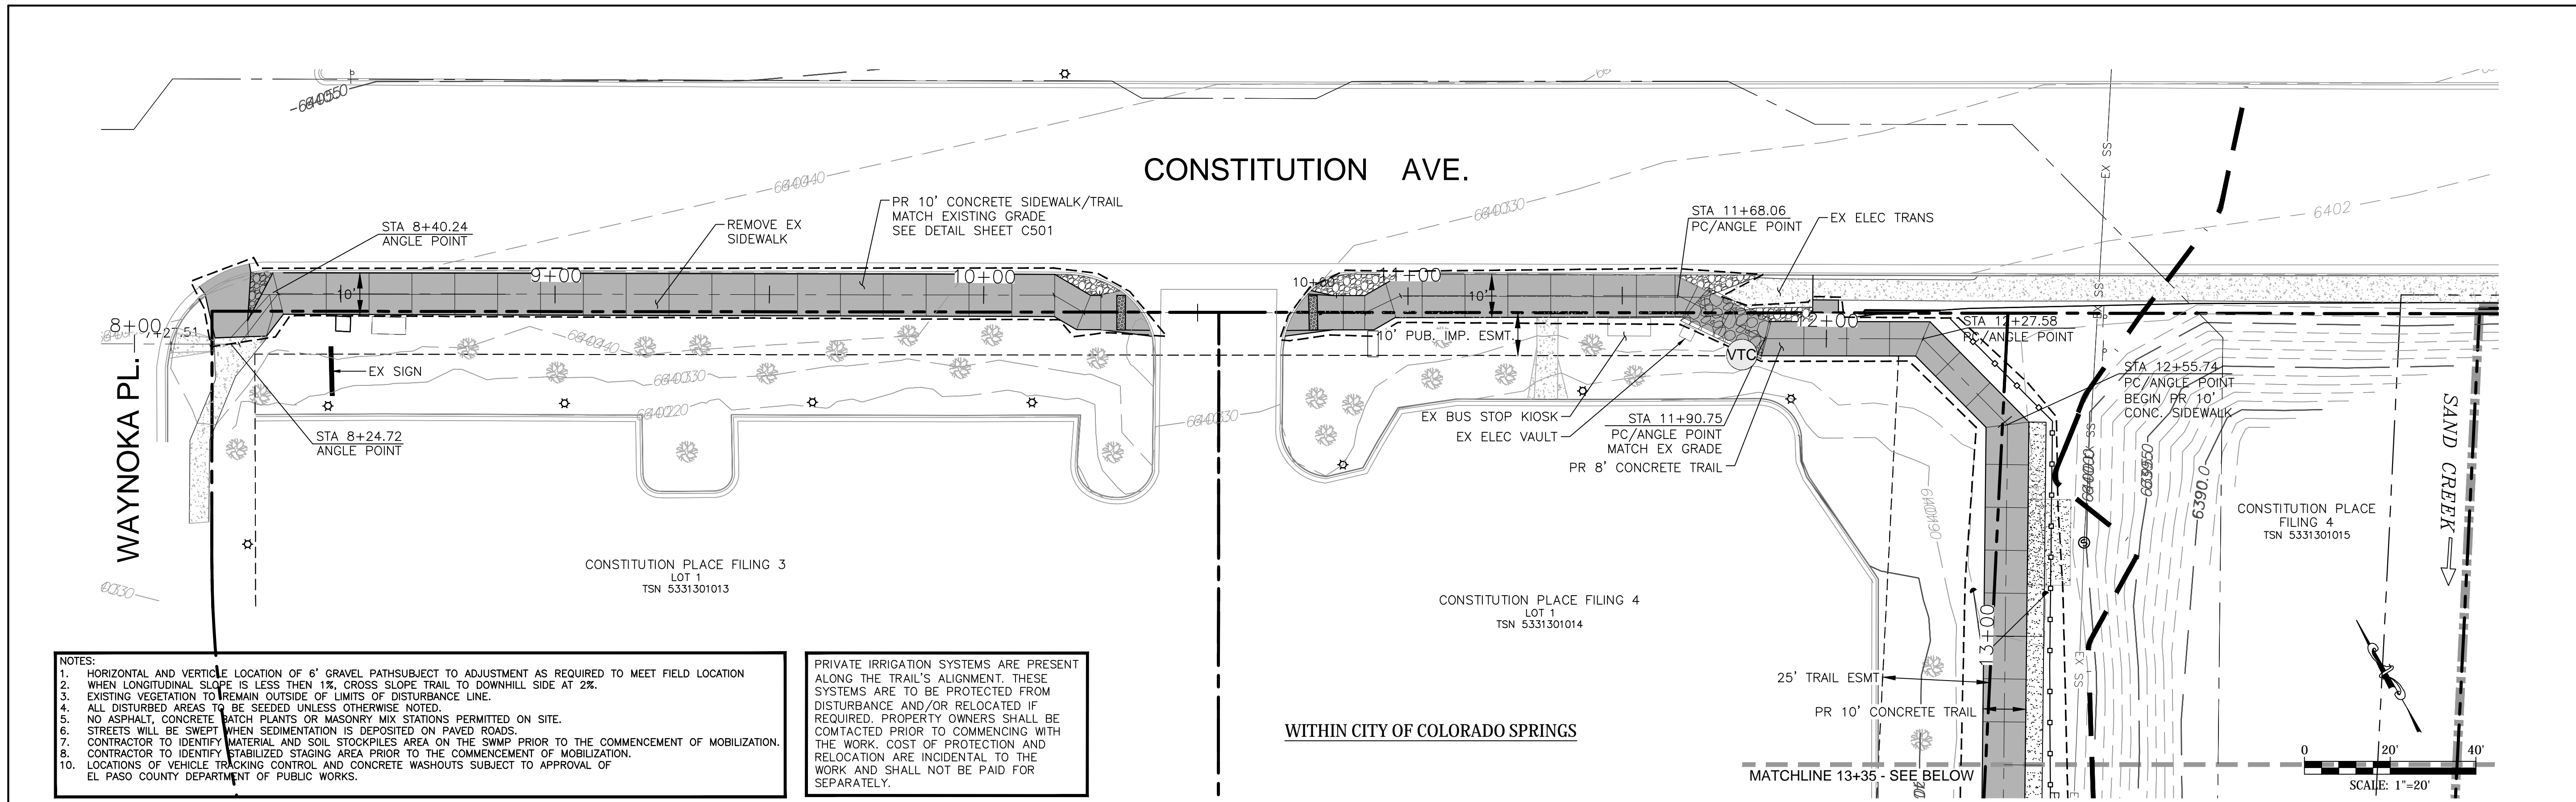


**NOTES:**

- HORIZONTAL AND VERTICAL LOCATION OF 6" GRAVEL PATHS SUBJECT TO ADJUSTMENT AS REQUIRED TO MEET FIELD LOCATION
- WHEN LONGITUDINAL SLOPE IS LESS THAN 1%, GROSS SLOPE TRAIL TO DOWNHILL SIDE AT 2%.
- EXISTING VEGETATION TO REMAIN OUTSIDE OF LIMITS OF DISTURBANCE LINE.
- ALL DISTURBED AREAS TO BE SEEDED UNLESS OTHERWISE NOTED.
- NO ASPHALT, CONCRETE BATCH PLANTS OR MASONRY MIX STATIONS PERMITTED ON SITE.
- STREETS WILL BE SWEEPED WHEN SEDIMENTATION IS DEPOSITED ON PAVED ROADS.
- CONTRACTOR TO IDENTIFY MATERIAL AND SOIL STOCKPILES AREA ON THE SWAMP PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
- CONTRACTOR TO IDENTIFY STABILIZED STAGING AREA PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
- LOCATIONS OF VEHICLE TRACKING CONTROL AND CONCRETE WASHOUTS SUBJECT TO APPROVAL OF EL PASO COUNTY DEPARTMENT OF PUBLIC WORKS.

PRIVATE IRRIGATION SYSTEMS ARE PRESENT ALONG THE TRAIL'S ALIGNMENT. THESE SYSTEMS ARE TO BE PROTECTED FROM DISTURBANCE AND/OR RELOCATED IF REQUIRED. PROPERTY OWNERS SHALL BE CONTACTED PRIOR TO COMMENCING WITH THE WORK. COST OF PROTECTION AND RELOCATION ARE INCIDENTAL TO THE WORK AND SHALL NOT BE PAID FOR SEPARATELY.

WITHIN CITY OF COLORADO SPRINGS

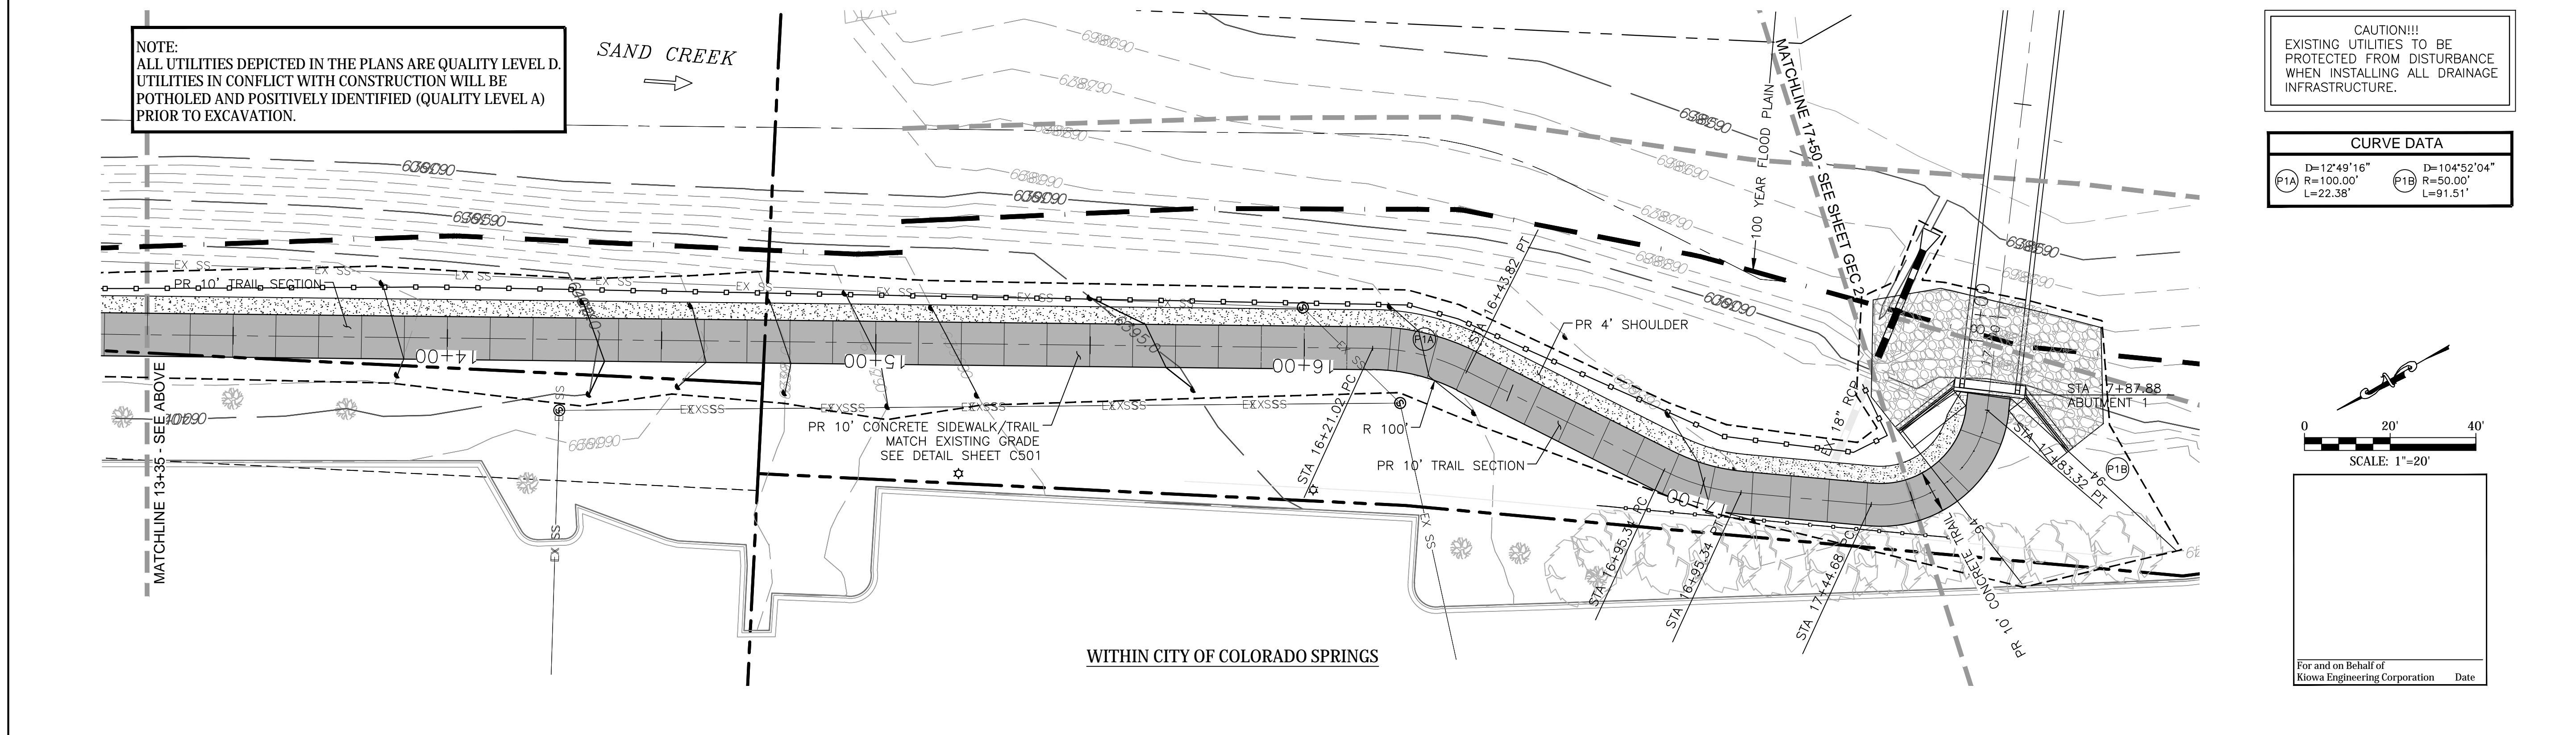


**NOTE:**  
ALL UTILITIES DEPICTED IN THE PLANS ARE QUALITY LEVEL D. UTILITIES IN CONFLICT WITH CONSTRUCTION WILL BE POTHOLED AND POSITIVELY IDENTIFIED (QUALITY LEVEL A) PRIOR TO EXCAVATION.

**CAUTION!!!**  
EXISTING UTILITIES TO BE PROTECTED FROM DISTURBANCE WHEN INSTALLING ALL DRAINAGE INFRASTRUCTURE.

**CURVE DATA**

|     |             |           |          |     |              |          |          |
|-----|-------------|-----------|----------|-----|--------------|----------|----------|
| P1A | D=12°49'16" | R=100.00' | L=22.38' | P1B | D=104°52'04" | R=50.00' | L=91.51' |
|-----|-------------|-----------|----------|-----|--------------|----------|----------|



For and on Behalf of  
Kiowa Engineering Corporation Date


|  |  |                 |  |               |   |                       |
|--|--|-----------------|--|---------------|---|-----------------------|
|  |  | Sheet Revisions |  | IFC           | <b>ROCK ISLAND TRAIL</b><br>GRADING AND EROSION CONTROL PLAN<br>STA 8+00 TO 17+50 | Kiowa Proj. No. 16028 |
|  |  |                 |  | No Revisions: |   |                       |
| For and on Behalf of<br>Kiowa Engineering Corporation Date | 1604 South 21st Street<br>Colorado Springs, Colorado 80904<br>(719) 630-7342 |                 |  | Revised:      | Designer: TAC   | SubAcct No. 20391     |
|  |  |                 |  | Void:         | Detailer: JDC/TEG   | Sheet Number GEC 1    |
|  |  |                 |  |               | Date: 11/22/2024  |                       |

**NOTE:**  
ALL UTILITIES DEPICTED IN THE PLANS ARE QUALITY LEVEL D. UTILITIES IN CONFLICT WITH CONSTRUCTION WILL BE POTHOLED AND POSITIVELY IDENTIFIED (QUALITY LEVEL A) PRIOR TO EXCAVATION.


**CAUTION!!!**  
EXISTING UTILITIES TO BE PROTECTED FROM DISTURBANCE WHEN INSTALLING ALL DRAINAGE INFRASTRUCTURE.

**CURVE DATA**  
D=104°52'04"  
R=50.00'  
L=91.51'

FOR LAYOUT OF ROCK ISLAND BRIDGE & DRAINAGEWAY IMPROVEMENTS, SEE SHEET C205

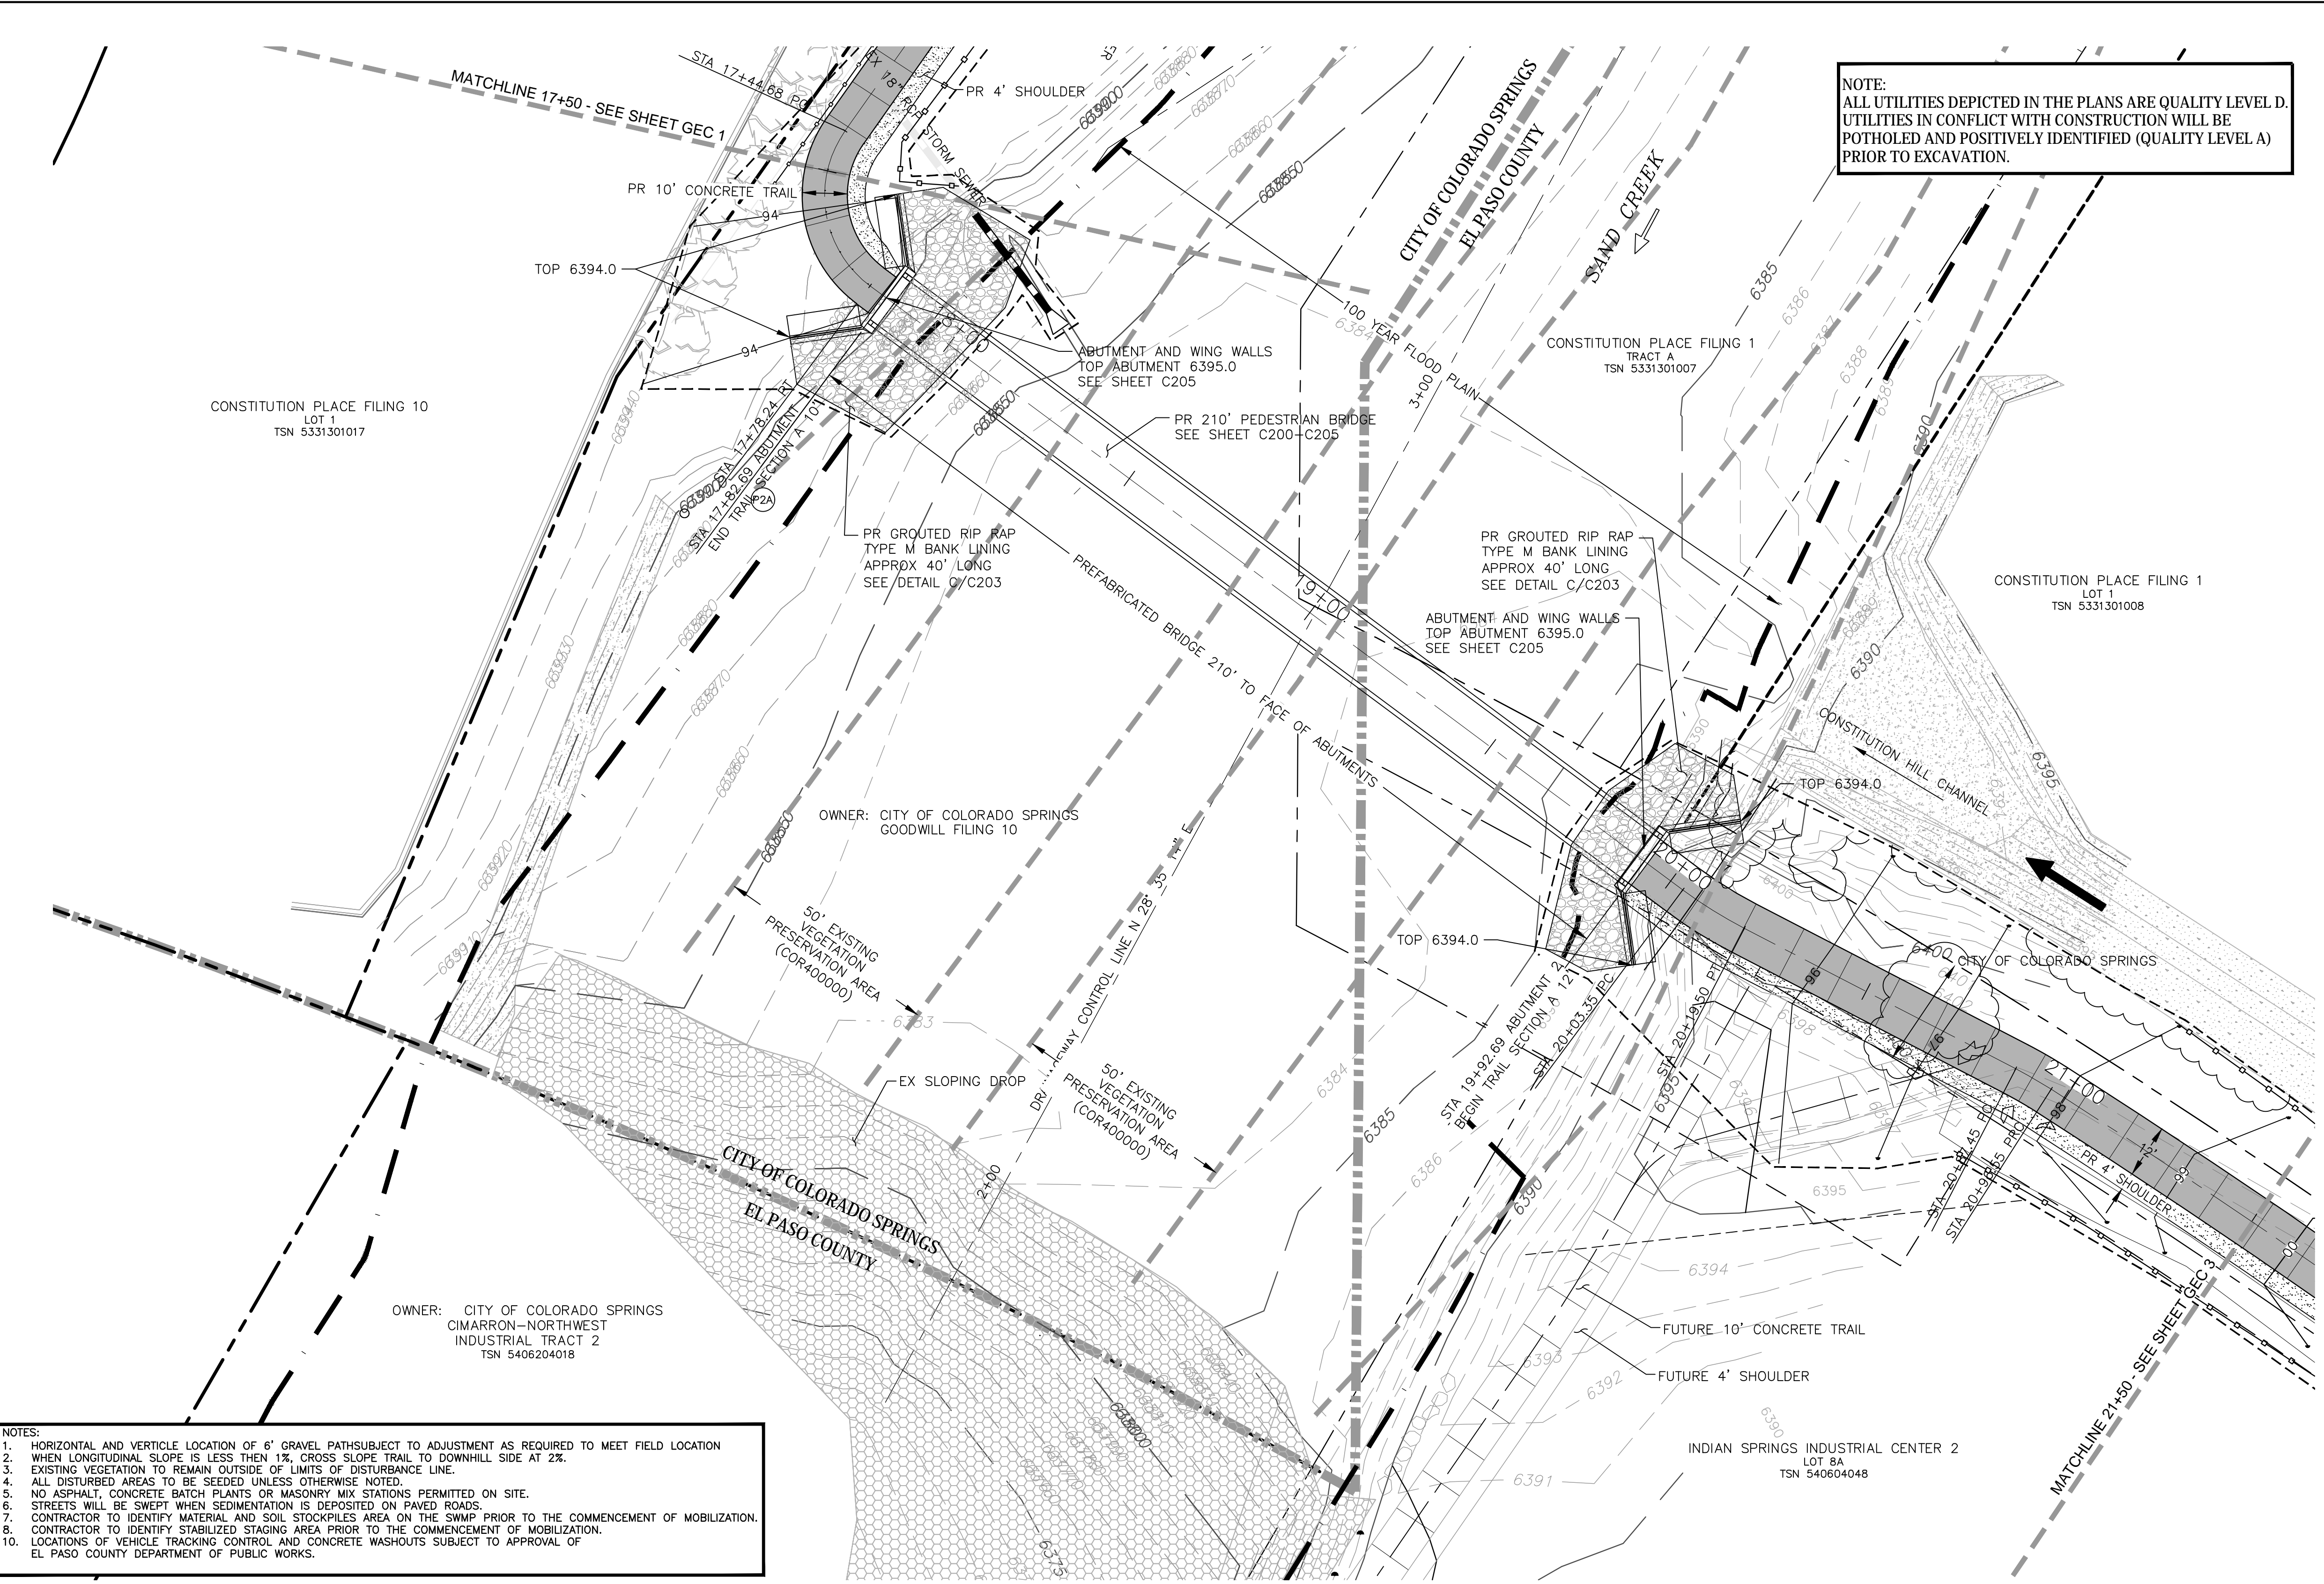


- NOTES:**
- HORIZONTAL AND VERTICLE LOCATION OF 6" GRAVEL PATHS SUBJECT TO ADJUSTMENT AS REQUIRED TO MEET FIELD LOCATION
  - WHEN LONGITUDINAL SLOPE IS LESS THEN 1%, CROSS SLOPE TRAIL TO DOWNHILL SIDE AT 2%.
  - EXISTING VEGETATION TO REMAIN OUTSIDE OF LIMITS OF DISTURBANCE LINE.
  - ALL DISTURBED AREAS TO BE SEEDED UNLESS OTHERWISE NOTED.
  - NO ASPHALT, CONCRETE BATCH PLANTS OR MASONRY MIX STATIONS PERMITTED ON SITE.
  - STREETS WILL BE SWEEPED WHEN SEDIMENTATION IS DEPOSITED ON PAVED ROADS.
  - CONTRACTOR TO IDENTIFY MATERIAL AND SOIL STOCKPILES AREA ON THE SWMP PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
  - CONTRACTOR TO IDENTIFY STABILIZED STAGING AREA PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
  - LOCATIONS OF VEHICLE TRACKING CONTROL AND CONCRETE WASHOUTS SUBJECT TO APPROVAL OF EL PASO COUNTY DEPARTMENT OF PUBLIC WORKS.

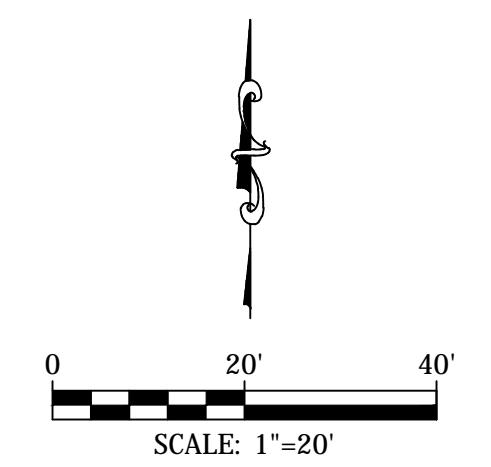

For and on Behalf of  
Kiowa Engineering Corporation Date



**Kiowa**  
Engineering Corporation  
1604 South 21st Street  
Colorado Springs, Colorado 80904  
(719) 630-7342



Sheet Revisions

IFC

**ROCK ISLAND TRAIL**  
GRADING AND EROSION CONTROL PLAN  
STA 17+50 TO 21+50



Kiowa Proj. No. 16028  
TAP M240-162  
SubAcct No. 20391  
Sheet Number GEC 2

Designer: TAC  
Detailer: JDC/TEG  
Date: 11/22/2024



No Revisions:  
Revised:  
Void:

For and on Behalf of  
Kiowa Engineering Corporation Date





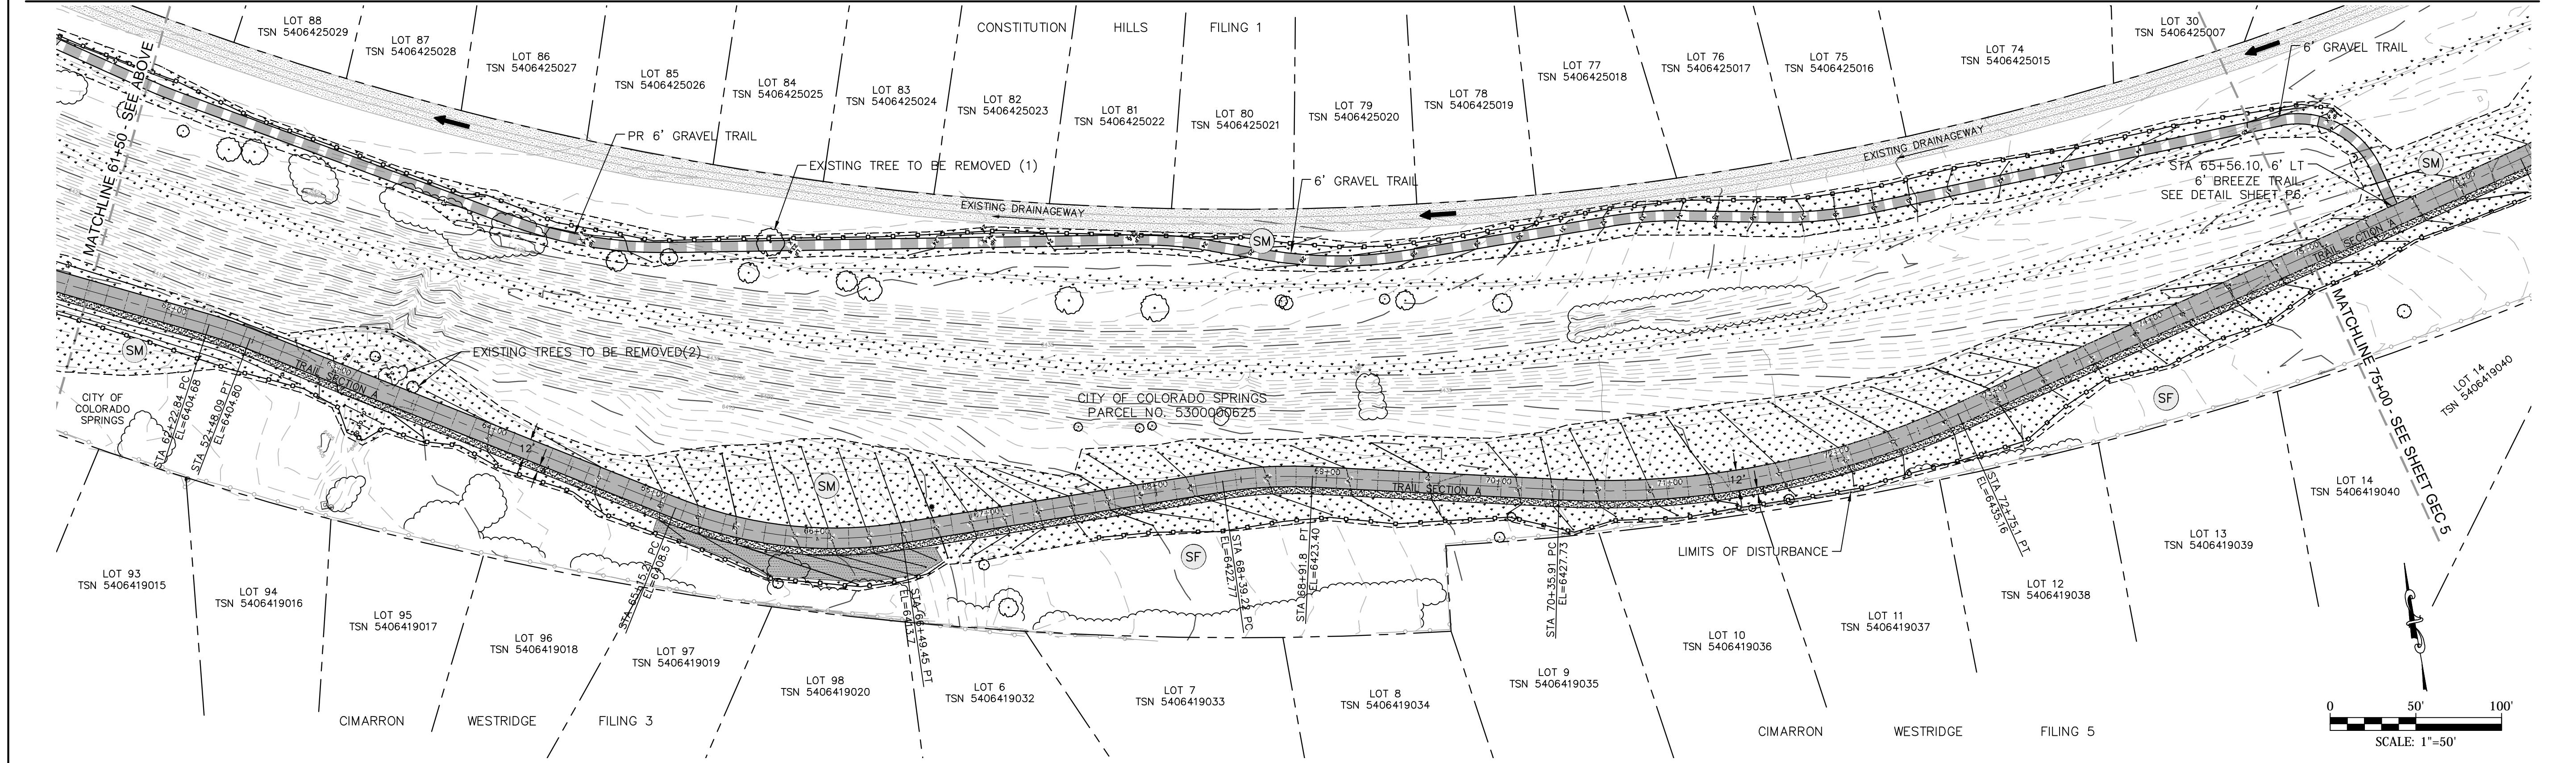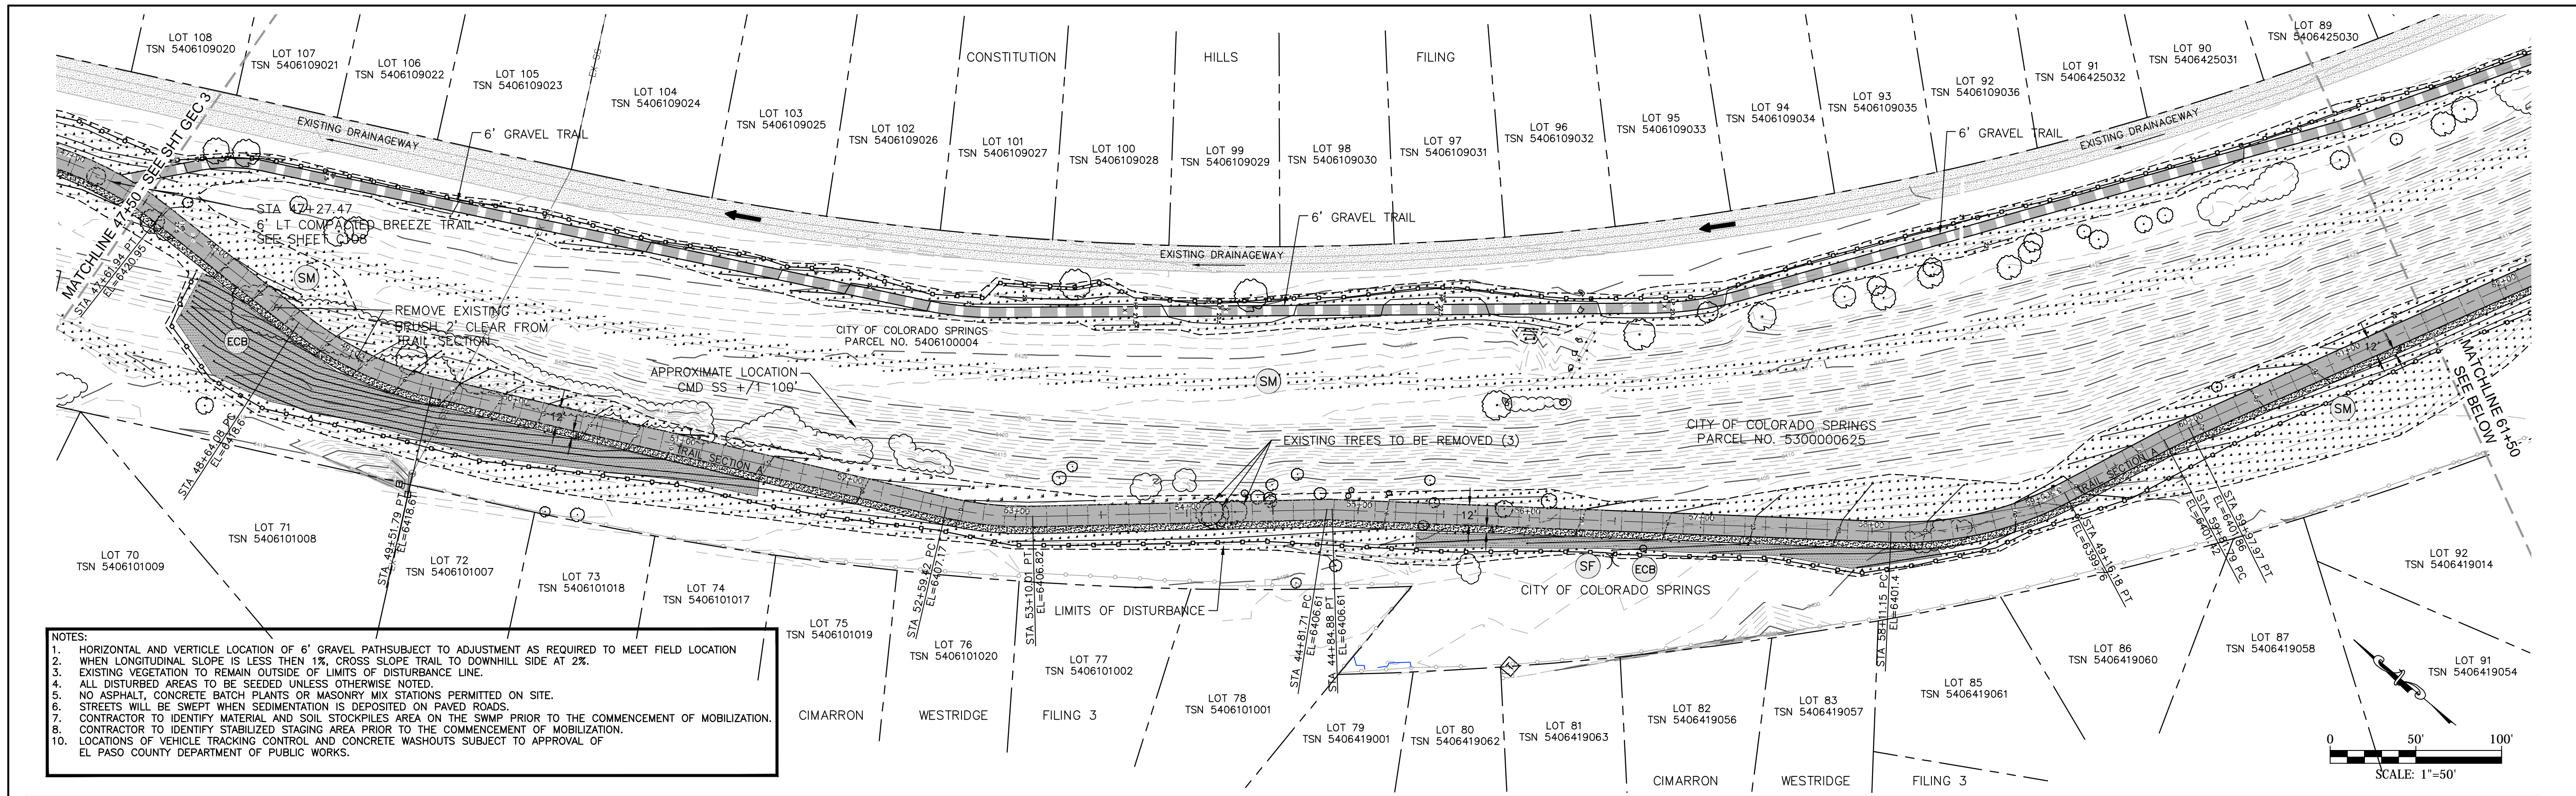

|  |  |  |  |  |                                    |  |  |  |                       |
|--|--|--|--|--|------------------------------------|--|--|--|-----------------------|
|  |  | 1604 South 21st Street<br>Colorado Springs, Colorado 80904<br>(719) 630-7342 | Sheet Revisions  |  | IFC                                |  | <b>ROCK ISLAND TRAIL</b><br>GRADING AND EROSION CONTROL PLAN<br>STA 47+50 TO 75+00 |  | Kiowa Proj. No. 16028 |
|  |  |  | For and on Behalf of<br>Kiowa Engineering Corporation Date | <input type="checkbox"/><br><input type="checkbox"/><br><input type="checkbox"/> | No Revisions:<br>Revised:<br>Void: | Designer: TAC<br>Detailer: JDC/TEG<br>Date: 11/22/2024 | TAP M240-162<br>SubAcct No. 20391<br>Sheet Number GEC 4                            |  |                       |

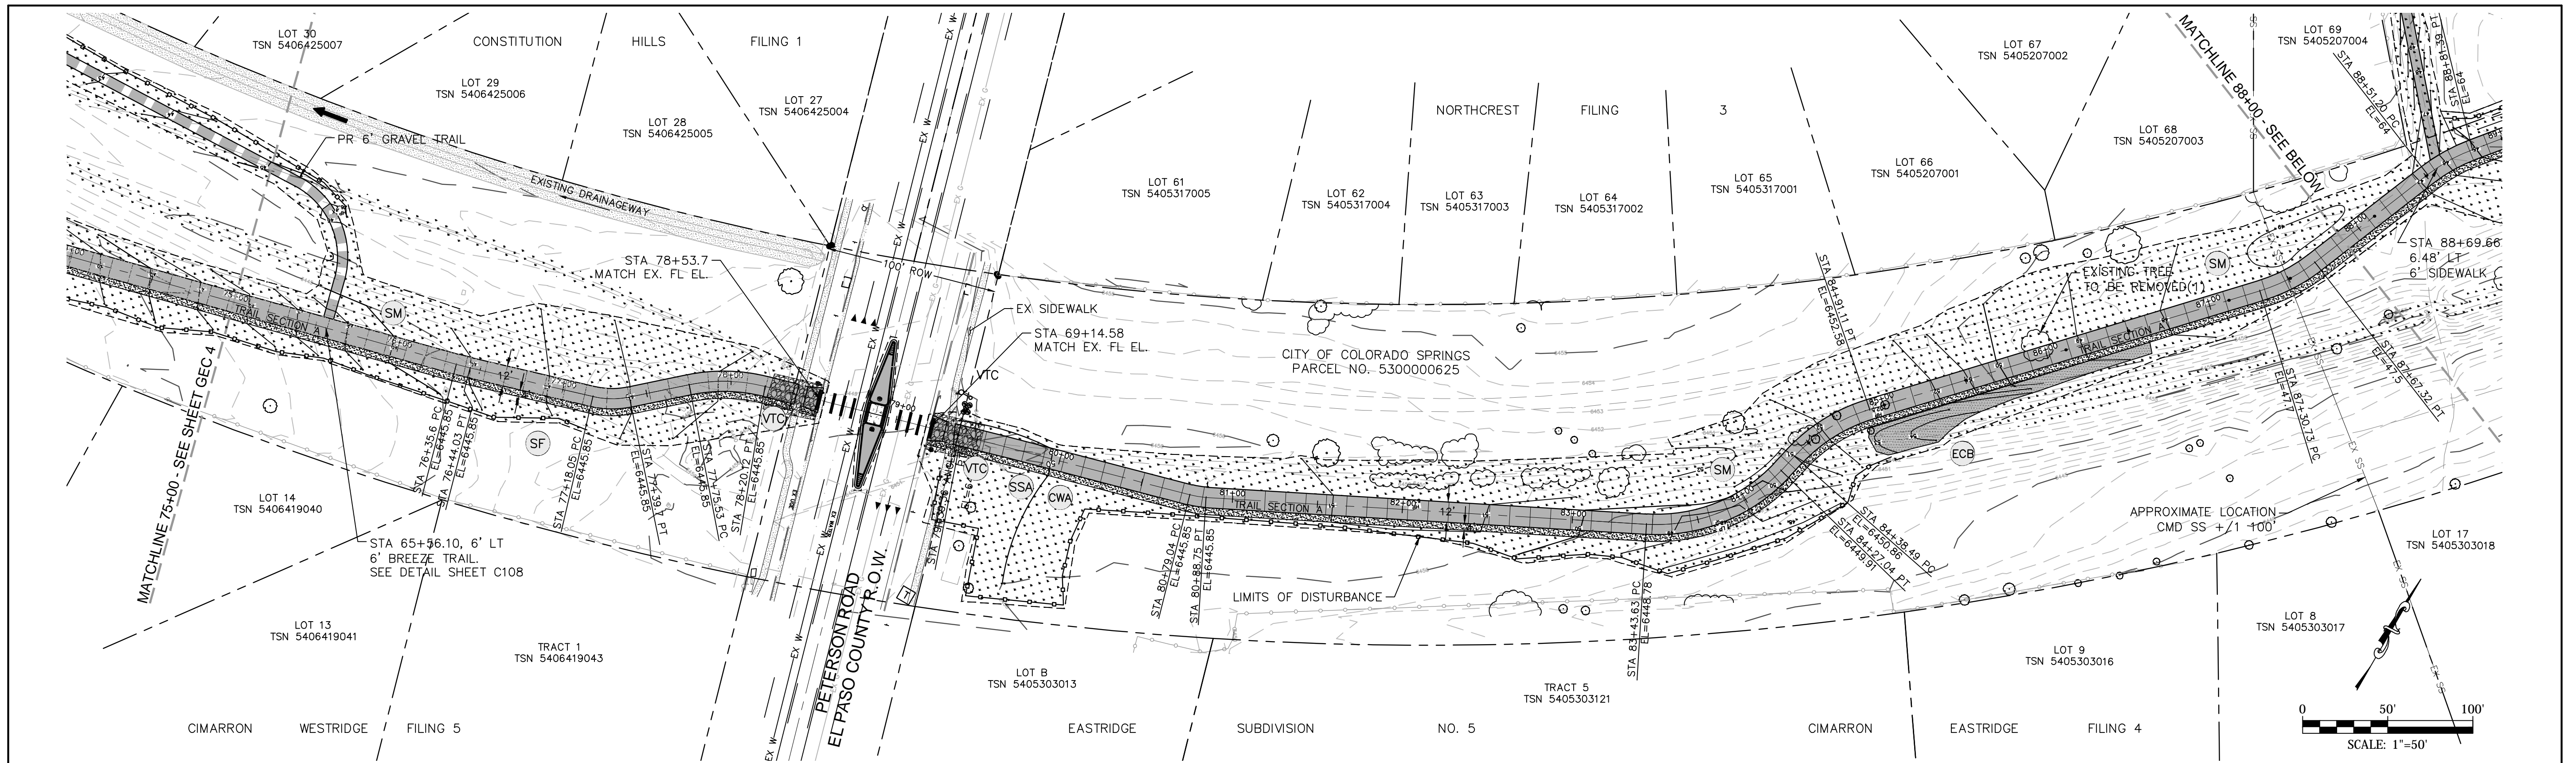

- NOTES:**
- HORIZONTAL AND VERTICAL LOCATION OF 6' GRAVEL PATHS SUBJECT TO ADJUSTMENT AS REQUIRED TO MEET FIELD LOCATION
  - WHEN LONGITUDINAL SLOPE IS LESS THAN 1%, CROSS SLOPE TRAIL TO DOWNHILL SIDE AT 2%.
  - EXISTING VEGETATION TO REMAIN OUTSIDE OF LIMITS OF DISTURBANCE LINE.
  - ALL DISTURBED AREAS TO BE SEEDED UNLESS OTHERWISE NOTED.
  - NO ASPHALT, CONCRETE BATCH PLANTS OR MASONRY MIX STATIONS PERMITTED ON SITE.
  - STREETS WILL BE SWEEPED WHEN SEDIMENTATION IS DEPOSITED ON PAVED ROADS.
  - CONTRACTOR TO IDENTIFY MATERIAL AND SOIL STOCKPILES AREA ON THE SWMP PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
  - CONTRACTOR TO IDENTIFY STABILIZED STAGING AREA PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
  - LOCATIONS OF VEHICLE TRACKING CONTROL AND CONCRETE WASHOUTS SUBJECT TO APPROVAL OF EL PASO COUNTY DEPARTMENT OF PUBLIC WORKS.

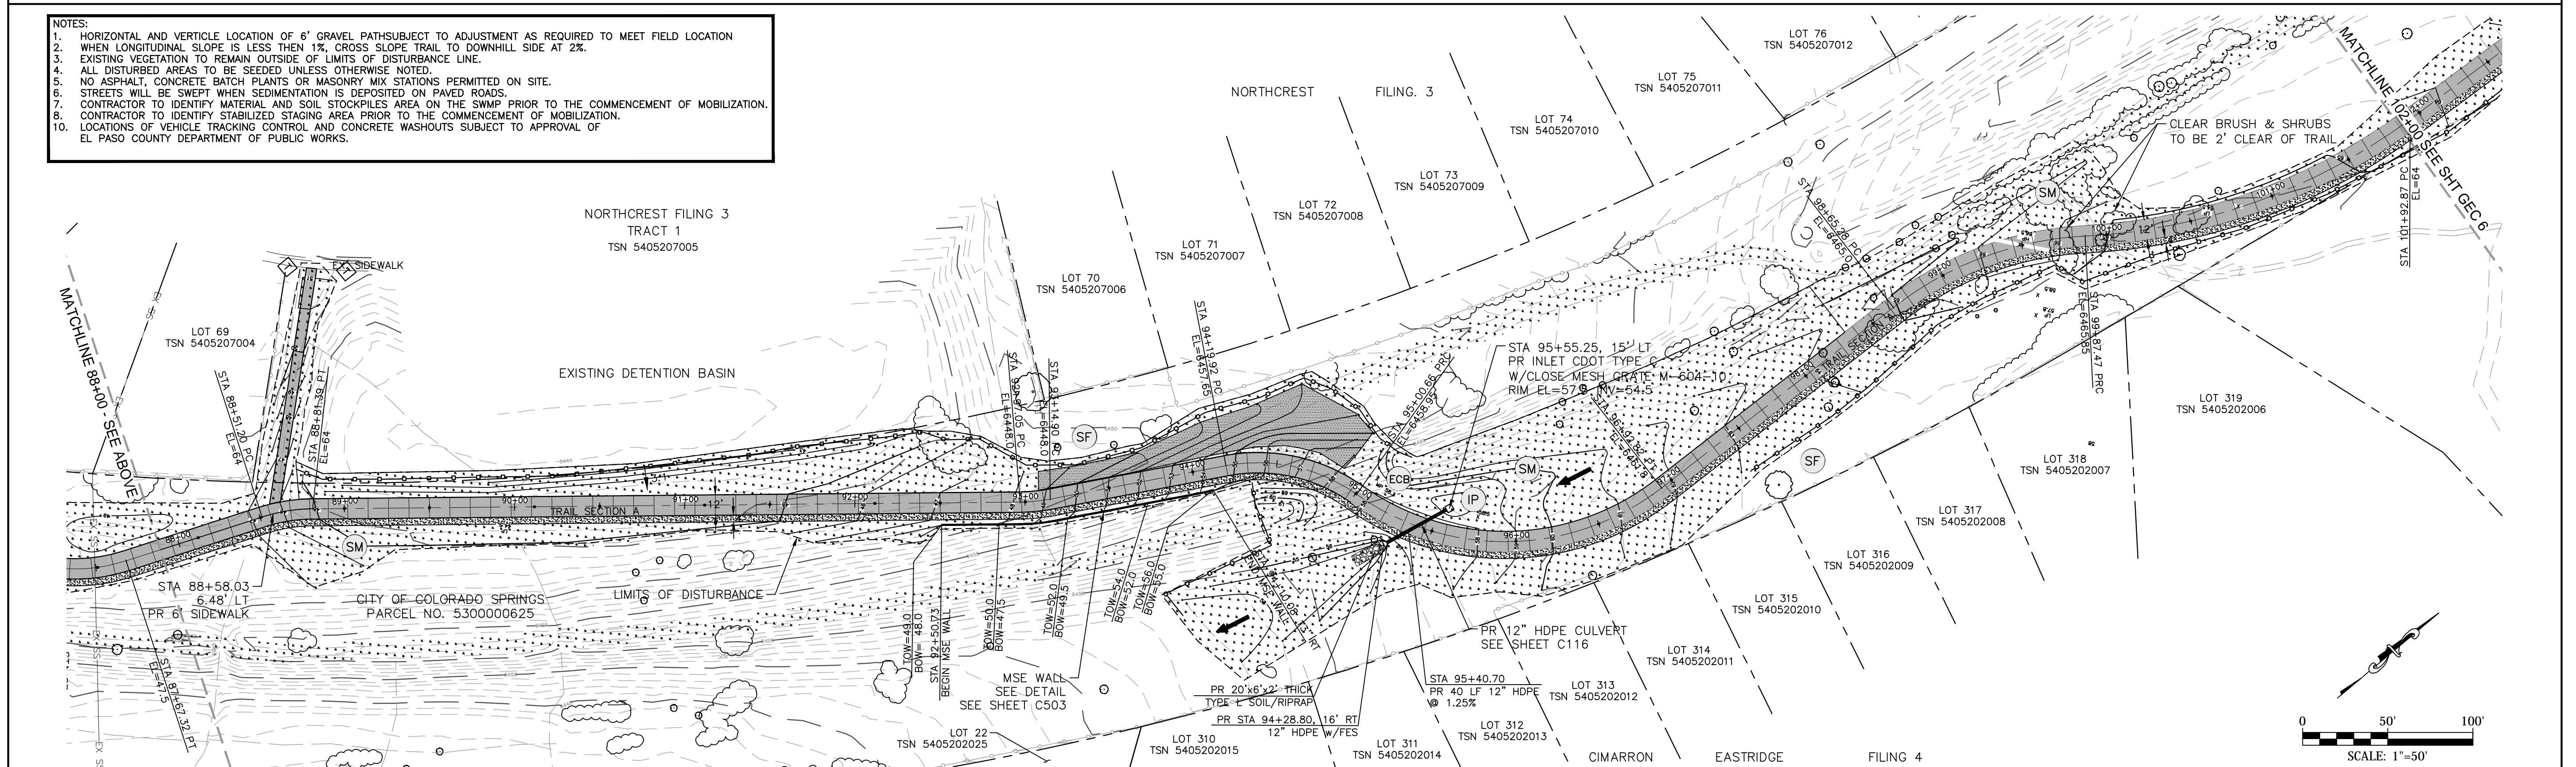

**Kiowa**  
Engineering Corporation  
1604 South 21st Street  
Colorado Springs, Colorado 80904  
(719) 630-7342


For and on Behalf of  
Kiowa Engineering Corporation Date

| Sheet Revisions | IFC           |
|-----------------|---------------|
|                 | No Revisions: |
|                 | Revised:      |
|                 | Void:         |

| ROCK ISLAND TRAIL<br>GRADING AND EROSION CONTROL PLAN<br>STA 75+00 TO 102+00 |            |
|--|------------|
| Designer:  | TAC        |
| Detailer:  | JDC/TEG    |
| Date:  | 11/22/2024 |

|                       |
|-----------------------|
| Kiowa Proj. No. 16028 |
| TAP M240-162          |
| SubAcct No. 20391     |
| Sheet Number GEC 5    |




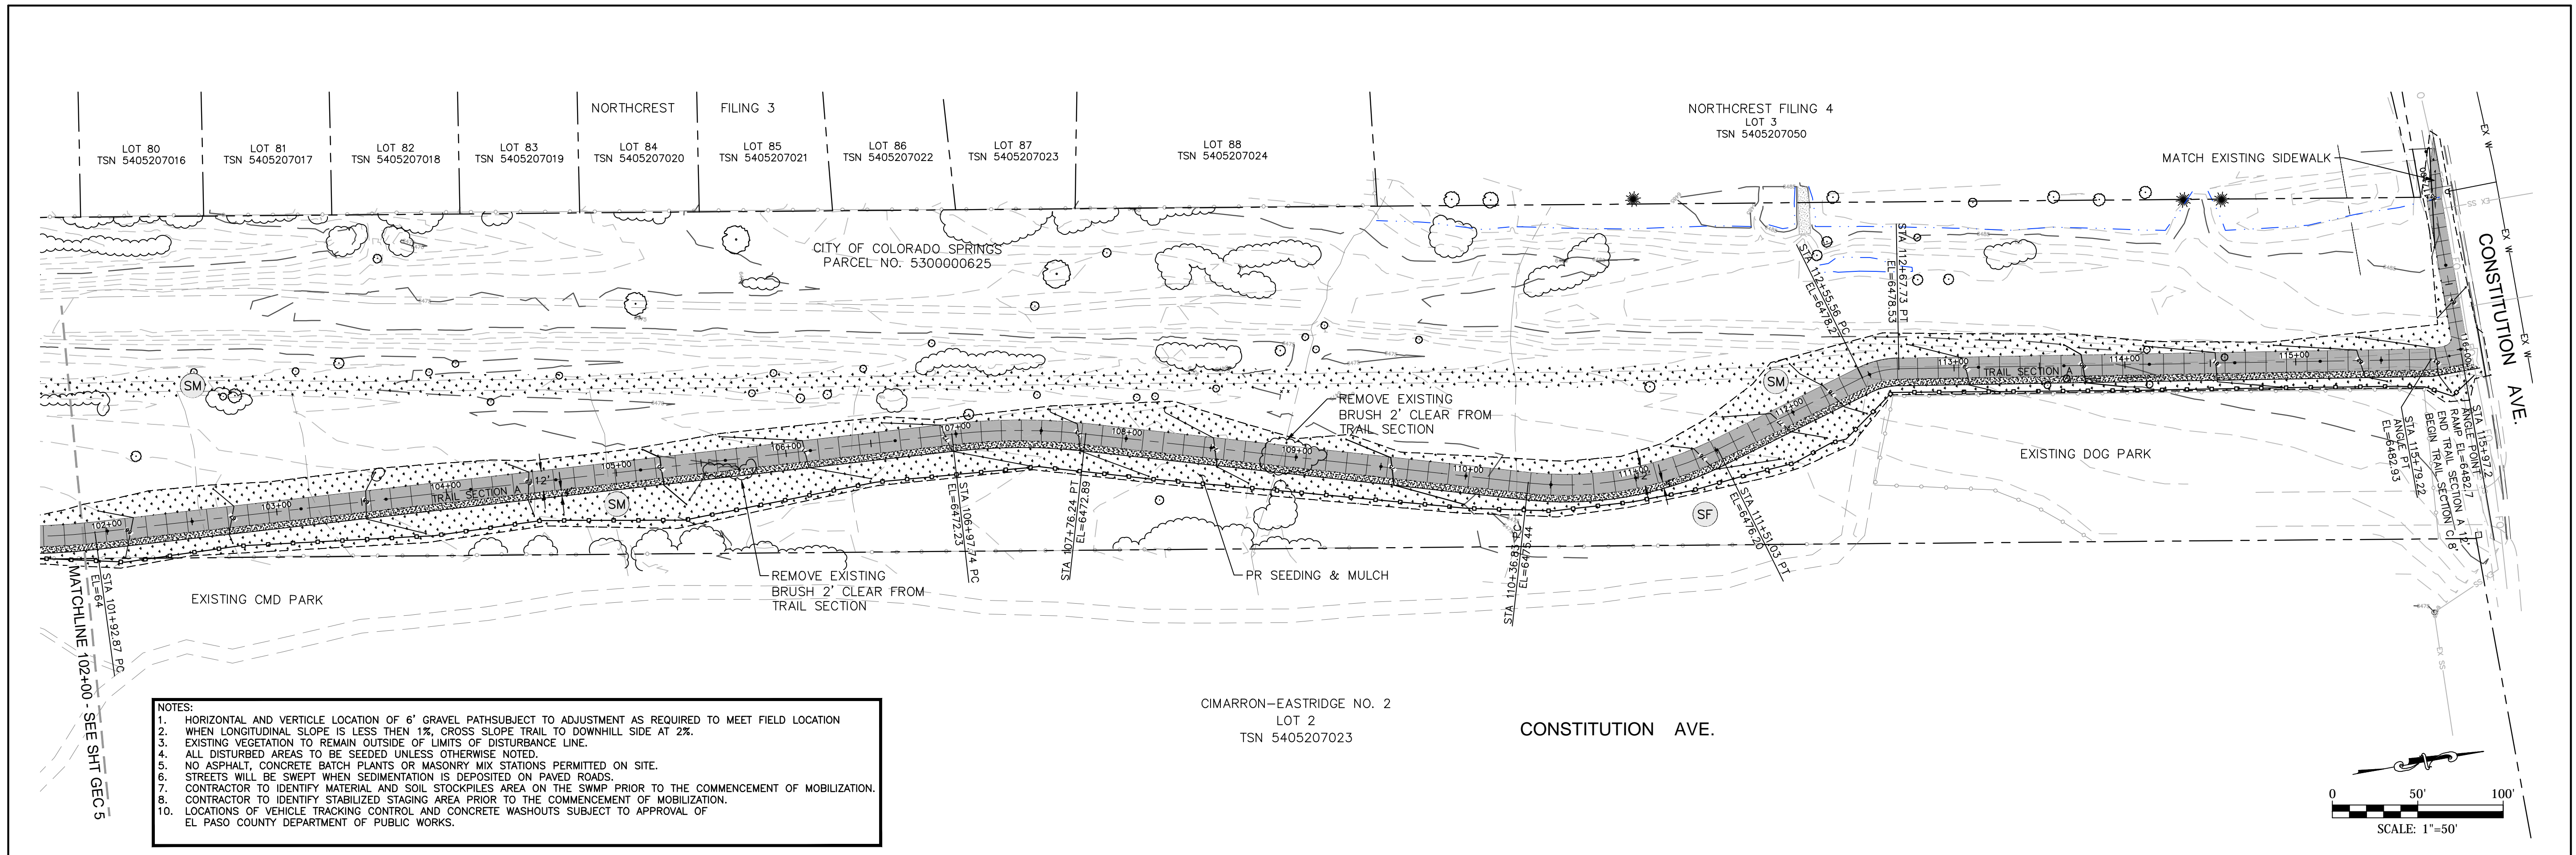




- NOTES:
1. HORIZONTAL AND VERTICLE LOCATION OF 6' GRAVEL PATHS SUBJECT TO ADJUSTMENT AS REQUIRED TO MEET FIELD LOCATION
  2. WHEN LONGITUDINAL SLOPE IS LESS THEN 1%, CROSS SLOPE TRAIL TO DOWNHILL SIDE AT 2%.
  3. EXISTING VEGETATION TO REMAIN OUTSIDE OF LIMITS OF DISTURBANCE LINE.
  4. ALL DISTURBED AREAS TO BE SEEDED UNLESS OTHERWISE NOTED.
  5. NO ASPHALT, CONCRETE BATCH PLANTS OR MASONRY MIX STATIONS PERMITTED ON SITE.
  6. STREETS WILL BE SWEEPED WHEN SEDIMENTATION IS DEPOSITED ON PAVED ROADS.
  7. CONTRACTOR TO IDENTIFY MATERIAL AND SOIL STOCKPILES AREA ON THE SWMP PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
  8. CONTRACTOR TO IDENTIFY STABILIZED STAGING AREA PRIOR TO THE COMMENCEMENT OF MOBILIZATION.
  9. LOCATIONS OF VEHICLE TRACKING CONTROL AND CONCRETE WASHOUTS SUBJECT TO APPROVAL OF EL PASO COUNTY DEPARTMENT OF PUBLIC WORKS.
  - 10.

CIMARRON-EASTRIDGE NO. 2  
LOT 2  
TSN 5405207023

CONSTITUTION AVE.



|   |   |   |                 |               |   |                    |                       |
|---|---|---|-----------------|---------------|---|--------------------|-----------------------|
|  |  |  | Sheet Revisions | IFC           | <b>ROCK ISLAND TRAIL</b><br>GRADING AND EROSION CONTROL PLAN<br><b>STA 102+00 TO 117+50</b> |                    | Kiowa Proj. No. 16028 |
|   |   |   |                 | No Revisions: | Designer: TAC   | SubAcct No. 20391  |                       |
|   |   |   |                 | Revised:      | Detailer: JDC/TEG   | Sheet Number GEC 6 |                       |
|   |   |   |                 | Void:         | Date: 11/22/2024  |                    |                       |



**SEEDING & MULCHING**

ALL SOIL TESTING, SOILS AMENDMENT AND FERTILIZER DOCUMENTATION, AND SEED LOAD AND BAG TICKETS MUST BE ADDED TO THE CSWMP.

**SOIL PREPARATION**

1. IN AREAS TO BE SEEDED, THE UPPER 6 INCHES OF THE SOIL MUST NOT BE HEAVILY COMPACTED, AND SHOULD BE IN FRABLE CONDITION. LESS THAN 85% STANDARD PROCTOR DENSITY IS ACCEPTABLE. AREAS OF COMPACTION OR GENERAL CONSTRUCTION ACTIVITY MUST BE SCARIFIED TO A DEPTH OF 6 TO 12 INCHES PRIOR TO SPREADING TOPSOIL TO BREAK UP COMPACTED LAYERS AND PROVIDE A BLENDING ZONE BETWEEN DIFFERENT SOIL LAYERS.
2. AREAS TO BE PLANTED SHALL HAVE AT LEAST 4 INCHES OF TOPSOIL SUITABLE TO SUPPORT PLANT GROWTH.
3. THE CITY RECOMMENDS THAT EXISTING AND/OR IMPORTED TOPSOIL BE TESTED TO IDENTIFY SOIL DEFICIENCIES AND ANY SOIL AMENDMENTS NECESSARY TO ADDRESS THESE DEFICIENCIES. SOIL AMENDMENTS AND/OR FERTILIZERS SHOULD BE ADDED TO CORRECT TOPSOIL DEFICIENCIES BASED ON SOIL TESTING RESULTS.
4. TOPSOIL SHALL BE PROTECTED DURING THE CONSTRUCTION PERIOD TO RETAIN ITS STRUCTURE AVOID COMPACTION, AND TO PREVENT EROSION AND CONTAMINATION. STRIPPED TOPSOIL MUST BE STORED IN AN AREA AWAY FROM MACHINERY AND CONSTRUCTION OPERATIONS, AND CARE MUST BE TAKEN TO PROTECT THE TOPSOIL AS A VALUABLE COMMODITY. TOPSOIL MUST NOT BE STRIPPED DURING UNDESIRABLE WORKING CONDITIONS (E.G. DURING WET WEATHER OR WHEN SOILS ARE SATURATED). TOPSOIL SHALL NOT BE STORED IN SWALES OR IN AREAS WITH POOR DRAINAGE.

**SEEDING**


1. ALLOWABLE SEED MIXES ARE INCLUDED IN THE CITY OF COLORADO SPRINGS STORMWATER CONSTRUCTION MANUAL. ALTERNATIVE SEED MIXES ARE ACCEPTABLE IF INCLUDED IN AN APPROVED LANDSCAPING PLAN.
2. SEED SHOULD BE DRILL-SEEDED WHENEVER POSSIBLE.
3. BROADCAST SEEDING OR HYDRO-SEEDED WITH TACKIFIER MAY BE SUBSTITUTED ON SLOPES STEEPER THAN 3:1 OR ON OTHER AREAS NOT PRACTICAL TO DRILL SEED.
  - SEEDING RATES MUST BE DOUBLED FOR BROADCAST SEEDING OR INCREASED BY 50% IF USING A BRILLIANT DRILL OR HYDRO-SEEDED.
  - BROADCAST SEEDING MUST BE LIGHTLY HAND-RAKED INTO THE SOIL.

**MULCHING**


1. MULCHING SHOULD BE COMPLETED AS SOON AS PRACTICABLE AFTER SEEDING, HOWEVER PLANTED AREAS MUST BE MULCHED NO LATER THAN 14 DAYS AFTER PLANTING.
2. MULCHING REQUIREMENTS INCLUDE:
  - HAY OR STRAW MULCH
    - ONLY CERTIFIED WEED-FREE AND CERTIFIED SEED-FREE MULCH MAY BE USED. MULCH MUST BE APPLIED AT 2 TONS/ACRE AND ADEQUATELY SECURED BY CRIMPING AND/OR TACKIFIER.
    - CRIMPING MUST NOT BE USED ON SLOPES GREATER THAN 3:1 AND MULCH FIBERS MUST BE TUCKED INTO THE SOIL TO A DEPTH OF 3 TO 4 INCHES.
    - TACKIFIER MUST BE USED IN PLACE OF CRIMPING ON SLOPES STEEPER THAN 3:1.
  - HYDRAULIC MULCHING
    - HYDRAULIC MULCHING IS AN OPTION ON STEEP SLOPES OR WHERE ACCESS IS LIMITED.
    - IF HYDRO-SEEDED IS USED, MULCHING MUST BE APPLIED AS A SEPARATE, SECOND OPERATION.
    - WOOD CELLULOSE FIBERS MIXED WITH WATER MUST BE APPLIED AT A RATE OF 2,000 TO 2,500 POUNDS/ACRE, AND TACKIFIER MUST BE APPLIED AT A RATE OF 100 POUNDS/ACRE.
  - EROSION CONTROL BLANKET
    - EROSION CONTROL BLANKET MAY BE USED IN PLACE OF TRADITIONAL MULCHING METHODS.



|                              |                     |
|------------------------------|---------------------|
| STORMWATER ENTERPRISE        | SEEDING & MULCHING  |
| APPROVED: <i>[Signature]</i> |                     |
| ISSUED: 10/7/19              | REVISION: 8/19/2020 |
|                              | DRAWING NO. 900-04  |

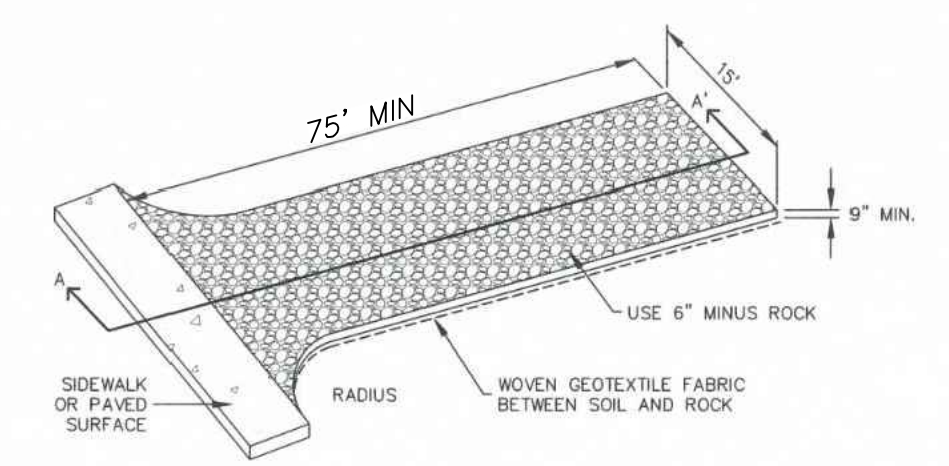

**AGGREGATE VEHICLE TRACKING CONTROL**

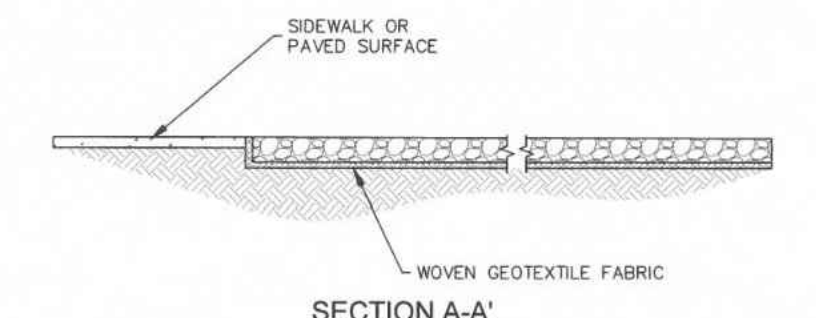

**SECTION A-A'**

**INSTALLATION NOTES**

1. A STABILIZED CONSTRUCTION ENTRANCE/EXIT SHOULD BE LOCATED AT ALL POINTS WHERE VEHICLES EXIT THE CONSTRUCTION SITE TO ADJACENT ROADWAY.
2. STABILIZED CONSTRUCTION ENTRANCE/EXITS SHALL BE INSTALLED PRIOR TO ANY LAND DISTURBING ACTIVITIES.
3. RADIUS MUST BE ADEQUATE FOR INTENDED CONSTRUCTION VEHICLE TURNING.
4. ROCK SHOULD CONSIST OF 6" MINUS ROCK.
5. INSTALL CONSTRUCTION FENCE ON BOTH SIDES OF VEHICLE TRACKING CONTROL PAD WHEN NEEDED OR REQUIRED BY INSPECTOR.

**MAINTENANCE NOTES**

1. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN CONTROL MEASURES IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.
2. SEDIMENT TRACKED ONTO THE ADJACENT ROAD SHALL BE REMOVED DAILY, BY SWEEPING OR SHOVELING, AND NEVER WASHED DOWN STORM DRAINS.
3. ROUGHEN, REPLACE AND/OR ADD ROCK AS NEEDED TO MAINTAIN CONSISTENT DEPTH AND TO PREVENT SEDIMENT TRACKING ONTO ADJACENT STREET.
4. PERMANENTLY STABILIZE AREA AFTER VEHICLE TRACKING CONTROL IS REMOVED.




|                              |                          |
|------------------------------|--------------------------|
| STORMWATER ENTERPRISE        | VEHICLE TRACKING CONTROL |
| APPROVED: <i>[Signature]</i> |                          |
| ISSUED: 10/7/19              | REVISION: 8/19/2020      |
|                              | DRAWING NO. 900-VTC      |



For and on Behalf of  
Kiowa Engineering Corporation Date

**Kiowa**  
Engineering Corporation

1604 South 21st Street  
Colorado Springs, Colorado 80904  
(719) 630-7342



| Sheet Revisions | IFC           |
|-----------------|---------------|
|                 | No Revisions: |
|                 | Revised:      |
|                 | Void:         |

**ROCK ISLAND TRAIL**  
GRADING AND EROSION CONTROL PLAN  
EROSION CONTROL DETAILS

Designer: TAC  
Detailer: JDC/TEG  
Date: 11/22/2024

|                       |
|-----------------------|
| Kiowa Proj. No. 16028 |
| TAP M240-162          |
| SubAcct No. 20391     |
| Sheet Number GEC 8    |
