

Client: Dave Gish
 Widefield School District 3
 1820 Main Street
 Colorado Springs, CO 80911

Webster Elementary School Addition & Alterations

Report Date: Apr 13, 2023
 Work Order Date: Apr 10, 2023

Work Order No.: 22-8500.Concrete.0051; ver: 1
 Reviewed by: Josiah Johnson

Concrete

Concrete Contractor: Gonzalez Concrete
 Placement Method: Tailgated
 Total Quantity Placed: 7.50 yd³
 Placement Location: Forebays and storm detention channel
 Comments: No mix design provided. Air and slump specifications provided by Steve Buellesbach with Nunn Construction. Air 5-8%, Slump 2.5-5".

Performed by: Nick Davidson
 Finish Method: Vibrated- Internally|Hand Finished|Trowel Finished
 Weather: Sunny

On-site Notifications, Specification, and Mix Information

On-Site Notification(s)	Item / Structure Type	Test	Specified	Mix Design
Steve Buellesbach with Nunn Construction	General Concrete	Air Content (%)	-	-
	Mix Placed	Slump (in)	-	-
	Transit Mix T34592110	Unit Weight (pcf)	-	-
		Comp. Strength (psi)	-	-

Sampling (ASTM C172 / AASHTO R60 / CDOT CP61)

Sample No.	Location	Sampled From	Quantity (yd ³)	Truck No.	Ticket No.	Batch Time	Test Time	Air Temp. (°F)	Water Added (gal)
50	See attachment for test location 1	Point of Placement	7.50	33	86505162	8:40 AM	9:39 AM	50	0

Field Tests (ASTM C138, C143, C231, and C1064 / AASHTO T119, T121, and T152)

Sample No.	Concrete Temp. (°F)	Slump (in)	Air Cont. (%)	Meas. Vol. (ft ³)	Empty Meas. (lb)	Full Meas. (lb)	Unit Wt. (pcf)	Lab Samples Cast
50	80	3.5	6.4	.250	7.76	42.56	139.2	Yes

Compressive Strength (ASTM C31 and C39 / AASHTO T22 and T23)

A set of compressive strength specimens were cast. Test results will be forwarded upon completion.

Results apply only to the specific items and locations referenced and at the time of testing, observations or special inspections. Unless noted otherwise, specimens were received in adequate condition. Compressive strength specimens, if tested, were capped in accordance with ASTM C1231 or ASTM C617, as applicable. This report should not be reproduced, except in full, without the written permission of GROUND Engineering Consultants, Inc.

Webster Elementary School Addition & Alterations

Report Date: Apr 13, 2023

Work Order No.: 22-8500.Concrete.0051; ver: 1

Work Order Date: Apr 10, 2023


Reviewed by: Josiah Johnson

Concrete

Photos



Forebay and storm detention channel

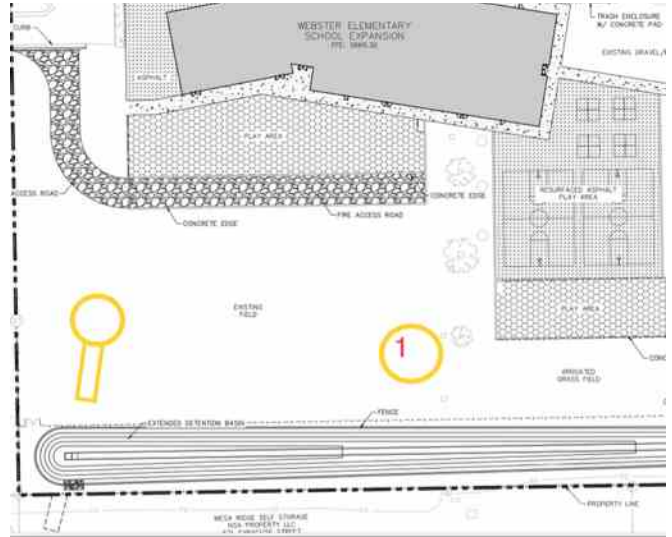

Yellow represents forebay and storm detention channel and red number represents test location
