

VILLAS AT ASPEN TRAILS

Stormwater Management Plan

(SWMP)

February 2023

Prepared for:

ROS Equity Holdings-Independence

17 S Wahsatch ST.

Colorado Springs, CO 80903

Prepared by:

Dakota Springs Engineering

31 N Tejon ST., Suite 500

Colorado Springs, CO 80903

Contractor:

N.B. Trenchless, Inc

101 N. Cascade Ave Suite 10

Colorado Springs , CO 80903

Stormwater Manager:

Charles K. Cothern

charlescothern@springseng.com

(719) 432-6889

EPC Project No. SP234

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

Table of Contents

1. INTRODUCTION.....	1
2. GENERAL LOCATION AND DESCRIPTION.....	1
3. DESCRIPTION OF CONSTRUCTION	2
4. PHASING PLAN	2
5. DESCRIPTION OF DRAINAGE CONVEYANCE.....	3
6. ESTIMATES OF EXCAVATION	3
7. CONSTRUCTION SCHEDULE	4
8. VEGETATION	4
9. SOILS	4
10. POTENTIAL POLLUTANTS	5
11. MATERIAL HANDLING AND SPILL PREVENTION.....	6
12. RECEIVING WATERS	6
13. DISCHARGE.....	6
14. GRADING AND EROSION CONTROL PLAN.....	7
15. BEST MANAGEMENT PRACTICES	7
16. FINAL STABILIZATION AND LONG-TERM STORM WATER MANAGEMENT	8
17. INSPECTIONS.....	8
18. SWMP REVISIONS	8
INSPECTION AND MAINTENANCE LOG	9
APPENDIX A – VICINITY MAP / SITE MAP.....	10
APPENDIX B– Grading and Erosion Control (GEC) Plan	11
APPENDIX C– EROSION AND STORMWATER QUALITY CONTROL PERMIT	12

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

1. INTRODUCTION

This Stormwater Management Plan is being submitted on the behalf of ROS Equity Holdings-Independence, LLC for a tract of land known as:

A TRACT OF LAND LOCATED IN A PORTION OF SECTION 9, IN TOWNSHIP 15 SOUTH, RANGE 65 WEST OF THE 6TH P.M., EL PASO COUNTY, COLORADO, MORE PARTICULARLY DESCRIBED AS FOLLOWS:

COMMENCING AT THE NORTH 1/4 CORNER OF SAID SECTION 9;

THENCE S00°19'32"E, ALONG THE NORTH-SOUTH CENTERLINE OF SAID SECTION 9, A DISTANCE OF 1612.07 FEET TO A POINT ON THE SOUTHERLY R.O.W. LINE OF BRADLEY ROAD AS RECORDED IN BOOK 5307 AT PAGE 1472 OF THE RECORDS OF SAID EL PASO COUNTY:

THE FOLLOWING 3 COURSES ARE ALONG THE SAID SOUTHERLY R.O.W. LINE OF BRADLEY ROAD.

- 1) THENCE S89°30'29"W A DISTANCE OF 3.78 FEET TO A POINT OF CURVE TO THE LEFT;
- 2) THENCE ON SAID CURVE, HAVING A RADIUS OF 2759.79 FEET, AN ARC LENGTH OF 730.29 FEET, A DELTA ANGLE OF 15°09'41", WHOSE LONG CHORD BEARS S81°55'38"W A DISTANCE OF 728.16 FEET;
- 3) THENCE S74°20'48"W A DISTANCE OF 385.14 FEET TO THE POINT OF BEGINNING;

THENCE S15°39'12"E DEPARTING SAID RIGHT-OF-WAY LINE, A DISTANCE OF 449.99 FEET;

THENCE S74°20'48"W A DISTANCE OF 160.21 FEET;

THENCE N15°39'12"W A DISTANCE OF 20.00 FEET;

THENCE S74°20'48"W A DISTANCE OF 199.80 FEET TO A POINT OF CURVE TO THE RIGHT;

THENCE ON SAID CURVE, HAVING A RADIUS OF 75.00 FEET, AN ARC LENGTH OF 78.64 FEET, A DELTA ANGLE OF 60°04'25", WHOSE LONG CHORD BEARS N75°37'00"W A DISTANCE OF 75.08 FEET;

THENCE N15°39'12"W A DISTANCE OF 392.40 FEET, RETURNING TO SAID SOUTHERLY R.O.W. LINE OF BRADLEY ROAD;

THENCE S74°20'48"W, ALONG SAID SOUTHERLY R.O.W. LINE OF BRADLEY ROAD, A DISTANCE OF 425.01 FEET TO THE POINT OF BEGINNING.

The purpose of this report is to outline the SWMP Plan for the Villas at Aspen Trails development located at the southeast corner of Bradley Rd and Legacy Hill Dr, El Paso County, Colorado. This report identifies Best Management Practices (BMPs) that will reduce or eliminate any possible water quality impacts.

2. GENERAL LOCATION AND DESCRIPTION

The site lies in Section 9 of Township 15 South, Range 65 West. The proposed plat is south of Bradley Road, east of Legacy Hill Dr. The site is currently zoned RM-12.

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

Other development in the area includes single family residential, multifamily, and commercial developments in the surrounding area.

The proposed site encompasses 4.32 acres. The topography of the site and surrounding area is typical of a high desert; short prairie grass and weeds with slopes generally ranging from 1% to 5%. The area generally drains to the south. This development is in the Jimmy Camp Creek Drainage Basin.

3. DESCRIPTION OF CONSTRUCTION

ROS Equity Holdings-Independence, LLC requests approval of site grading for 4.32 acres of property within the recently amended Waterview Sketch. The Villas at Aspen Trails proposed Land Uses consist of 41 residential lots on 4.32 acres.

The Pre-Subdivision Site Grading does not include authorization to install wet utilities. The request will be limited to over lot grading and balancing of the site prior while the final subdivision design is refined through the pending preliminary plan design, submittal, and review process.

A final plan will be submitted to approve a residential subdivision. This final plan may include requests for additional Site Grading to include installation of wet utilities after final site, lot, roadway, and stormwater designs are refined through the preliminary subdivision design and review processes. The addition of installation of wet utilities will require additional coordination with the respective utility service providers and approval by the CDPHE.

4. PHASING PLAN

Pre-subdivision site grading will be done on the entire site at one time. The contractor will manage the grading activities. Once the site is graded construction will be phased according to any internal phasing required for the subdivision. The general sequence of the related pre-subdivision site grading activities will occur according to the following anticipated sequence:

Phased BMP Implementation - Initial and Interim Phase

Add in TSB

The initial phase shall consist of the temporary construction BMPs to minimize potential for erosion and sediment transfer while mobilizing and preparing the site for construction activities. The Contractor shall complete the anticipated initial and interim phase sequencing as follows:

1. Install vehicle tracking control (VTC) as indicated on the GEC plans or as necessitated by field conditions.
2. Install silt fence (SF) as shown on the GEC plans or as necessitated by field conditions.
3. Install rough cut street control (RC) as shown on the GEC plans or as necessitated by field conditions.
4. Upon completion of the initial BMP installation the operator shall schedule a pre-construction meeting with the owner and the city erosion control inspector to confirm BMPs installed are adequate prior to proceeding with additional land disturbing activities.

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

Phased BMP Implementation - Final Phase

The final phase shall consist of the temporary construction BMPs to minimize potential for erosion and sediment transfer during construction of the proposed sites and associated limited site improvements. The Contractor shall complete the anticipated final phase sequencing as follows:

1. Confirm existing BMPs from the initial phases, which are to be maintained throughout construction, are in working order and compliant with applicable regulations.
2. Repair and/or replace any existing BMPs which are deemed inadequate.
3. Temporarily stabilize (TS) all areas of the site which will remain inactive for a period greater than 30 days. Temporary stabilization shall be implemented within 14 days of disturbance.
4. Complete required grading operations necessary for construction of the proposed sites and associated site improvements.
5. Complete fine grading and proceed with temporary stabilization (TS) and permanent stabilization (PS) practices in accordance with approved plans.
6. Achieve permanent stabilization in accordance with the El Paso County (EPC) and owner requirements.
7. Remove remaining BMPs once permanent stabilization (PS) has been achieved. Repair and stabilize areas disturbed through BMP removal.
8. Notify the EPC of the intent to file the notice of inactivation and receive EPC field acceptance prior to proceeding with filing the notice of inactivation with the EPC.
9. Proceed with filing the notice of inactivation with the EPC.
10. Provide the owner with a copy of all stormwater documentation (permits, inspection reports, logs, etc.). Upon completion of project, file the notice of inactivation.

5. DESCRIPTION OF DRAINAGE CONVEYANCE

The site drains to the south; the drainage captured by the property is conveyed to a Type R inlet in a low point in Frontline Dr. This inlet joins a drainage system that discharges toward the Jimmy Camp Creek Drainage Basin. Stormwater facilities to be constructed with the early grading permit will consist of a permanent detention pond. Storm sewer facilities will be installed throughout the site and in the streets with future final plat approvals; these will eventually replace the swales and sedimentation basins to convey storm water runoff to the permanent detention facilities.

6. ESTIMATES OF EXCAVATION

The subject site is approximately 4.32 acres.

clarify how much of that is to be disturbed. According to page 2 of the ESQCP App, it's all 4.32ac.

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

Over site grading will be limited to the construction of the primary street sections and sloping the site toward the detention basin to meet minimum design requirements. As the lots are developed by private builder’s disturbance will be for building foundations, landscaping, roadways, and sidewalks. The earthwork volumes are as follows:

CUT 4,982 CY

FILL 4,624 CY (Adjusted for shrinkage)

NET 358 CY (Cut)

All volumes assume 2,269 CY of topsoil either useable on site or imported

Revise to future dates

7. CONSTRUCTION SCHEDULE

- Clearing and grubbing
- Rough grading for lots and roads
- Utility Installation
- Final grading, curb and gutter and paving
- Final Stabilization

<u>Estimated Start</u>	<u>Estimated End</u>
June 1, 2023	July 1, 2023
June 15, 2023	July 15, 2023
July 15, 2023	September 15, 2023
October 1, 2023	November 30, 2023
	January 1, 2024

8. VEGETATION

The existing Site is currently undeveloped consisting of on-site native vegetation; short prairie frass and weeds with slopes ranging from 5% to 15%. The estimated vegetative coverage is about 60% and unvegetated (40%), determined by observation from site visit. The sites surrounding this land is currently at varying stages of development.

9. SOILS

The site is composed of several different soil types. From the NRCS report, the site falls into the following soil types:

- 8 - Blakeland loamy sand (1-3%) – Type A Soil
- 31 - Fort Collins Loam (3-8%) – Type B Soil
- 56 - Nelson Tassel fine sandy loam (3-18%) – Nelson Type B, Tassel Type D Soil
- 86 - Stoneham sandy loam (3-8%) – Type B Soil
- 108 - Wiley silt loam (3-9%) – Type B Soil

Hydrologic soil groups are based on estimates of runoff potential. Soils are assigned to one of four groups according to the rate of water infiltration when the soils are not protected by vegetation, are thoroughly wet, and receive precipitation from long-duration storms.

The soils in the United States are assigned to four groups (A, B, C, and D) and three dual classes (A/D, B/D, and C/D). The groups are defined as follows:

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

Group A. Soils having a high infiltration rate (low runoff potential) when thoroughly wet. These consist mainly of deep, well drained to excessively drained sands or gravelly sands. These soils have a high rate of water transmission.

Group B. Soils having a moderate infiltration rate when thoroughly wet. These consist chiefly of moderately deep or deep, moderately well drained or well drained soils that have moderately fine texture to moderately coarse texture. These soils have a moderate rate of water transmission.

Group C. Soils having a slow infiltration rate when thoroughly wet. These consist chiefly of soils having a layer that impedes the downward movement of water or soils of moderately fine texture or fine texture. These soils have a slow rate of water transmission.

Group D. Soils having a very slow infiltration rate (high runoff potential) when thoroughly wet. These consist chiefly of clays that have a high shrink-swell potential, soils that have a high water table, soils that have a claypan or clay layer at or near the surface, and soils that are shallow over nearly impervious material. These soils have a very slow rate of water transmission.

If a soil is assigned to a dual hydrologic group (A/D, B/D, or C/D), the first letter is for drained areas and the second is for undrained areas. Only the soils that in their natural condition are in group D are assigned to dual classes.

Estimated Runoff Coefficients

Average Prior to Construction	C5=0.08 and C100=0.35
Average After Buildout	C5=0.55 and C100=0.69

Potential for soil erosion during construction is minimal. The grading and erosion control plan includes measures to reduce this potential. Where the majority of the property drains to will be constructed to capture any sediment. The pond discharges to an existing storm drainage system south of the property.

10. POTENTIAL POLLUTANTS

During construction, the largest possible source of non-stormwater pollution will be during equipment refueling operations. Refueling of construction equipment will be completed in a designated area established by the contractor. The contractor shall be responsible for any spill cleanup while refueling, in accordance with applicable local, county and state regulations. The contractor will also be responsible for cleanup of any off-site vehicle tracking on paved roads. Tracking control will be provided at the entrances to the site. No other source of pollution such as vehicle washing, chemical storage or waste disposal is anticipated. No batch plants will be onsite. Any onsite facilities that could be identified as a source of pollutants will follow preventive measures found in the Material Handling and Spill Prevention section below.

A list of all potential sources of pollution which may reasonably be expected to affect the quality of stormwater discharges associated with construction activity from the site are as follows:

1. Disturbed and stored soils
2. Vehicle tracking of sediments

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

3. Loading and unloading operations
4. Outdoor storage activities
5. Vehicle and equipment maintenance and fueling
6. Significant dust or particulate generating processes
7. Routine maintenance activities involving fertilizers, pesticides, herbicides, detergents, fuels, solvents, oils, etc.
8. Non-industrial waste sources such as worker trash and portable toilets.

All construction waste will be removed along with contaminated soil and disposed of offsite at the end of the construction period. Construction debris will also be removed from the site as it is accumulated and disposed of properly offsite. After construction any pollutants will be captured in the detention pond; specifically in the fore bays and will be dealt with as part of regular maintenance by the owners of Villas at Aspen Trails.

11. MATERIAL HANDLING AND SPILL PREVENTION

The most probable source of non-stormwater pollution is refueling and daily maintenance operations. If mobile fuel trucks are used to service equipment, absorbent materials and containers for the storage of used absorbent material will be close by. If a fuel tank is left on site, berms will be built around the tank to capture any spilled fuel. Again, absorbent materials and their containers will be on hand.

If storage of chemicals on site is required the contractor shall be responsible for the construction of berms around the storage to capture any spilled material. Again, absorbent materials and their containers will be on hand

12. RECEIVING WATERS

The site is located within the Jimmy Camp Creek basin. Per the project's preliminary drainage report (November 2022, Kimley-Horn and Associates, LLC.) off-site basins sheet flow onto the site from the **ease** and west. The offsite flow is within the same basin: the Jimmy Camp Creek Basin.

13. DISCHARGE

There are no anticipated non-stormwater components of the discharge. The receiving waters for this discharge are Jimmy Camp Creek which drains to Fountain Creek and ultimately the Arkansas River.

The site is mostly vacant land and has no springs, streams wetlands or any other surface waters on or crossing the site.

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

14. GRADING AND EROSION CONTROL PLAN

A map is provided with this SWMP application that details the site, limits of construction and erosion control measures. This map will be used by the contractor to track installation, maintenance and removal of BMP's during construction; including any field changes that are required during construction.

15. BEST MANAGEMENT PRACTICES

Construction operations including grading, hauling of soil, drainage, and final stabilization shall implement erosion and sediment control measures as described below and in the Phasing section found above. Additional measures shall be implemented as appropriate.

Structural BMP's: ← And TSB.

SF - Silt fences will be installed prior to any grading occurring on the site. The silt fence will be installed in the areas shown on the provided map.

VC - Vehicle tracking control will be provided at the entrances to the site on Bradley Road.

DP- Detention pond will be constructed as show on the provided map.

Nonstructural BMP's:

Non-structure practices to control erosion and sedimentation will include reseeding of ground cover in disturbed areas according to the grading and erosion control plan. Seeding of bank slopes and mulching along steep embankments will be performed as required. Seeding of disturbed areas will be mitigated until growth has reached 70% of pre-disturbed levels: $0.6\% \times 0.7\% = 42\%$

Other BMP's:

There are several best management practices that can be employed to prevent or mitigate the source of pollutants and contamination of stormwater runoff. Some of these are:

- All dumpsters and receptacles shall be equipped with functional lids to prevent rain and snow from entering.
- Storage containers, drums and bags shall be stored away from direct traffic routes to prevent accidental spills.
- Empty drums shall be covered to prevent collection of precipitation.
- Containers shall be stored on pallets or other dunnage to prevent corrosion of containers, which can result when containers come in contact with moisture on the ground.
- Regularly scheduled removal of construction trash and debris.

The contractor is certainly not limited to these good housekeeping measures and may implement further controls as prudence and good judgement deem necessary.

The contractor will be responsible for any re-excavation of sediment and debris that collects in the basin depression required to ensure that the basin meets the design grades following construction. The storm lines shall also be cleaned and free of sediment once the site becomes stabilized.

Portable toilets will be located a minimum of 10ft from stormwater inlets and 50ft from state waters. They will be secured at all four corners to prevent overturning and cleaned on a weekly basis. They will be inspected daily for spills.

SWMP Checklist Item 26. Add a note stating that this project does not rely on control measures owned or operated by another entity.

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

Discuss the EDB too.

16. FINAL STABILIZATION AND LONG-TERM STORM WATER MANAGEMENT

Permanent stabilization will be achieved by seeding of disturbed areas. The silt fence installed on site will not be removed until the site is stabilized, and the entire site is established with vegetation growth of 70% of pre-disturbed levels: $0.6 \times 0.7 = 42\%$. Please reference the GEC plan standard notes for seeding of disturbed areas. Areas requiring seeding to provide stabilization to disturbed areas shall use the seed mix set forth in Chapter 14, Volume 1 of the Drainage Criteria Manual.

The site is subject to the NPDES permit program for both construction and post-construction activities. The owner shall obtain all pertinent permits required by controlling agencies including the El Paso County Health Department and the Colorado Department of Public Health & Environment

17. INSPECTIONS

The permit holder shall be responsible for implementation, inspection, and maintenance of all BMP's throughout the construction process to ensure functionality and conformance with all applicable permits and jurisdictional regulations.

A thorough inspection of the storm water management system shall be performed every 14 days as well as after any rain or snowmelt event that causes surface erosion:

- Erosion of channels and side slopes shall be repaired.
- Silt fences shall be cleaned whenever sediment has reached a depth of 6" at the fence, and broken wooden parts or torn fabric shall be repaired or replaced.
- Any accumulated trash or debris shall be removed from the site.

An Inspection and Maintenance Log follows this Storm Water Management Plan.

SWMP Checklist Item 25 - state that the inspection logs must include the QSM's signature.

18. SWMP REVISIONS

Revisions to the SWMP will occur from time to time as construction proceeds. The contractor shall be responsible for revisions to the plan to include the following:


1. Changes to the plan will be tracked by marking changes on the plan with date and note of the responsible party requesting/requiring the change.
2. Dates and responsible party for addition or removal of BMP's will be noted on the plan.
3. If there are any changes the contractor deems to be a significant modification of the approved GEC plan he must contact the owner prior to proceeding.
4. The SWMP will be kept on site and up to date at all times.

Add text stating that the SWMP should be viewed as a "living document" that is continuously being reviewed and modified as a part of the overall process of evaluating and managing SW quality issues at the site. The QSM shall amend the SWMP when there is a change in design, construction, O&M of the site which would require the implementation of new or revised BMPs or if the SWMP proves to be ineffective in achieving the general objectives of controlling pollutants in SW discharges associated with construction activity or when BMPs are no longer necessary and are removed.

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

APPENDIX A – VICINITY MAP / SITE MAP

Z:\0001-Dakota Springs\02-Waterview Partners\19-06_Ray_0_5\CAD\Plansheets\EXHIBITS\RO5 - Vicinity Map.dwg

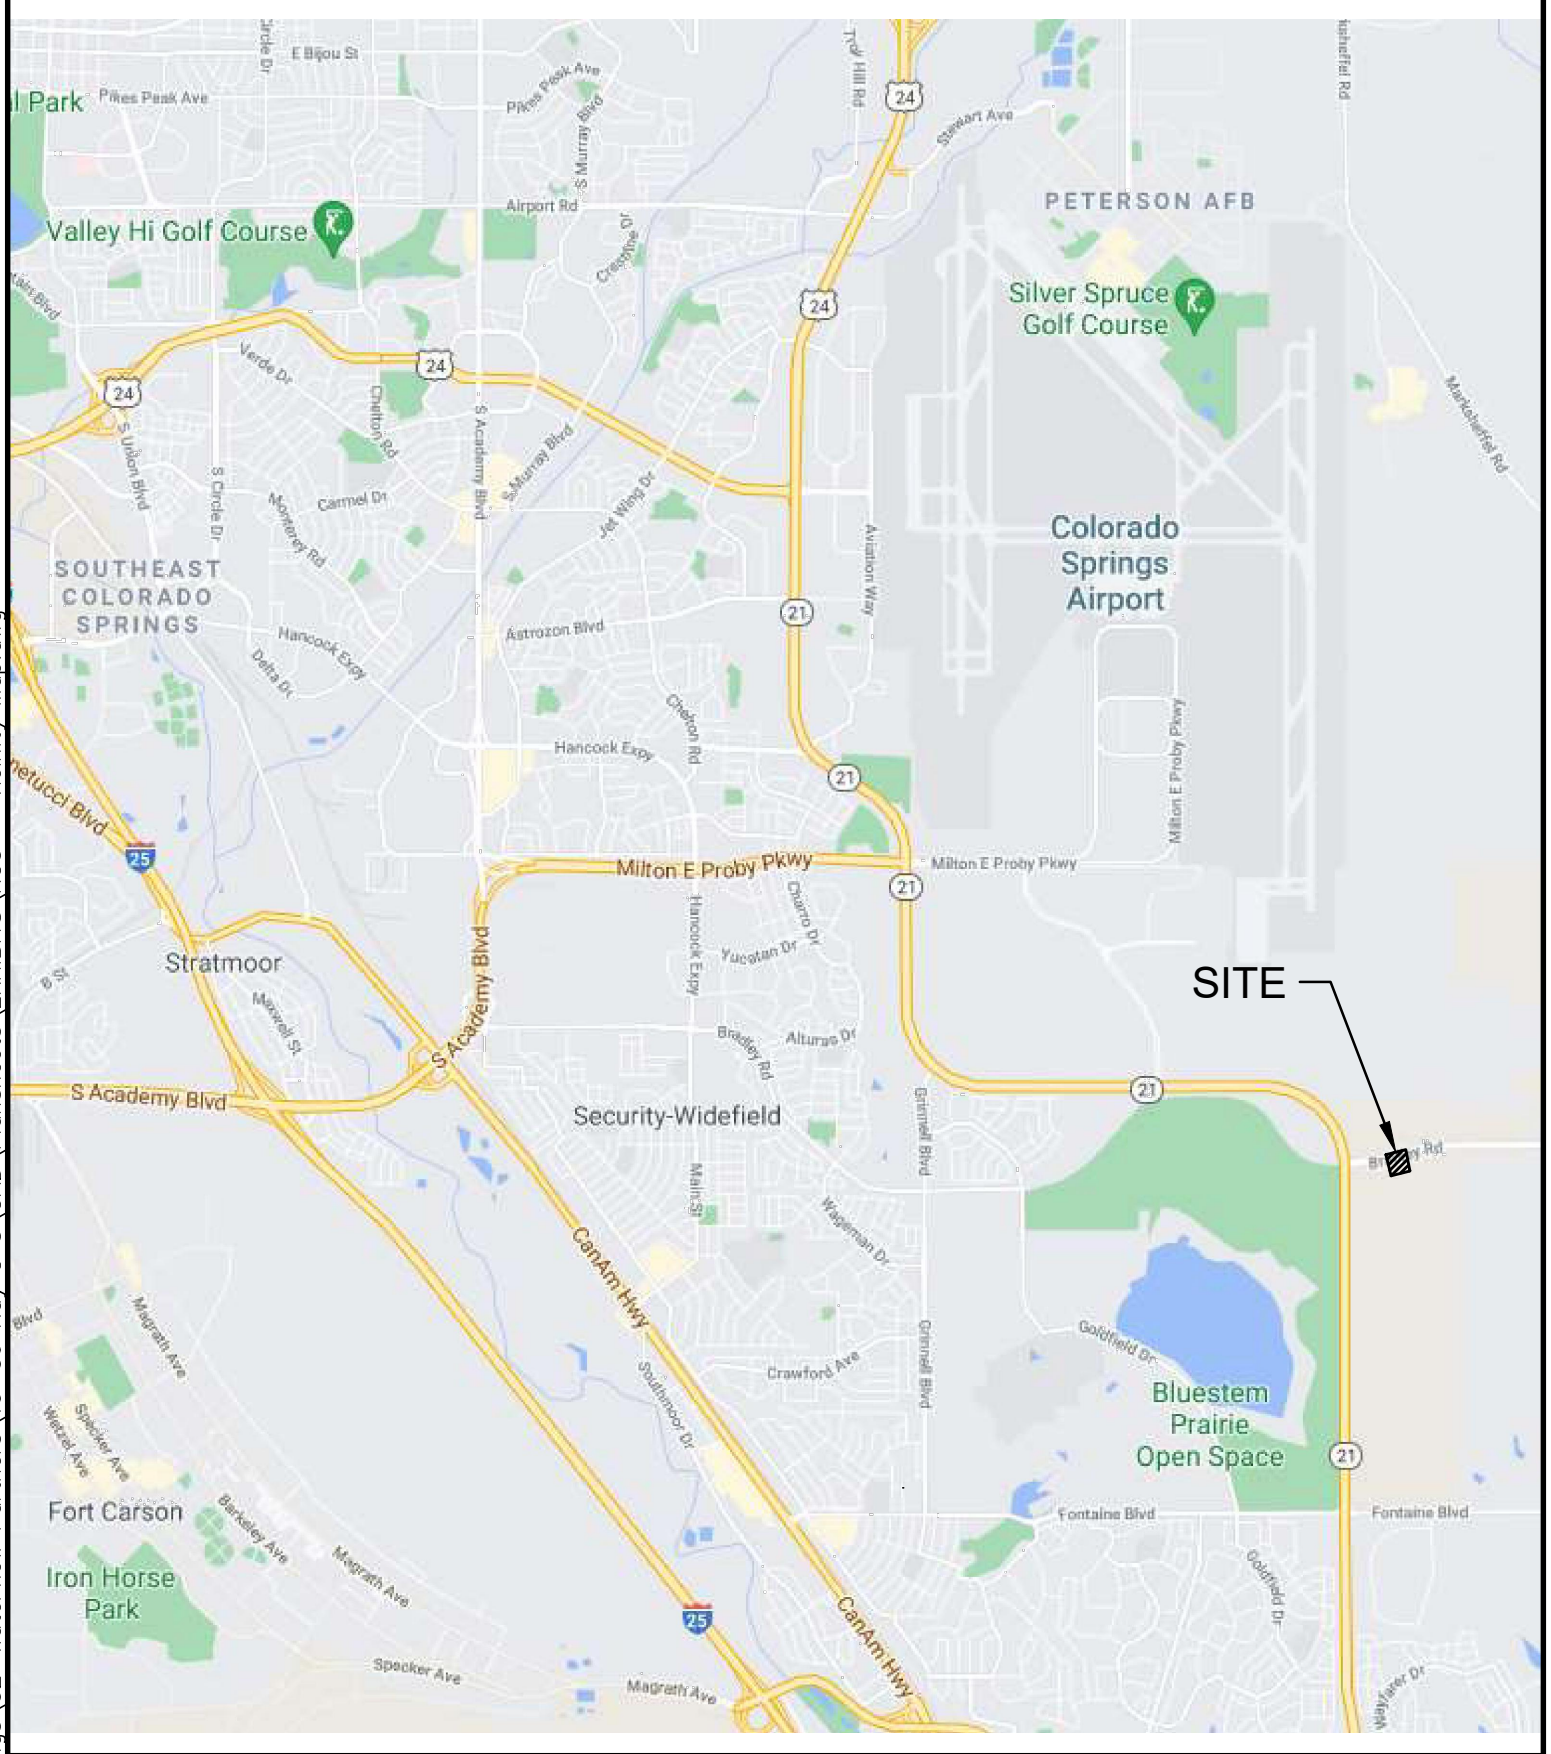

VILLAS AT ASPEN TRAILS

VICINITY MAP



Dakota Springs Engineering

Engineering Consultants

31 N. TEJON, SUITE 518
COLORADO SPRINGS, CO 80903

P: (719) 227-7388 F: (719) 227-7392

SHEET	PROJECT NUMBER:
1 OF 1	0219-06



PROJECT NUMBER:
0219-06



**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**



APPENDIX B– Grading and Erosion Control (GEC) Plan

Z:\0001-Dakota Springs\02-Waterview Partners\19-08 Roy O S\CAD\Plansheets\Prelim Plans\RO5 - Grading.dwg


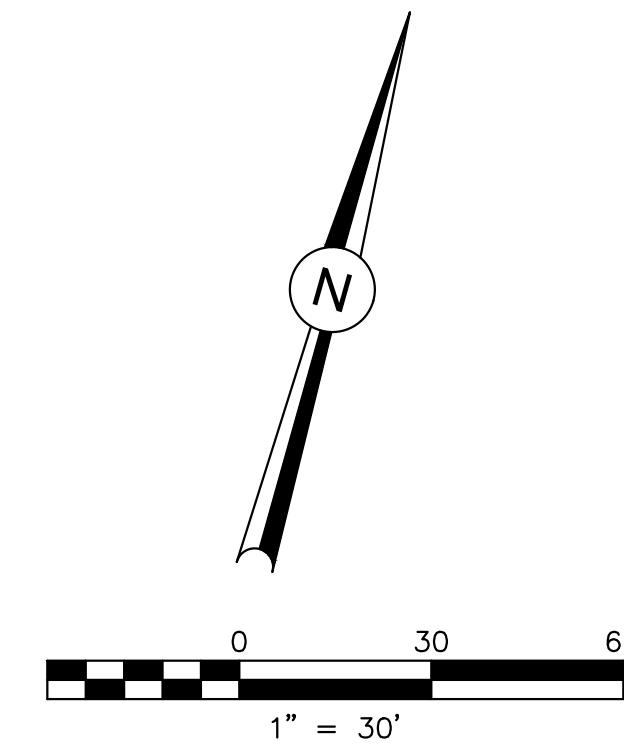
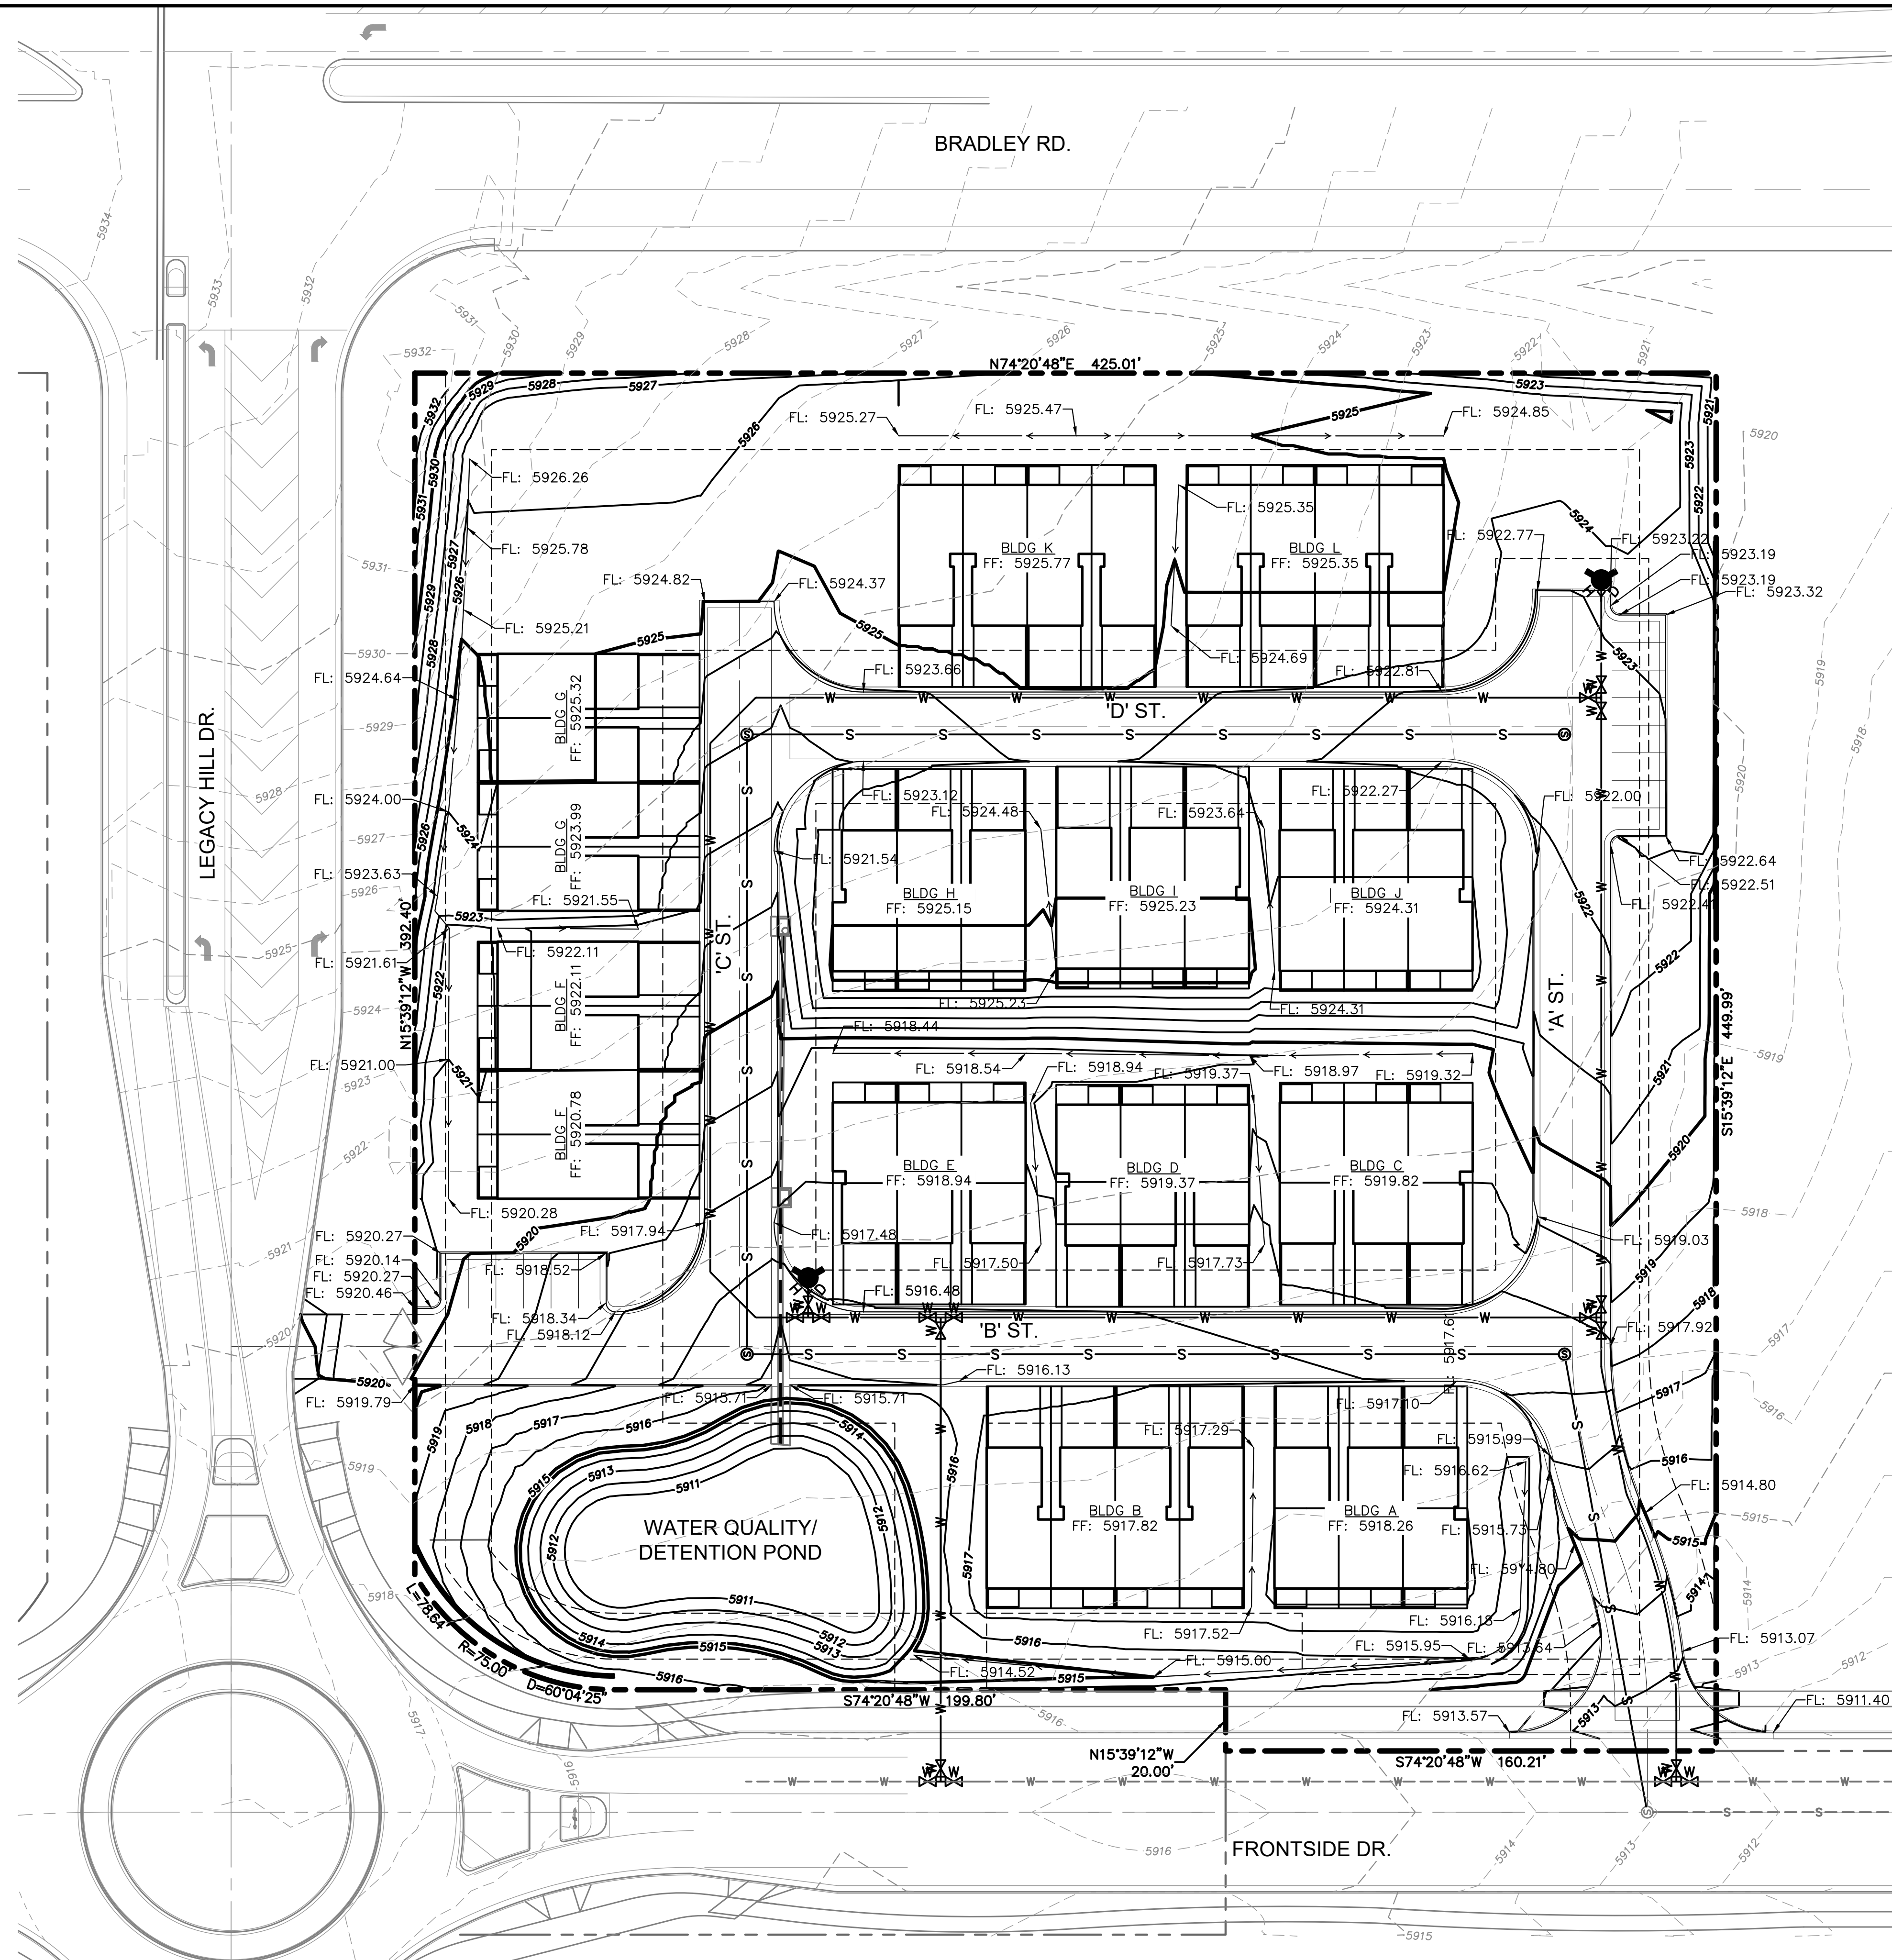


VILLAS AT ASPEN TRAILS
 PRELIMINARY GRADING & EROSION CONTROL PLAN
 GRADING PLAN


NO.	DESCRIPTION	DATE

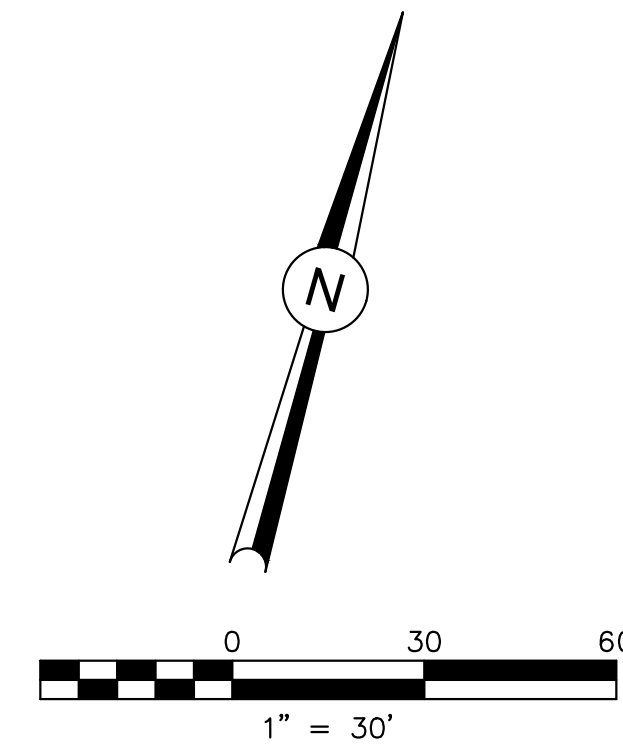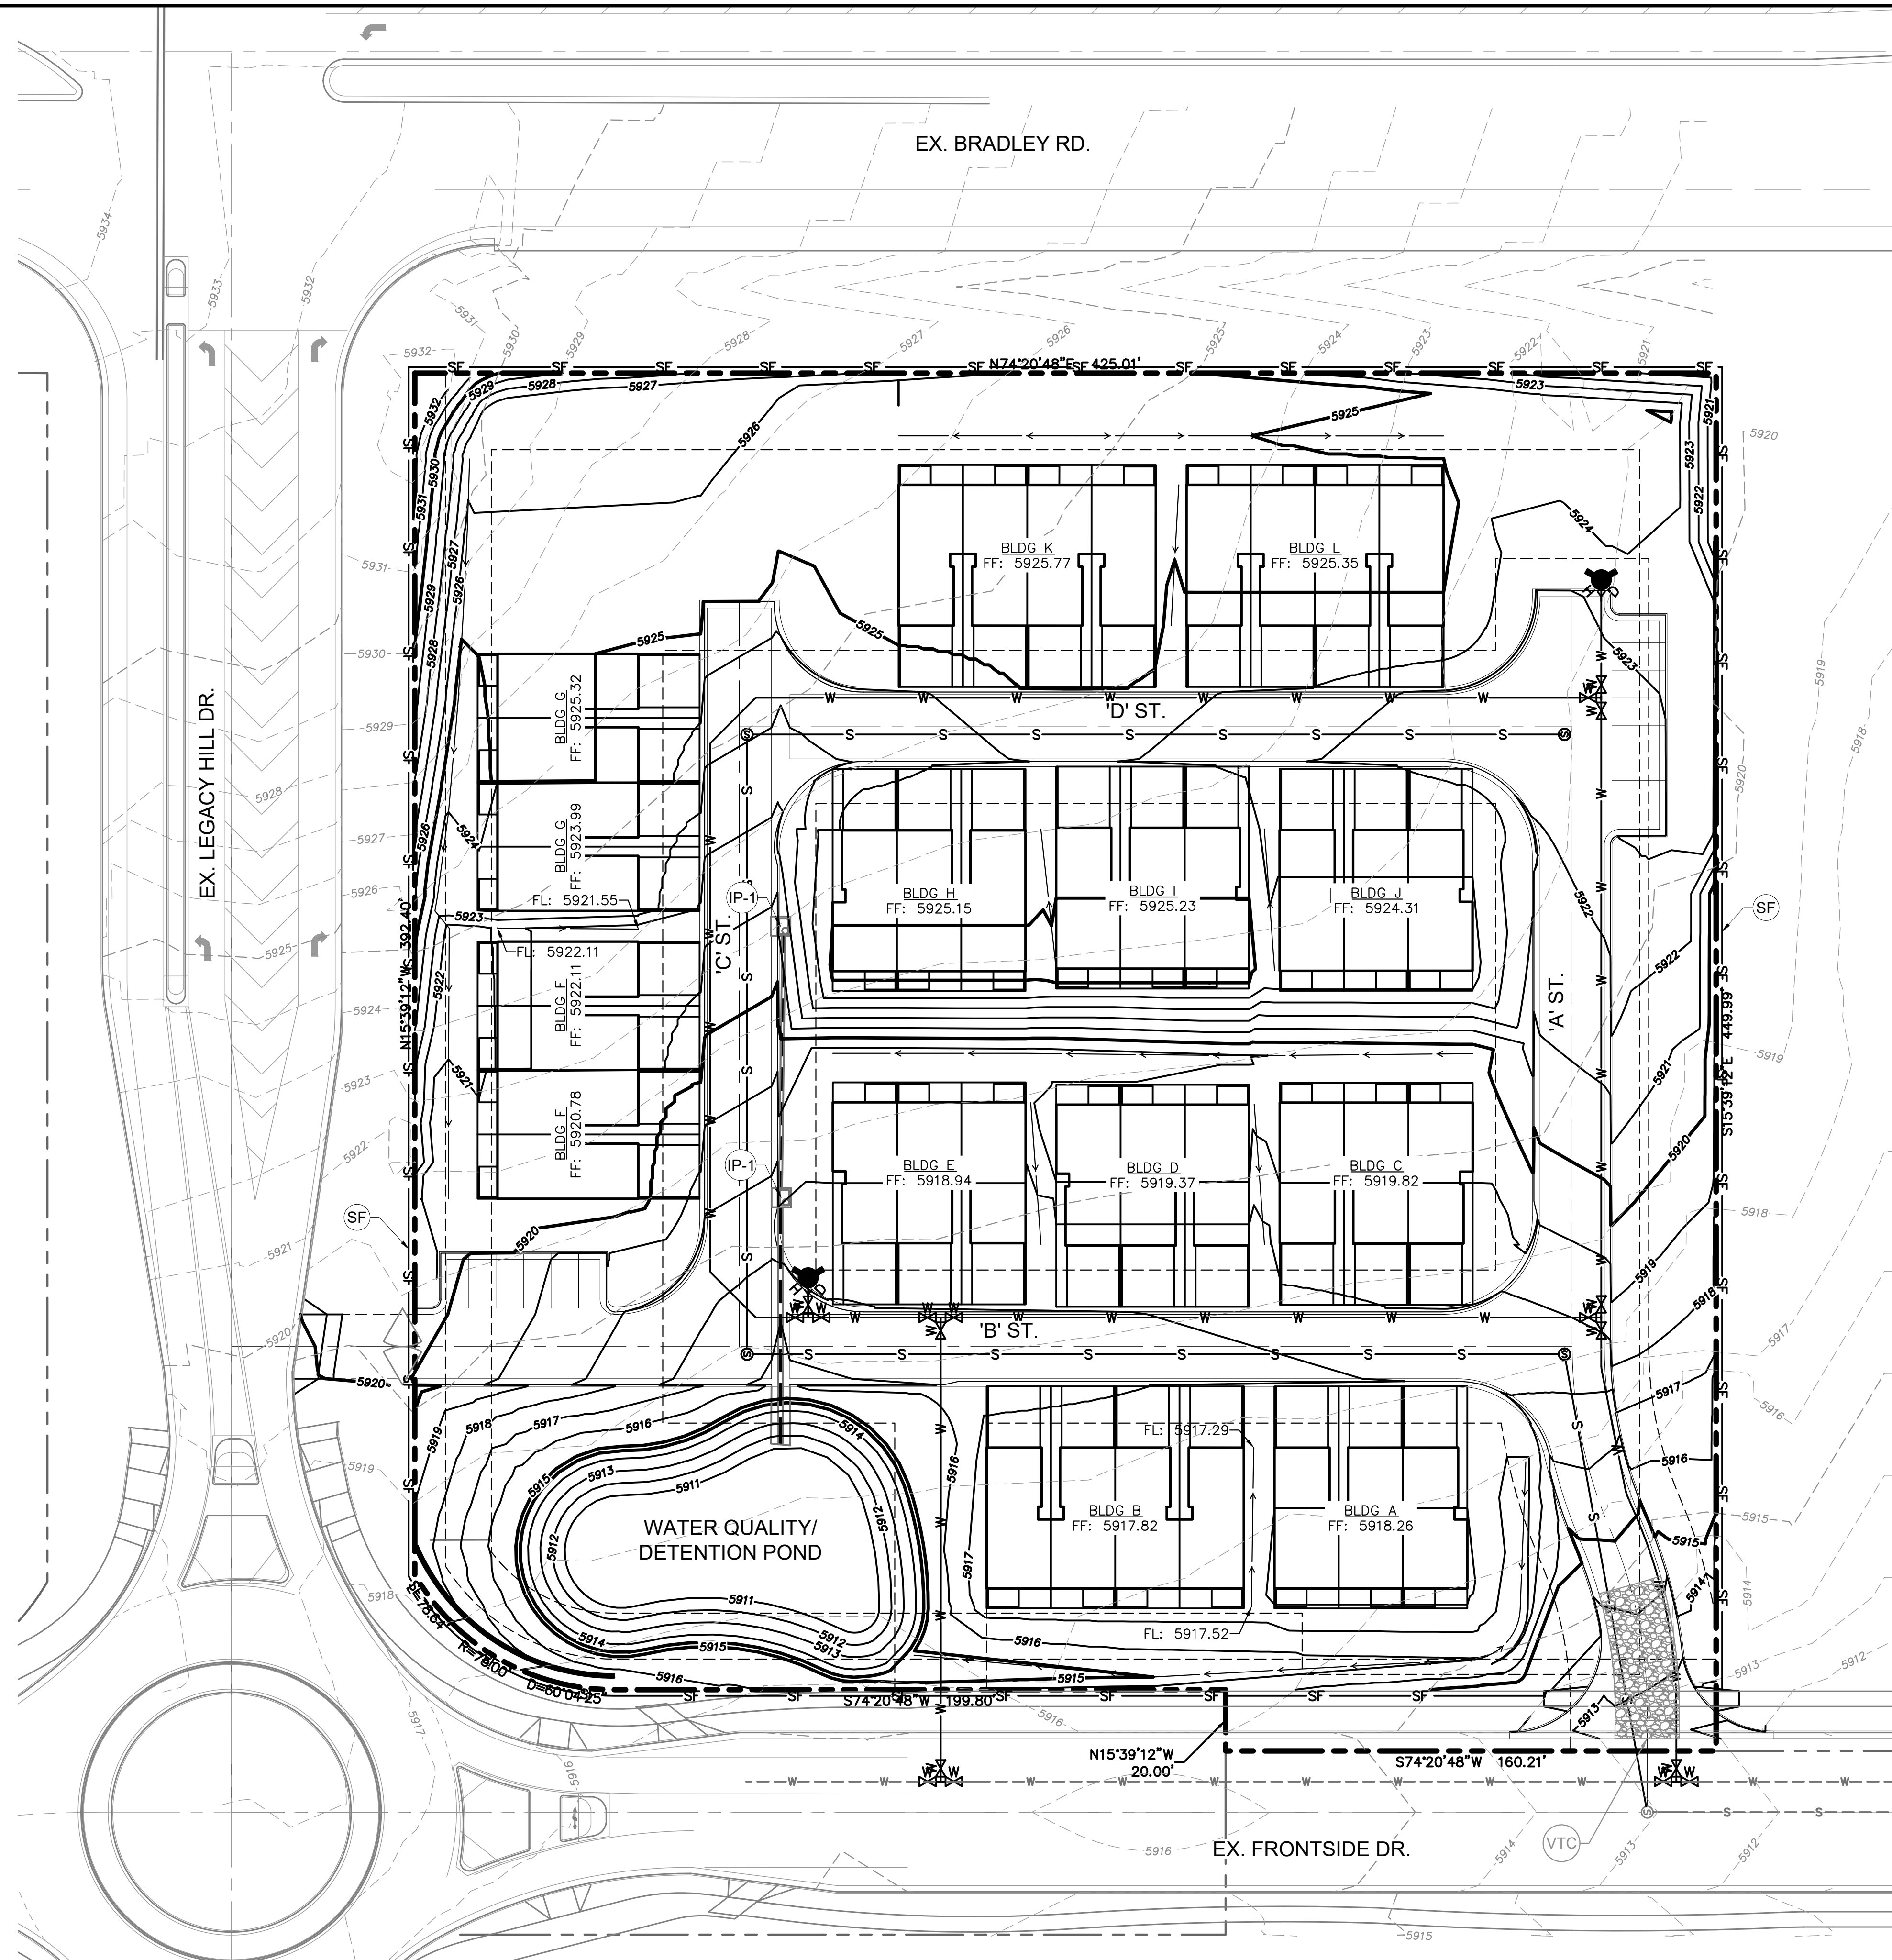


NO.	DESCRIPTION	DATE

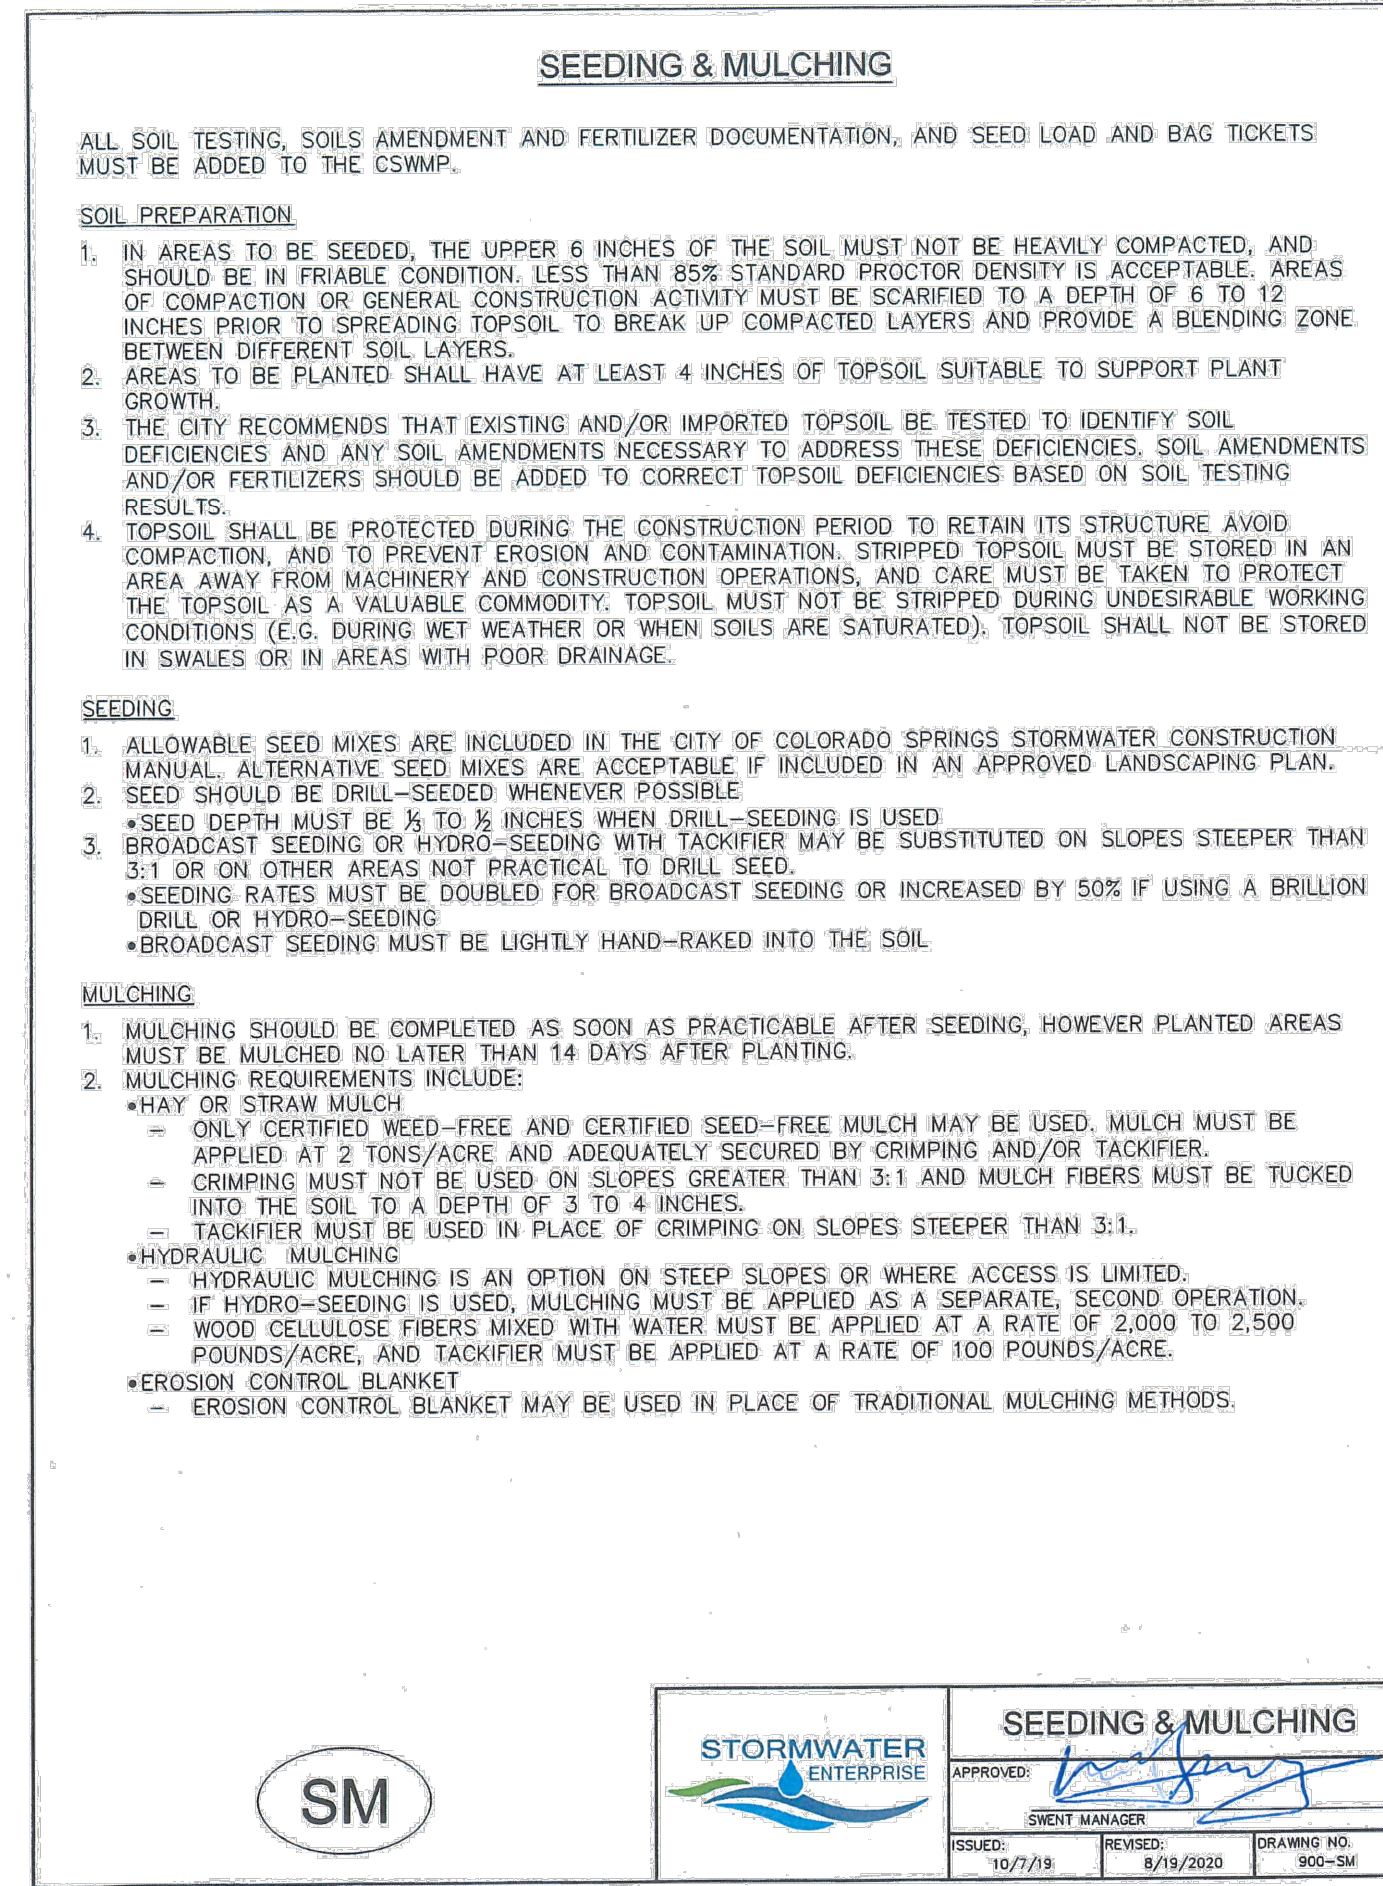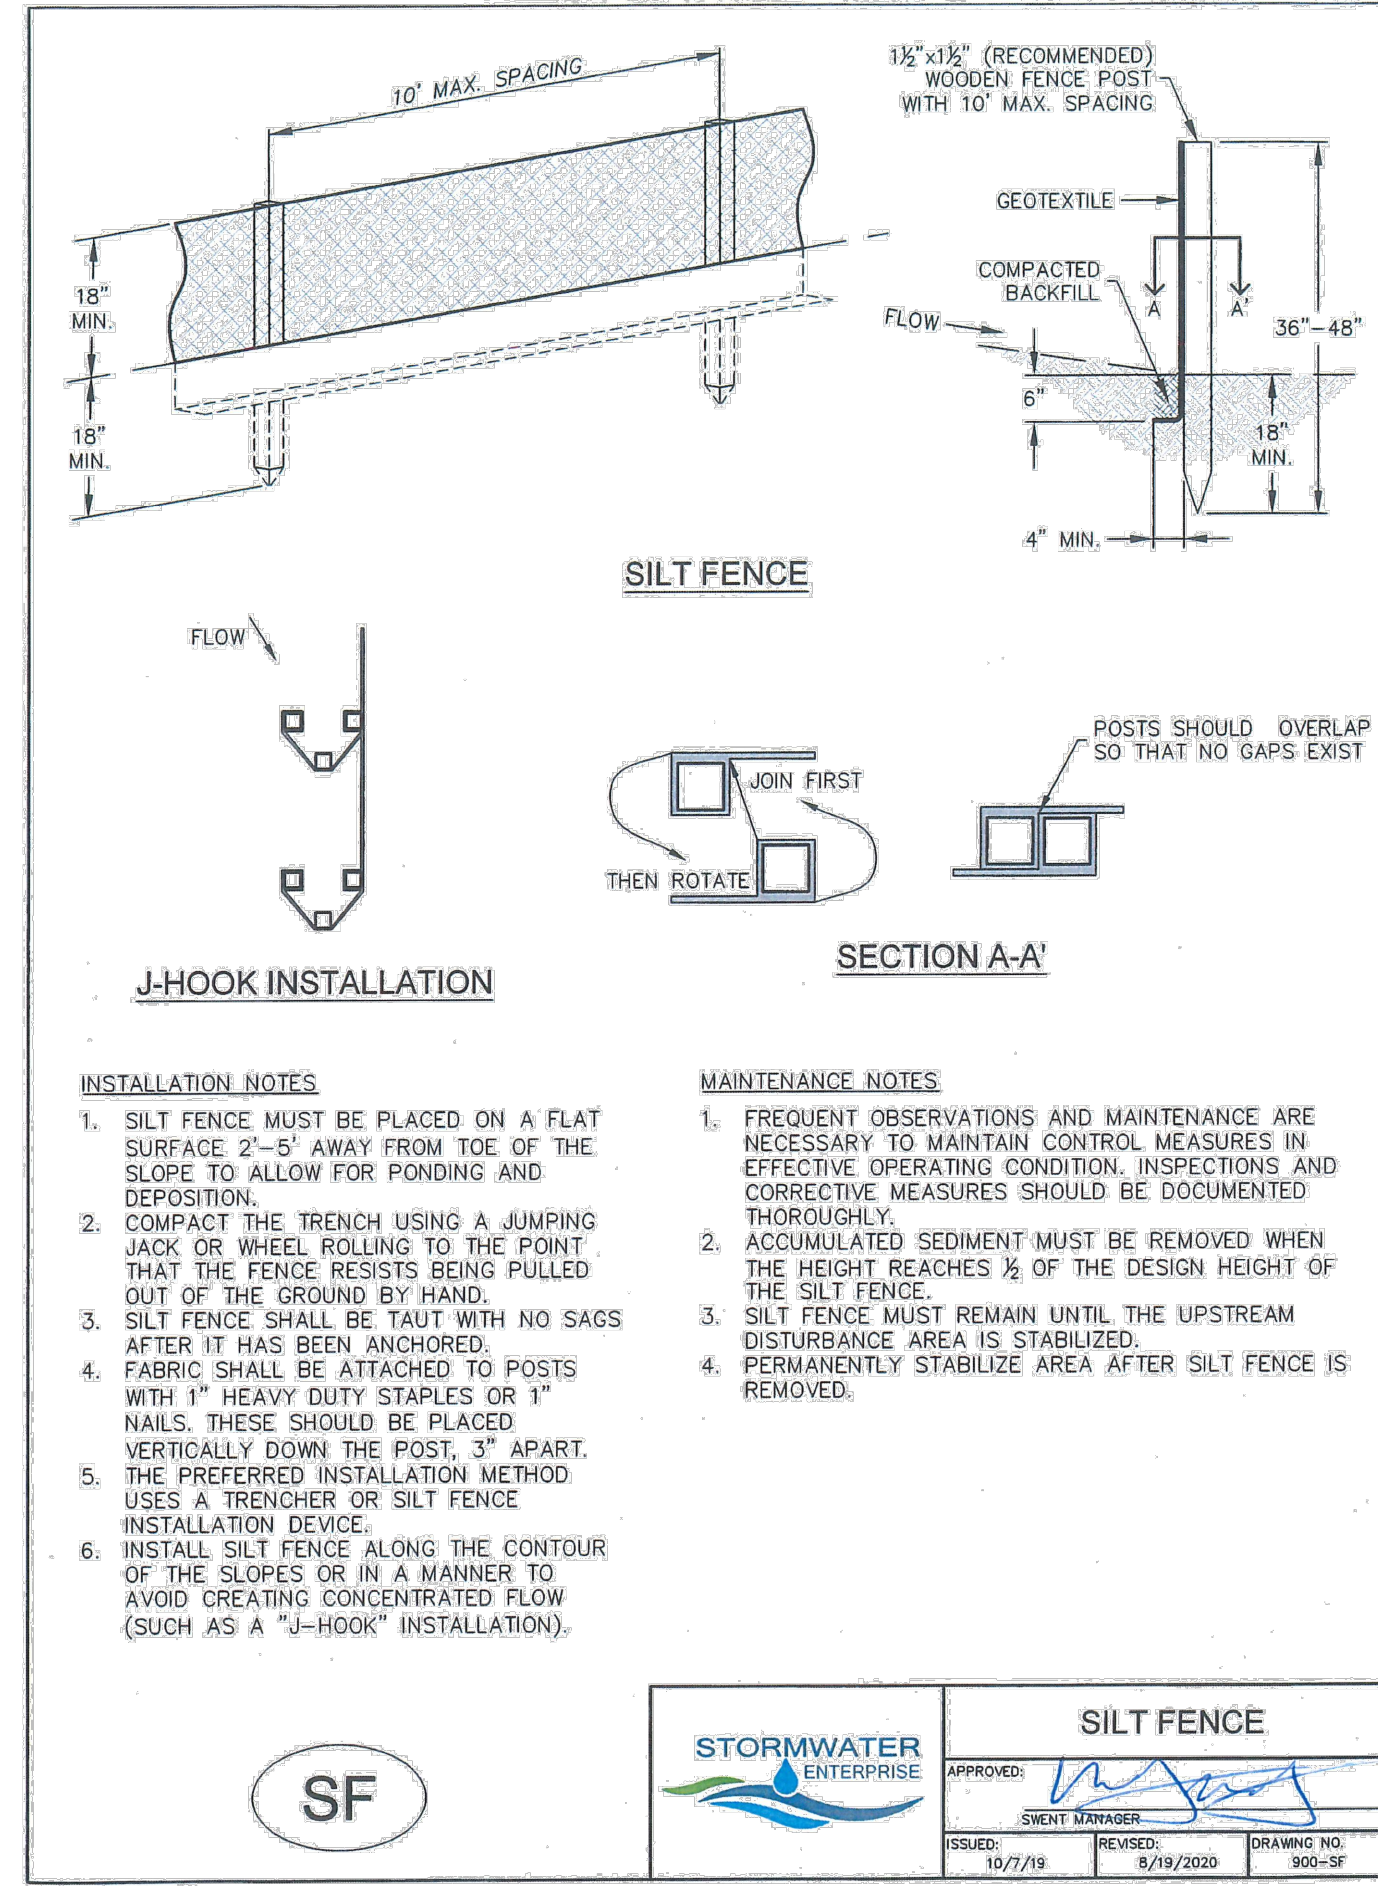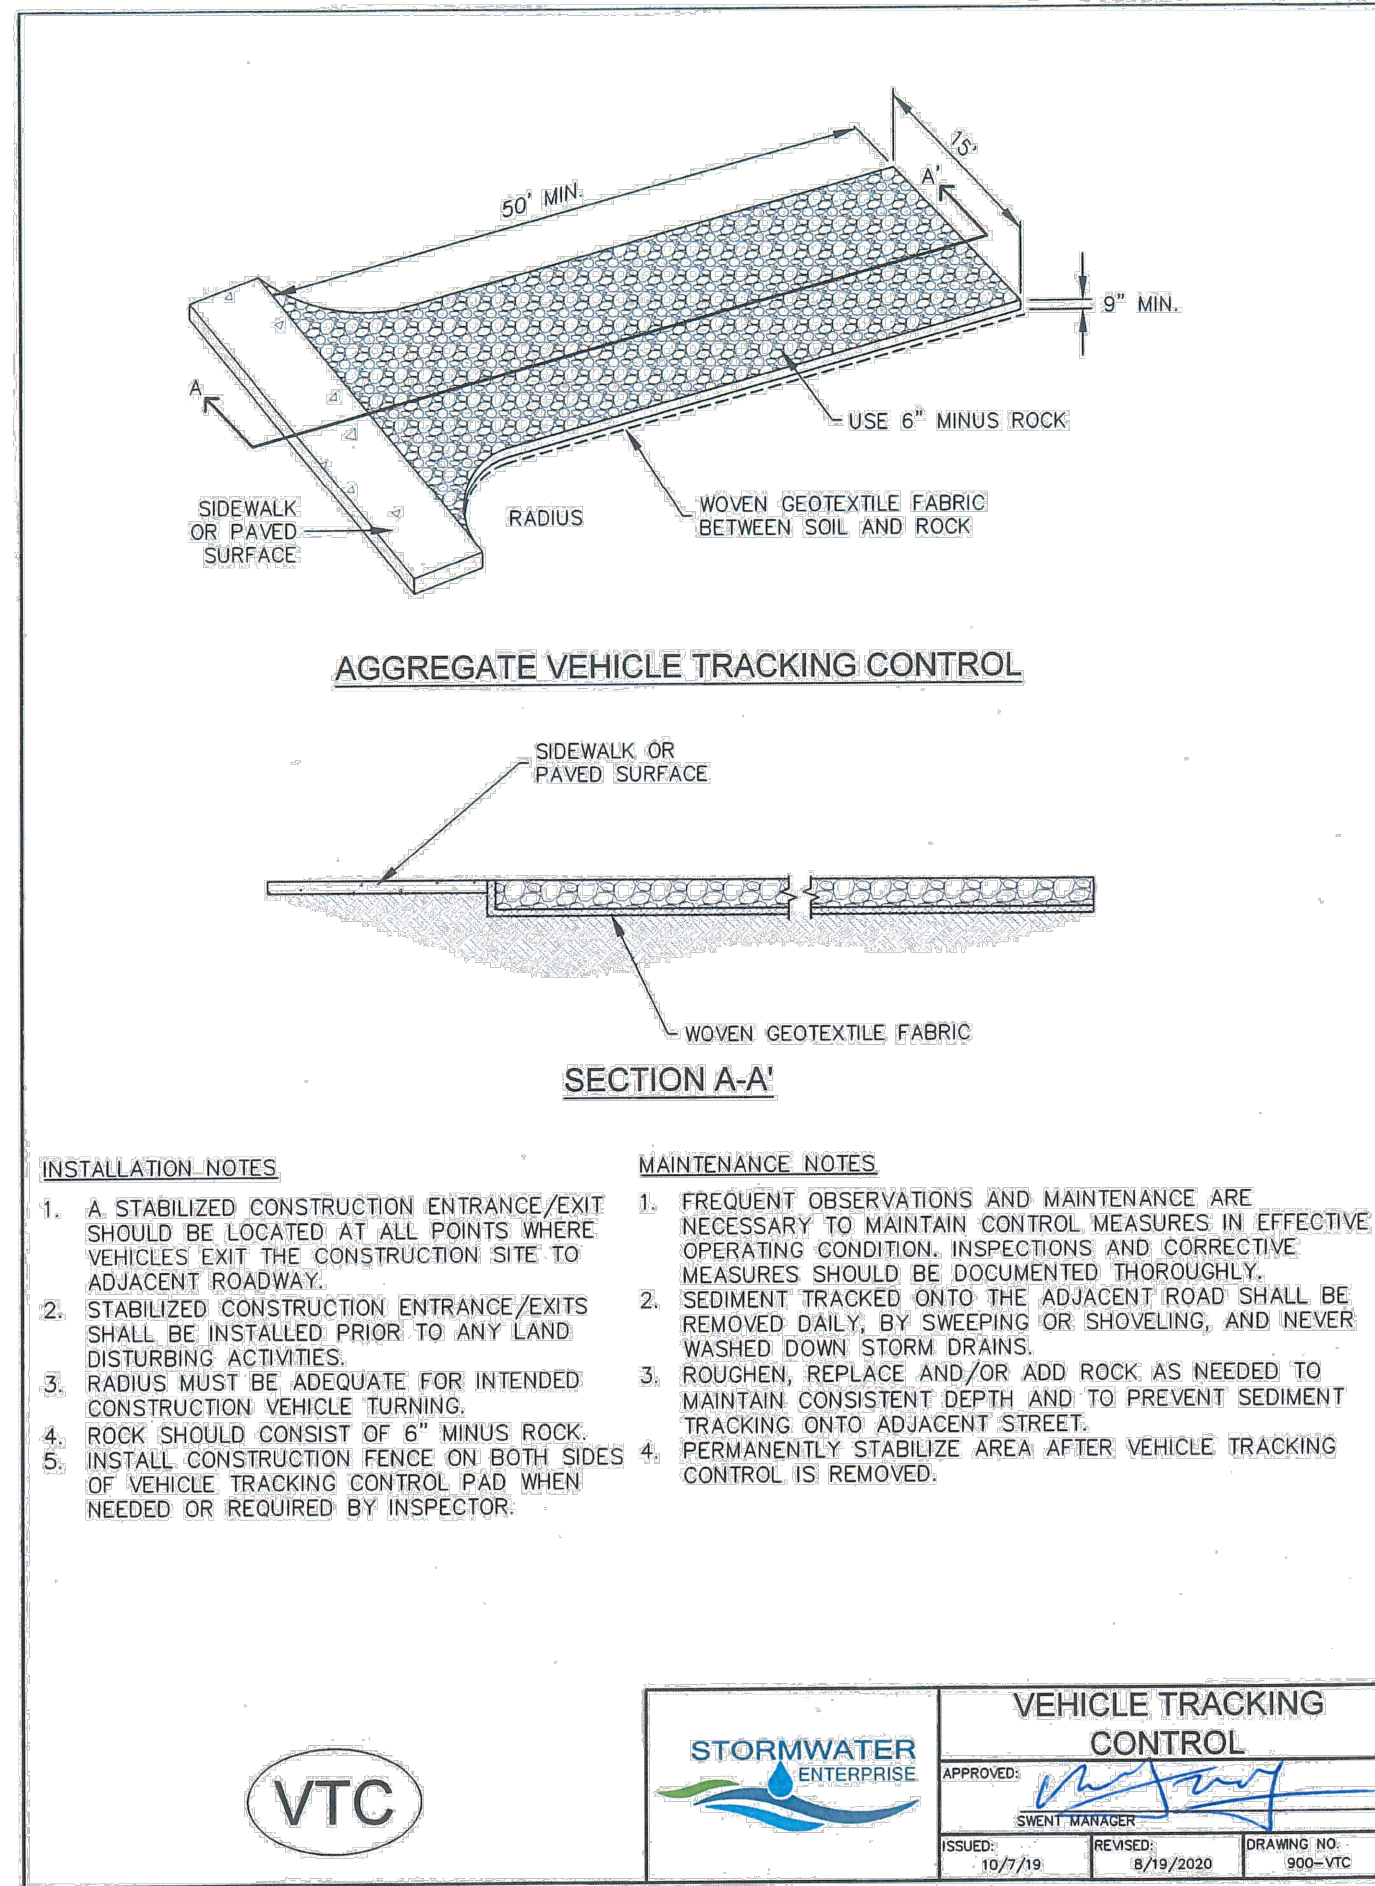


Earth Dikes and Drainage Swales (ED/DS) EC-10

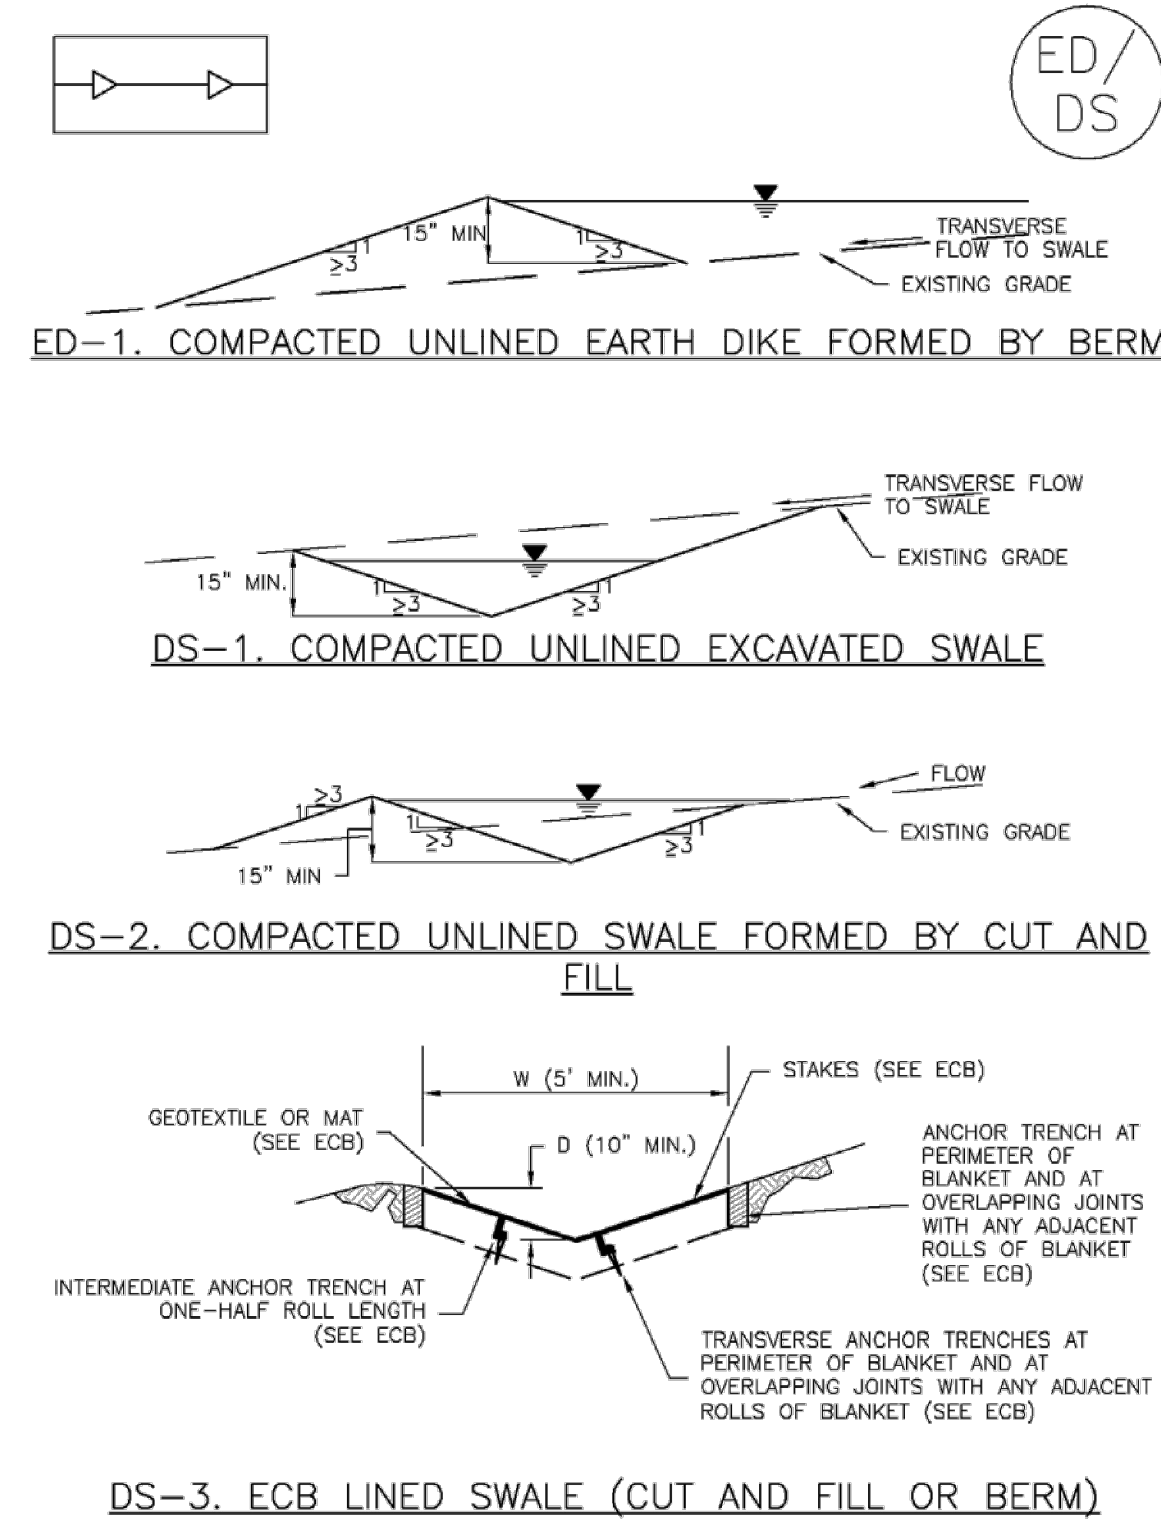

EC-10 Earth Dikes and Drainage Swales (ED/DS)

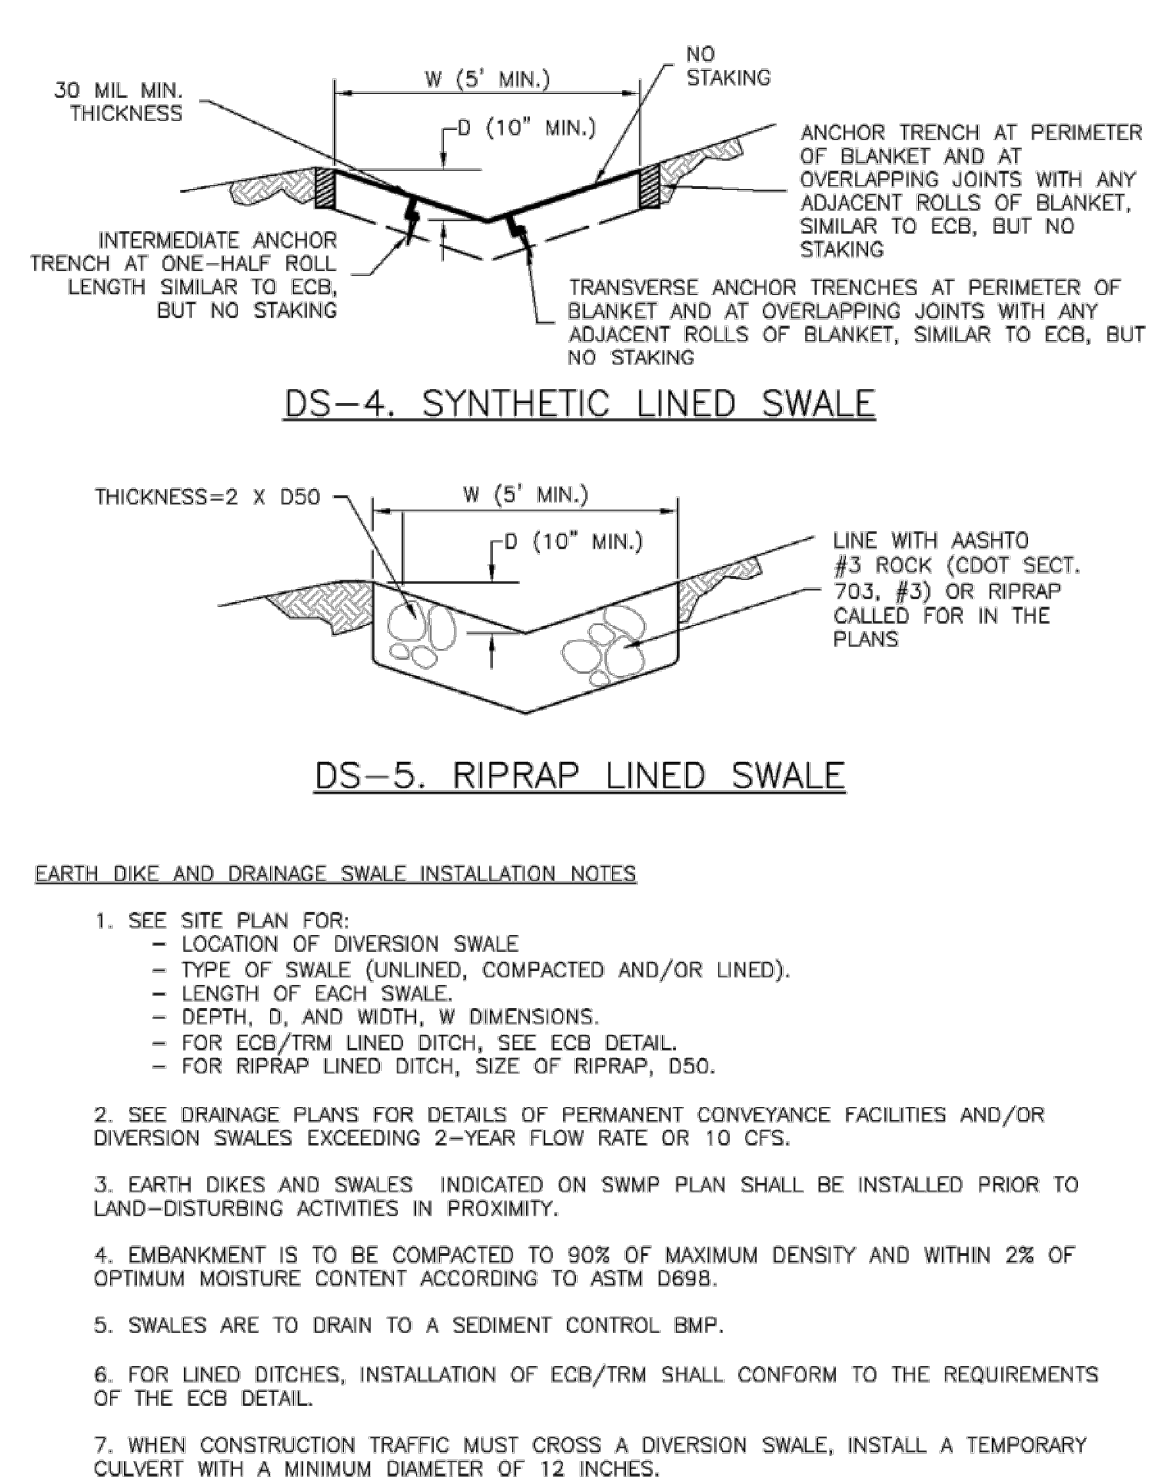

Earth Dikes and Drainage Swales (ED/DS) EC-10

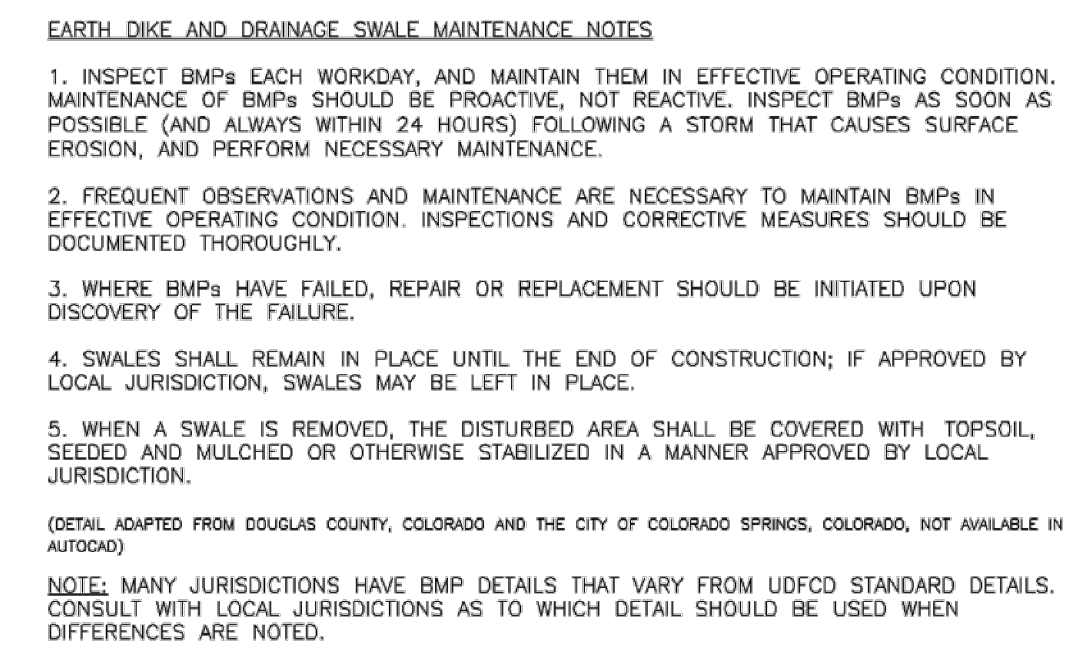

Z:\0001-Dakota Springs\02-WaterView Partners\19-08 Roy O S\CAD\plansheets\Prelim Plans\RD5 - GEC DETAILS.dwg

**VILLAS AT ASPEN TRAILS
STORMWATER MANAGEMENT PLAN (SWMP)**

APPENDIX C– EROSION AND STORMWATER QUALITY CONTROL PERMIT
