

30. COUNTY DEPARTMENT OF HEALTH AND ENVIRONMENT
INDIVIDUAL SEWAGE DISPOSAL SYSTEM INSPECTION FORM

Permit # 0N0007349

Date 10 Aug. 2006

5308000129

APPROVED: Yes ☒ No ☐ Environmental Health Specialist: J. Christensen

Address 7345 ADVENTURE WAY 80908 Owner Mountain Springs Church

Legal Description SAC 8, TOWN 135

Residence ☐ # Bedrooms ☐ Commercial ☒ System Installer Excel Excavating

SEPTIC TANK:

Commercial ☒ Noncommercial ☐ Construction Material Concrete Capacity Gallon 5000

DISPOSAL FIELD:

Trench: Depth (Range) ☐ Width ☐ Total Length ☐ Sq. Ft. ☐

Bed: Depth (Range) ☐ Length ☐ Width ☐ Sq. Ft. ☐

Depth of Rock ☐ Under PVC ☐ Type of cover on Rock ☐

DRYWELLS: # of Pits ☐ Rings (Pit 1) ☐ Rings (Pit 2) ☐ Working Depth #1 ☐ #2 ☐

Size (L x W) #1 ☐ #2 ☐ Total Sq. Ft. ☐

ROCKLESS SYSTEMS:

Standard Chamber: Type Infiltrator #Chambers 40 Sq. Ft./Chamber 15.5 Bed Trench ☒

High Profile Units: Type Chamber ☐ #Chambers ☐ Sq. Ft./Chamber ☐ Bed ☐ Trench ☐

Reduction Allowed ☐ % Sq. Ft. Required ☐ Depth (Range) ☐

Sq. Ft. Installed 744 Equivalent Sq. Ft. Installed with Reduction 1240

Engineer Design ☒ N Engineering Firm Noite



Approval letter provided? ☒ N

Well installed at time of septic system inspection? ☒ N Public Water? ☐

*Approval will be revoked if in the future the well is found to be within 50 feet of the septic tank and/or 100 feet of the disposal field.


NOTES: Sewer line for church was installed by Hoier (Dan) Excavating ph. 499-6491. Not inspected by Health Dept. Cleanouts (pipe above ground) are > 50' lengths. Entire Sewer line was covered.

E. Woodmen Rd.



Septic tank & 14' of sewer line inspected 28 Jul 06
40' of sewer line and Absorption field inspected 10 Aug. 06

2250 gallon Existing Septic Tank (To be Abandoned) Permit # 3388 Jan. 2002

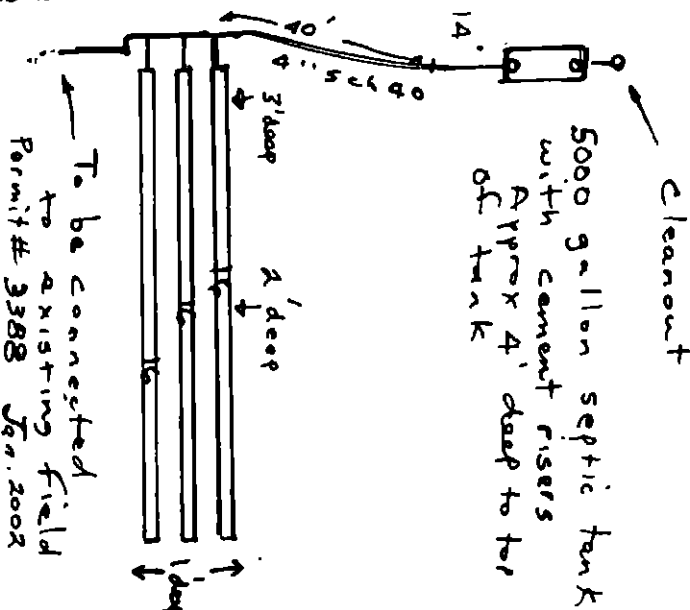

EL PASO COUNTY
DEPARTMENT OF HEALTH AND ENVIRONMENT
301 S Union Blvd, Colorado Springs, Colorado 719-575-8636

INDIVIDUAL SEWAGE DISPOSAL SYSTEM PERMIT

600

OWNER NAME: MOUNTAIN SPRINGS CHURCH
ADDRESS: 7345 E WOODMEN ROAD - *Adventure Way*
CITY, STATE, ZIP: COLORADO SPRINGS CO 80908
INSTALLED BY:

PERMIT NUMBER: ON0007349
DATE PERMITTED: 8/2/2006
PHONE NUMBER: 7194956688

This permit is issued in accordance with 25-10-107 Colorado Revised Statutes. PERMIT EXPIRES upon completion-installation of sewage-disposal system or at the end of twelve (12) months from date of issue- whichever occurs first-(unless work is in progress). If both a building and an ISDS permit are issued for the same property and construction has not commenced prior to the expiration date of the building permit, the ISDS permit shall expire at the same time as the building permit. This permit is revokable if all stated requirements are not met.

Sewage disposal system to be installed by an El Paso County Licensed System Contractor or the property owner.

THIS PERMIT DOES NOT DENOTE APPROVAL OF ZONING AND ACREAGE REQUIREMENTS.

Rosemary C. Baker-Martin

DIRECTOR, EL PASO COUNTY DEPARTMENT OF HEALTH AND ENVIRONMENT

PERMIT EXPIRATION DATE :
Expires twelve months from date of issue

Brad Wallen 578-3127
ENVIRONMENTALIST / PHONE NUMBER*

WATER SOURCE: WELL

MINIMUM SEPTIC TANK SIZE : _____ GALLONS MINIMUM ABSORPTION AREA REQUIRED _____ SQ FT

PLANNING DEPARTMENT ☒ ENUMERATION ☒ FLOOD PLAIN ☒ WASTEWATER ☒

COMMENTS:

- * FOR INSPECTIONS CALL 575-8699 BEFORE 8:30 A.M. OF THE DAY TO BE INSPECTED.
(WEEKENDS & HOLIDAYS EXCLUDED)
- LEAVE THE ENTIRE SEWAGE DISPOSAL SYSTEM UNCOVERED FOR FINAL INSPECTION.

INSTALL LEACH FIELD IN GENERAL AREA OF EXISTING LEACH FIELD ACCORDING TO ENGINEER'S DESIGN.

BACK HOE PROFILE WILL BE REQUIRED IN AREA WHERE NEW SYSTEM WILL BE INSTALLED AND VERIFIED BY ENGINEER THAT SOIL IS ACCEPTABLE, AND DEPTH OF BEDROCK OR GROUND WATER IF PRESENT.

LEACH FIELD MUST MEET THE REQUIRED SET BACKS OF 168 FEET TO WELL AND 118 FEET TO POND, WATER COURSE OR STREAM.

CLEAN OUTS MUST BE INSTALLED EVERY 50 FEET FROM BUILDING TO SEPTIC TANK.

EXISTING LINES WITH CLEAN OUTS WILL HAVE TO BE VERIFIED AT TIME OF FINAL INSPECTION.

ENGINEER APPROVAL LETTER MUST BE RECEIVED BEFORE FINAL APPROVAL CAN BE GIVEN.

The Health Office shall assume no responsibility in case of failure or inadequacy of a sewage-disposal system, beyond consulting in good faith with the property owner or representative. Free access to the property shall be authorized at reasonable time for the purpose of making such inspections as are necessary to determine compliance with requirements of this law.

FOR ADMINISTRATIVE USE ONLY

Permit Ready: *9/17/2006* Called *9/18/2006* Mailed

Final Inspection Requested: BY: *Thack - Ewell Epc* Date Called In: *8/9/06 2:04*

Phone # *330-3118* Septic Site will be ready: *now*

Inspector

Record I.D.

7349 / 600

*Call 578-8833 and Fax to

EL PASO COUNTY DEPARTMENT OF HEALTH & ENVIRONMENT

578-5650

301 South Union Boulevard • Colorado Springs, CO • 80910-3123 • (719) 575-8635 • Fax: (719) 578-3188

*ALL PAYMENTS ARE DUE AT TIME OF SUBMITTAL IN CASH OR CHECK

Justine or Kurt

APPLICATION FOR AN ON-SITE WASTEWATER TREATMENT SYSTEM PERMIT

☐ NEW CONSTRUCTION ☐ MINOR REPAIR ☒ MAJOR REPAIR/ADDOwner Mountain Springs Church Daytime Phone 719-495-6688Address of Property 7345 Woodman Rd City & Zip COS, CO 80908Legal Description The portion of Section 8, Township 13 S., Range 65 WOwner's MAILING Address 7345 Woodman Rd City, State & Zip COS, CO 80908Lot Size 17.85 Tax Schedule # 53080-00-095Type of Building: ☐ Frame ☐ Modular ☐ Mobile ☒ Commercial ☐ Manufactured ☐ OtherWater Supply: ☒ Well or Spring ☐ Cistern ☐ Public Inside City Limits: ☐ No ☐ Yes-City☐ MAIL PERMIT OR ☐ PICK UP PERMIT ☐ THERE IS AN ADDITIONAL RESIDENCE ON THIS PROPERTYMAXIMUM POTENTIAL NUMBER OF BEDROOMS 0 (Commercial)Percolation Test Attached Y ☒ N Basement Y ☒ N Garbage Disposal Y ☒ N Clothes Washer Y ☒ N

I have supplied a plot plan as described on the back of this form. I acknowledge the completeness of the application is conditional upon such further mandatory and additional tests and reports as may be required by the Department to be made and furnished by an applicant for purposes of evaluating the application, and issuance of the permit is subject to such terms and conditions as deemed necessary to ensure compliance with rules and regulations adopted pursuant to C.R.S. 25-10-107 et. seq. I hereby certify all represented to be true and correct to the best of my knowledge and belief, and are designed to be relied on by the El Paso County Department of Health and Environment in evaluating the same for purposes of issuing the permit applied for herein. I further understand any falsification or misrepresentation may result in the denial of the application or revocation of any permit granted based upon said application and in legal action for perjury as provided by law.

OWNER'S SIGNATURE

Date 7/31/06

You will be notified by telephone when your permit is ready for pick up. Please allow a minimum of 10 days for new septic.

DEPARTMENT OF HEALTH USE ONLY

- Eng Design -
Minimum Tank Capacity- Eng Design -
Minimum Absorption Area8-1-06
Date of Site Inspection

REMARKS Install Leach Field in general area of existing Leach Field according to engineer design. A backhoe profile will be required in area where new system will be installed and verified by engineer that soil is acceptable and ~~existence~~ ^{depth} of bedrock or ground water if present. Leach Field must meet the required setbacks of 168' to well and 118' FT to pond, water course or stream. Clean outs must be installed every 50' from building ~~and~~ to septic tank.

EHS INSPECTOR

Brad HallanDATE 8-2-06☒ APPROVED

DENIED

FEES AS OF 02/22/2006:

NEW CONSTRUCTION \$350.00 + Planning Department Surcharge of \$118.00. = \$468.00
 MAJOR REPAIR/ADDITION \$430.00
 MINOR REPAIR/ADDITION \$179.00

DATE TO PLANNING / WASTEWATER: _____

DATE TO FLOODPLAIN/ENUMERATIONS _____

PLEASE COMPLETE THE BACK OF THIS FORM

(Call 779) (watercourse 118') (New lines & cleanouts & existing cleanouts)

Existing lines with cleanouts will have to be verified
 at time of final inspection. Engineering letter must be received before
 final inspection can be given.

- 1) We require an original of your **PERCOLATION (PERC) TEST** with an original professional engineer's (PE) stamp and signature as well as a plot of the percolation test hole locations with measurements from a fixed reference point.
- 2) **PROPERTY ADDRESS OR LOT NUMBER MUST BE POSTED AND CLEARLY VISIBLE FROM ROAD. PERC HOLES MUST BE CLEARLY MARKED OR AN ADDITIONAL CHARGE FOR A RETURN TRIP TO THE SITE MAY BE ASSESSED.**
- 3) A **PLOT PLAN** must be drawn (not to scale) on an 8 1/2 x 11 sheet of paper. The plot plan must include:
- | | | |
|------------------------|---|---|
| 1) a north bearing | 4) all buildings (proposed or existing) | 7) driveway (proposed or existing and name of adjoining street) |
| 2) property lines | 5) proposed septic system site | |
| 3) property dimensions | 6) alternate septic system site | |
- 4) Initial any of the following features that apply to your property and **INCLUDE** them on your **PLOT PLAN**.
- | | | |
|---------------|---------------------------------|---------------------|
| _____ Well(s) | _____ Adjacent property well(s) | _____ Subsoil drain |
| _____ Cistern | _____ Water line | |
- 5) Initial any of the following that are within 100 feet of your proposed septic system and **INCLUDE** on your **PLOT PLAN**.
- | | |
|---------------------|----------------------------------|
| _____ Spring(s) | _____ Lake(s) |
| _____ Pond(s) | _____ Stream(s) |
| _____ Dry Gulch(es) | _____ Natural drainage course(s) |

6) **GIVE COMPLETE DIRECTIONS TO THE PROPERTY FROM A MAIN HIGHWAY**

Woodman East on S Side
(Bu)
