HRGreen

HRGREEN.COM

Colorado Kids Ranch – 105 Access Improvements
Stormwater Management Plan (SWMP)

October 2026

HR Green Project No: 2502599

El Paso County No. XXXX

Prepared For (Applicant/Owner):

JD Chapman

Colorado Pumpkin Patch LLC

18065 Saddlewood Road

Monument, CO 80132

(719) 799 - 6708

Prepared By:

HR Green Development, LLC

1975 Research Parkway, Ste. 160

Colorado Springs, CO 80920

Contact: Richie Lyon, PE

Richie.Lyon@hrgreen.com

719-318-0871

Designated Stormwater Manager:

TBD

GEC Administrator:

TBD

Table of Contents

Table of Contents 1
Engineer's Statement 3
I. Site Location & Description 4
II. Construction Phasing 5
III. Pre-Development Conditions and Soils 5
IV. Description of Potential Pollutants 6
V. Areas and Volumes 7
VI. Self-Inspections 8
VII. Materials Handling 9
VIII. Spill Prevention & Response Plan 10
IX. Implementation of Control Measures 11
X. Final Stabilization & Long-Term Stormwater Management Plan 13
XI. References 14

Appendices

A. Maps & Exhibits
B. GEC Plans
C. GEC Details
D. ESQCP Form
E. CDPS General Permit COR400000 Certification and Copy of the General Permit
F. CDPHE Low-Risk Discharge Guidance Documents
G. Self-Inspection Form and Spill Prevention Document
H. Other Documents and Credentials

PREPARING ENGINEER:

Name: Richie Lyon, P.E.

Company: HR Green Development, LLC

Title: Project Manager

Phone Number: (719) 318-0871

Address: 1975 Research Pkwy, Suite 160 Colorado Springs 80920

▷ PERMITEE:

Name: JD Chapman

Company: Colorado Pumpkin Patch LLC

Title: Owner/Developer

Phone Number: (719) 799-6708

Address: 18065 Saddlewood Road, Monument, CO 80132

▷ DESIGNATOR STORMWATER MANAGER

Contact: TBD

Company:.

Title:

Phone Number:

Address:

▷ GEC ADMINISTRATOR:

Contact: TBD

Company:

Title:

Phone Number:

Address:

Engineer's Statement

The Stormwater Management Plan was prepared under my direction and supervision and is correct to the best of my knowledge and belief. Said Plan has been prepared according to the criteria established by the County and State for Stormwater Management Plans.

Name: Richard D. Lyon, P.E. Date:

Phone Number: 719-318-0871

Seal

I. Site Location & Description

Location

The Colorado Kids Ranch property is located 18065 Saddlewood Road in northern El Paso County, Colorado. This report specifically analyzes improvements to County Road 105 along the northern property boundary of the Colorado Kids Ranch that are required for a permanent access permit. The site is described as a tract in the North Half of Section 16 lying east of Canterbury West, North of Saddlewood Road, and West of Canterbury East, Section 16, Township 11 South, Range 66 West of the 6th Principal Meridian, El Paso County, Colorado.

Description of Property

The Colorado Kids Ranch is a developed agritainment center on an unplatted 40.5 acre property. In September of 2023, El Paso County conditionally approved a Special Use (El Paso County Project No. AL217) allowing agritainment activities on the property with up to 325 vehicles on site, with one of the conditions being approval of the Site Development Plan in El Paso County Project Number PPR2235. In 2024, a temporary access permit was granted to the development under El Paso County Project Number AP24480. El Paso County and the TIS have identified that improvements will now be required to County Road 105 to grant permanent access to the property. A deviation request and traffic memo have been submitted to El Paso County under PCD File No. DEV261 which outlines the necessary improvements to County Road 105. This report will address the impacts and design only for the necessary infrastructure for the County Road 105 improvements.

The Colorado Kids Ranch 105 Access Improvements project has a disturbed area of 1.65 acres, and a limit of construction of 1.79 acres to include staging area, concrete washout, and culvert inlet protection outside of the limits of disturbance. The development includes the widening of County Road 105 for an additional left and right turn lane into the Colorado Kids Ranch property, and minor grading, signage, and striping improvements.

The Colorado Kids Ranch is in the West Cherry Creek Drainage Basin, and drainage from the site is tributary to an existing unnamed tributary drainage channel in the West Cherry Creek Drainage Basin. The unnamed tributary channel generally flows northeast from the project site to its convergence with West Cherry Creek.

Neighboring Areas

The surrounding developments around the Colorado Kids Ranch property include rural residential lots along the west boundary (Lots 29-35 of Canterbury West Subdivision; Zoned RR-5). The east boundary of the site adjoins developed rural residential lots (Tracts 106-112 Canterbury East Subdivision; Zoned RR-5). The south boundary of the property is Saddlewood Road, an improved gravel-paved local public roadway. The north boundary of the property is County Road 105, an improved asphalt-paved arterial public roadway.

Construction Activity

The proposed development is to only include construction of the roadway and utilities including stormwater. Construction activities include but are not limited to corridor grading, pavement installation, final stabilization of the proposed roadways and right-of-way corridors, storm sewer installation, street signage and re-striping.

Construction will begin with setting up perimeter controls which are prescribed to be silt fence along the disturbance areas, staging area and concrete washout, and installing culvert inlet protection where necessary. Following perimeter control, construction activity includes corridor grading for the roadways, roadside ditch sections, and storm pipe and drainage structure installations. Construction will be completed with final

stabilization including permanent seeding and mulch per the GEC plan set. Once final stabilization is achieved for disturbed areas, temporary erosion control measures will be removed.

Temporary stabilization measures (silt fence, staging areas, culvert inlet protection, concrete washout) will be installed prior to construction. Stabilized staging area (are shown on the GEC plans in designated areas. During construction, temporary stabilization measures, including culvert inlet protection and check dams will be utilized to control stormwater runoff.

Off-site disturbance is limited to work within the adjacent private parcel at the southwest end of the development. This area will include temporary grading and permanent stabilization and requires coordination with the adjacent property owner.

II. Construction Phasing

Phasing and Sequence Schedule

The proposed sequence of major construction activities and Construction Control Measures for the project as are follows:

1. Install SSA, CWA, SF and other perimeter erosion and stormwater control measures (i.e. silt fence, construction fence etc.) (Spring of 2027)
2. Install Inlet Protection control measures (Spring of 2027)
3. Clear, grub and grade site for improvements. (Spring of 2027)
4. Excavate and install improvements including underground piping and drainage structures. Install storm sewer and TRM per GEC plans. (Spring of 2027)
5. Landscaping, restoration and final stabilization. Ensure final stabilization achieved prior to site closure. (Summer 2027)
6. Remove construction BMPs (Summer 2027)

Construction Documentation

Construction drawings are provided with this document showing the Grading and Erosion Control plan for this project and are intended to be a “living” document used by the SWMP Manager to document construction activities. See ***Appendix G*** for record log.

III. Pre-Development Conditions and Soils

Floodplain

Per FEMA FIRM 08041C0285G (eff. 12/7/2018), there is a FEMA flood zone A at the eastern end of this project for an unnamed tributary. This project will have disturbance within the FEMA flood zone A. A “less than 6” rise” analysis and certification as required by the El Paso County floodplain administrator has been completed as part of this report. A floodplain development permit is also required for disturbance within the zone A floodplain.

Existing Vegetation

Ground cover within the project area consists of paved roadway and gravel shoulders for County Road 105, and existing native grasses and weeds outside of the roadway area. The existing vegetative cover is 90 percent, based on field observations and aerial imagery. The existing vegetation includes native grasses and weeds, shrubs, and pine trees.

Existing Drainage Patterns

The Colorado Kids Ranch is in the West Cherry Creek Drainage Basin, and drainage from the site is tributary to an existing unnamed tributary drainage channel in the West Cherry Creek Drainage Basin. The unnamed tributary channel generally flows northeast from the project site to its convergence with West Cherry Creek.

Drainage generally flows from the southwest to the northeast across the site. There is an existing public quad 36" CMP storm sewer culvert underneath County Road 105 near the eastern limits of this project. This culvert flows for the unnamed tributary which has a FEMA flood zone A association to it.

Existing Slopes

Slopes range from 1% to 33% with a maximum elevation of 7375' and a minimum elevation of 7310'.

Soils

According to the US Department of Agriculture Natural Resources Conservation Service Soil Survey of El Paso County, Colorado, the primary soils through the filing area are Tomah-Crowfoot Loamy Sands and Ustic Torrifluvents, Loamy. These soil types within the filing are within Hydrologic Soil Group B. Runoff coefficients for this study were selected based on "A/B" type soils. A copy of the soil map for the site can be found in ***Appendix A***.

The existing soil types have a low to moderate potential for erosion based on the soil K factor of 0.17. Erosion factor K indicates the susceptibility of a soil to sheet and rill erosion by water. Values of K range from 0.02 to 0.69; other factors being equal, the higher the value, the more susceptible the soil is to sheet and rill erosion by water. The potential for erosion can be mitigated by employing appropriate downstream construction control measures before/during/after construction to limit potential impacts to stormwater discharges. The potential impacts are sediment discharge into the existing stormwater conveyance system and drainageway.

IV. Description of Potential Pollutants

Potential sources of sediment to stormwater runoff include earth moving and concrete/asphalt activities associated with roadway improvement.

Potential pollutants and sources other than sediment to stormwater runoff include trash, debris, fueling and equipment failure. Materials of significance stored on the project site include: sediment, concrete washout, cement, trash & debris, fuels and oils.

Discharge of concrete wash water to ground within the contained concrete washout area is an allowable non-stormwater discharge per the COR400000 Permit if properly identified in the Stormwater Management Plan and if the appropriate control measures are implemented.

There are no other non-stormwater discharge anticipated from the site.

Construction activities can produce a variety of pollutants that can potentially cause stormwater contamination. Grading activities remove rocks, vegetation and other erosion controlling surfaces and can result int he exposure of underlying soil to the elements, which can then be displaced into water sources.

Wind and erosion and vehicular transport can produce sediment debris.

Potential Sources of Pollution:

1. Potential sources of pollution from construction activities include
    a. Disturbed or stored soils
    b. Vehicle tracking of sediment
    c. Loading & unloading operations
    d. Outdoor Storage activities
    e. Vehicle and Equipment Maintenance/Fueling
    f. Dust or Particulate Generating Processes
    g. Routine maintenance activities involving fertilizers, pesticides, detergents, fuels, solvents etc.
    h. On-site waste management (waste piles, liquid wastes, dumpsters)
    i. Concrete truck/equipment washing (washing truck chute and associated fixtures)
    j. Non-industrial waste (worker trash and portable toilets)

V. Areas and Volumes

The limit of disturbance is 1.65 acres and limits of construction is 1.78 acres per the Grading and Erosion Control Plan for improvements such as roadways, stormwater infrastructure, and daylight grading from the right-of-way. The final construction phase shows a limit of disturbance and construction that encompasses the full development.

Below are roadway construction earthwork figures. These numbers are adjusted using a fill factor of 1.15.

Roadway Construction Phase:

Earthwork Analysis with 15% Compaction Factor

Cut Quantity (adjusted) : 915.82 cubic yards

Fill Quantity (adjusted): 2,447.45 cubic yards

Net (adjusted): 1,531.62 cubic yards FILL

*This analysis is to finished grade and does not include the pavement thickness of the roadways

Earthwork Analysis with no Compaction Factor

Cut Quantity (unadjusted) : 915.82 cubic yards

Fill Quantity (unadjusted): 2,128.22 cubic yards

Net (unadjusted): 1,212.39 cubic yards FILL

*This analysis is to finished grade and does not include the pavement thickness of the roadways

VI. Self-Inspections

Self-inspections of the Construction Control Measures must be completed by the certified GEC Administrator. The below provides the minimum to satisfy the El Paso County self-inspection requirements. A more frequent self-inspection schedule may be required to ensure Control Measures are operating in compliance with the approved GEC plan.

1. Inspection Schedules:
    a. The GEC Administrator shall make a thorough inspection of the Control Measures:
        i. At least once every fourteen (14) calendar days.
        ii. Within 24 hours following any precipitation event (i.e. rain, snow, hail etc.) that causes surface erosion.
            - Alternatively, the GEC Administrator can perform a thorough inspection of the Control Measures once every seven (7) days and forego post-precipitation inspections.
    b. For sites where construction activities have completed and final stabilization measures installed but final stabilization has not yet been achieved, the GEC Administrator shall make a thorough inspection of the Control Measures:
        i. At least once every month
        ii. Within 72 hours following any precipitation event that causes surface erosion
2. Inspection Procedures:
    a. Site Inspection & Observation Items:
        i. Limits of disturbance perimeter and stormwater discharge points
        ii. All disturbed areas to ensure necessary Construction Control Measures are in place to control potential stormwater runoff.
        iii. Areas used for material/waste storage.
        iv. Any areas having a signification potential for storm water pollution (i.e site entrances, concrete washout areas etc.)
        v. All Construction Control Measures identified on the GEC plans.
    b. Inspection Requirements:
        i. Determine any locations, or potential locations, where pollutants and stormwater may be exiting the site/entering the receiving waters.
        ii. Evaluate Construction Control measures and determine if they are constructed in accordance with the latest revision of the approved GEC plan and operating effectively.
        iii. Provide recommendations for the need of additional Construction Control measures and the maintenance of existing measures in disrepair to ensure complication with the El Paso County Stormwater Construction Manual.
    c. Construction Control Measure Maintenance/Replacement:
        i. The GEC administrator shall ensure sediment has been removed from perimeter controls and relocated to an area without the potential for sediment to discharge from the site
        ii. The GEC administrator shall ensure diversion ditches and temporary sediment ponds have not accumulated excess sediment that impedes their functionality.
        iii. The GEC administrator shall ensure that failed Control Measures are repaired/reinstalled within three (3) calendar days, according to the El Paso County Stormwater Control

Measure details, to ensure pollutants and/or sediment do not discharge from the site. GEC details are provided in ***Appendix C***.

d. Documentation:
    i. Update the GEC plan to document the installation/revision of Control Measures
    ii. Identify Control Measure deficiencies and that noncompliance is resolved within three (3) calendar days.
    iii. Identify Self-Inspection schedule in most recent inspection form
    iv. Complete and submit Self-Inspection forms to the El Paso County within five (5) business days of the completed inspection
    v. Ensure Self-Inspections are available, either physically or electronically, throughout the duration of the project
    vi. Self-Inspection Repost shall contain at least the following:
        - Inspection Date
        - Name and title of the GEC Administrator performing inspection
        - Location(s) of illicit discharges of stormwater, sediment or pollutants from the site
        - Location(s) of Construction Control Measures in need of maintenance/repair
        - Location(s) of Construction Control Measures that failed to operate as designed or proved inadequate
        - Location(s) of additional Construction Control Measures not shown on the latest, approved revision of the GEC plan
        - Any deviations from the minimum inspection schedule
        - Signature of GEC Administrator

VII. Materials Handling

1. General Materials Handling Practices:
    a. Potential pollutants shall be stored and used in a manner consistent with the manufacturer's instructions in a secure location. To the extent practical, material storage areas should be located away from storm drain inlets and should be equipped with covers, roofs or secondary containment as required to prevent stormwater from contacting stored materials. Chemicals that are not compatible shall be stored in segregated areas so that spill materials cannot combine and react.
    b. Disposal of materials shall be in accordance with the manufacturer's instructions and applicable local, state, and federal regulations.
    c. Materials no longer required for construction shall be removed from the site as soon as possible.
    d. Adequate garbage, construction waste, and sanitary waste handling and disposal facilities shall be provided as necessary to keep the site clear of obstruction and Control Measures clear and functional.
2. Specific Materials Handling Practices:
    a. All pollutants, including waste materials and demolition debris, that occur onsite during construction shall be handled in a way that does not contaminate stormwater.
    b. All chemicals including liquid products, petroleum products, water treatment chemicals, and wastes stored onsite shall be covered and protected from vandalism.
    c. Maintenance, fueling, and repair of all equipment and vehicles involving oil changes, hydraulic system drain down, degreasing operation, fuel tank drain down and removal, and other activities

which may result in the accidental release of contaminants, shall be conducted under cover during wet weather and on an impervious surface to prevent release of contaminants onto the ground. Materials spilled during maintenance operations shall be cleaned up immediately and properly disposed of.

d. Wheel wash water shall be settled and discharged onsite by infiltration.
e. Application of agricultural chemicals, including fertilizers and pesticides, shall be conducted in a manner and at application rates that will not result in loss of chemical to stormwater runoff. Follow manufacturer's recommendations for application rates and procedures.
f. pH-modifying sources shall be managed to prevent contamination of runoff and stormwater collected onsite. The most common sources of pH-modifying materials are bulk cement, cement kiln dust (CKD), fly ash, new concrete washing and curing waters, waste streams generated from concrete grinding and sawing, exposed aggregate processes, and concrete pumping and mixer washout waters.

VIII. Spill Prevention & Response Plan

1. The primary objective in responding to a spill is to quickly contain the material and prevent or minimize their mitigation into stormwater runoff and conveyance systems. If the release has impacted onsite stormwater, it is critical to contain the released materials onsite and prevent their release into receiving waters.
2. Spill Response Procedures:
    a. Notify site superintendent immediately when a spill, or the threat of a spill, is observed. The superintendent shall assess the situation and determine the appropriate response.
    b. If spills represent an imminent threat of escaping onsite facilities and entering the receiving waters, site personnel shall respond immediately to contain the release and notify the superintendent once the situation has stabilized.
    c. The site superintendent shall be responsible for completing a spill reporting form and for reporting the spill to the appropriate agency.
    d. Spill response equipment shall be inspected and maintained as necessary to replace any materials used in spill response activities.
3. Spill kits shall be on-hand at all fueling sites. Spill kit locations shall be reported to the GEC administrator.
4. Absorbent materials shall be on-hand at all fueling areas for use in containing advertent spills. Containers shall be on-hand at all fueling sites for disposal of used absorbents.
5. Recommended components of spill kits include the following:
    a. Oil absorbent pads
    b. Oil absorbent booms
    c. 55-gallon drums
    d. 9-mil plastic bags
    e. Personal protective equipment including gloves and goggles
6. Concrete wash water: unless confined in a pre-defined, bermed containment area, the cleaning of concrete truck delivery chutes is prohibited at the job site.
7. Notification procedures:
    a. In the event of an accident or spill, the GEC administrator shall be notified.

b. Depending on the nature of the spill and material involved, the Colorado Department of Public Health and Environment, downstream water users, or other agencies may also need to be notified.
c. Any spill of oil which 1) violates water quality standards, 2) produces a "sheen" on a surface water, or 3) causes a sludge or emulsion, or any hazardous substance release, or hazardous waste release which exceeds the reportable quantity, must be reported immediately by telephone to the National Response Center Hotline at (800) 424-8802.

There are no dedicated batch plants proposed as a part of this project and therefore are not a source of pollution requiring spill prevention and response.

IX. Implementation of Control Measures

Stormwater control measures must be installed according to El Paso County design specifications, presented in ***Appendix C***, and the approved Grading and Erosion Control plan this report supports. Within the context of this SWMP's construction activities the following control measures, at a minimum, are required:

- Perimeter Silt Fence
  - Silt fence is to be installed at the initial construction phase at the perimeter of the project to prevent sediment runoff offsite from the project disturbance area. While disturbance for roadway construction may be more central to the project construction area, the silt fence acts as a barrier for downstream sediment from the disturbed area and may remain in place for private lot construction.
- Vehicle Tracking Control
  - Vehicle Tracking Control is required for the ingress/egress areas of the project for large construction vehicles to access the site with minimal disturbance to existing infrastructure and pavement. The VTC also assists in debris removal from vehicles prior to exit of the site. The control measure is to be installed at the initial construction phase
- Stabilized Staging Area
  - A designated stabilized staging area is required for equipment staging at the initial construction phase. This area is to be sufficient in size and relatively flat to prevent erosion and sediment runoff when handling materials and maneuvering vehicles. Perimeter controls of the SSA are recommended as localized erosion and sediment control of this area.
- Stockpile Management
  - A designated stockpile area is required for dirt and debris containment at the initial construction phase. This area is to have perimeter controls for localized erosion and sediment control. Frequent export haul is recommended to maintain a minimal stockpile size and minimize sediment runoff during rain events during construction activities.
- Inlet Protection
  - Inlet protection is to be installed to prevent sediment runoff from entering storm systems and allow present and future stormwater conveyance as designed. Inlet protection is to remain in place until permanent stabilization is completed. Any sediment identified in inlets and storm pipes is to be removed prior to inspection and/or final permanent stabilization. Frequent inspection and maintenance of the inlet protection is to take place to ensure that wear and tear of the control measure has not taken place.
- Temporary Outlet Protection

  - Temporary outlet protection is to be installed at the initial construction phase and as outlet pipes are installed to prevent sediment runoff from entering storm systems and allow present and future stormwater conveyance as designed. Culvert protection is to remain in place until permanent stabilization is completed. Any sediment identified in inlets and storm pipes is to be removed prior to inspection and/or final permanent stabilization. Frequent inspection and maintenance of the culvert inlet protection is to take place to ensure that wear and tear of the control measure has not taken place.
- Erosion Control Blanket
  - Erosion Control Blanket is to be installed on disturbed slopes of 3:1 or greater to stabilize these areas for permanent stabilization in future construction phases. The erosion control blanket remains in place from the time of disturbance and establishment of the slope in perpetuity as natural degradation of the control measure will occur over time. Any disturbance of the blanket itself requires replacement to ensure stabilization of the slope.
- Diversion Ditches (Earth Dikes & Drainage Swales)
  - Diversion Ditches proposed within this project scope include drainage swales that outfall to temporary sediment basins. The drainage swales are to be maintained throughout the initial construction phase to ensure that tributary areas that the temporary sediment basins are designed for are captured during rain events.
- Temporary Sediment Basins
  - A Temporary Sediment Basin is to be constructed at the initial construction phase for stormwater attenuation during the initial construction phase which includes earthwork disturbance and results in sediment runoff. The TSB is designed to capture sediment runoff during this phase to minimize sediment runoff directly offsite.
- Seeding & Mulching
  - Seeding and mulching is proposed as a temporary construction phase control measure for slope stabilization and restoration of disturbed areas to remain pervious areas. Permanent seeding and mulching is included in the final construction phase as a permanent stabilization method to stabilize disturbed areas and provide vegetation.
- Rock Socks
  - Rock socks are to be installed in curb and gutter urban roadway sections along flowlines as shown on the GEC. The rocks socks assist in mitigating sediment runoff within paved curb and gutter sections where earthwork disturbance erosion and sediment runoff can be conveyed downstream to inlets and stormwater infrastructure. Rock socks are to be inspected and maintained as needed. Cleaning of rock socks is to occur as needed to dispose of sediment build up during construction activities.
- Concrete Washout Areas
  - Concrete Washout Areas are to be established at the initial construction phase as designated concrete washouts per MHFD details. The designated CWA’s are to be monitored to ensure that effluent does not overflow or drain out of the excavation. Removal of materials is to take place prior to deconstruction and fill of the CWA.

Additional control measures may be required at the discretion of the County Stormwater Inspector.

Stormwater pollutant control measures for waste disposal and off-site soil tracking are to follow the State's CDPHE Brochure instructions and guidelines. Site specific off-site soil tracking is to be mitigated via Vehicle Tracking Control measures and daily project site street sweeping. Perimeter control measures are to be inspected and maintained as required to reduce sediment runoff.

X. Final Stabilization & Long-Term Stormwater Management Plan

1. Temporary seeding and mulching will be installed to provide interim stabilization prior to final landscaping installation (Refer to approved Landscape Plan). Final stabilization will be achieved at time of final landscaping. See approved landscaping plans for final stabilization details. Final stabilization is met when 70% of pre disturbance levels, not including noxious weeds, are stabilized. Final stabilization must be achieved prior to removal of temporary stormwater control measures. Anticipated date of final stabilization is Summer of 2027; however, this is subject to change. Long term stormwater management is not required for this disturbance. See below for seeding and mulching details:
    a. Prior to seeding, fill any eroded rills and gullies with topsoil.
    b. Ensure all areas are seeded and mulched per the County Stormwater Construction Manual.
    c. Continue monthly self-inspections of final stabilization methods and the stormwater management system to ensure proper function. If repairs are needed, reseed and re-mulch as needed.
    d. Control noxious weeds in a manner acceptable to the GEC inspector.
    e. Seed Mix: See ***Appendix C*** for approved seed mixes.
    f. Seeding Requirements:
        i. Drill seed whenever possible, seed depth must be 1/3 to ½ inch when drill-seeding. Cross drilling should be used whenever possible with the seed divided between the two operations. The second drilling should be perpendicular to the first.
        ii. When drill seeding is not possible or on slopes greater than 3:1, hydro-seeding with tackifier may be substituted at the discretion of the GEC inspector. Hydro-seeding must be lightly raked into soil. Seeding rates are presented in ***Appendix C***.
        iii. All seeded areas must be mulched.
    g. Mulching Requirements:
        i. Mulching shall be completed as soon as practical after seeding but no more than fourteen (14) days after planting. Erosion control blanket can be used in place of the below mulching methods.
        ii. Hay or straw mulch:
            1. Only certified weed-free and certified-seed free mulch may be used. Must be applied at 2 tons/acre and adequately secured.
            2. Crimping shall not be used no slopes greater than 3:1, tackifier must be used in place.
        iii. Hydraulic mulching:
            1. Allowable on steep slopes or areas with limited access
            2. If hydro-seeding is used, mulching must be applied secondly.
            3. Wood cellulose fibers mixed with water must be applied at a rate of 2,000-2,500 lbs/acre, and tackifier applied at a rate of 100 lbs/acre.

2. The project control measures are to be owned and maintained by the Developer or their assigns (General Contractor, GEC Administrator).
3. This Stormwater Management Plan Report is a living document that is to be continuously reviewed and modified as part of the overall process of evaluating and managing stormwater quality issues at the site. The Qualified Stormwater Manager shall amend the SWMP when there is a change in design, construction, or operations and maintenance of the site which would require the implementation of new or revised control measures or if the SWMP proves to be ineffective in achieving the general objectives of controlling pollutants in stormwater discharges associated with the construction activity when control measures are no longer necessary and are removed.


XI. References

El Paso County – Drainage Criteria Manual, latest revision October 31, 2018

El Paso County – Engineering Criteria Manual, latest revision October 14, 2020

Mile High Flood District Urban Storm Drainage Criteria Manual Volumes 1, 2, and 3; latest revisions

APPENDIX A – MAPS & EXHIBITS

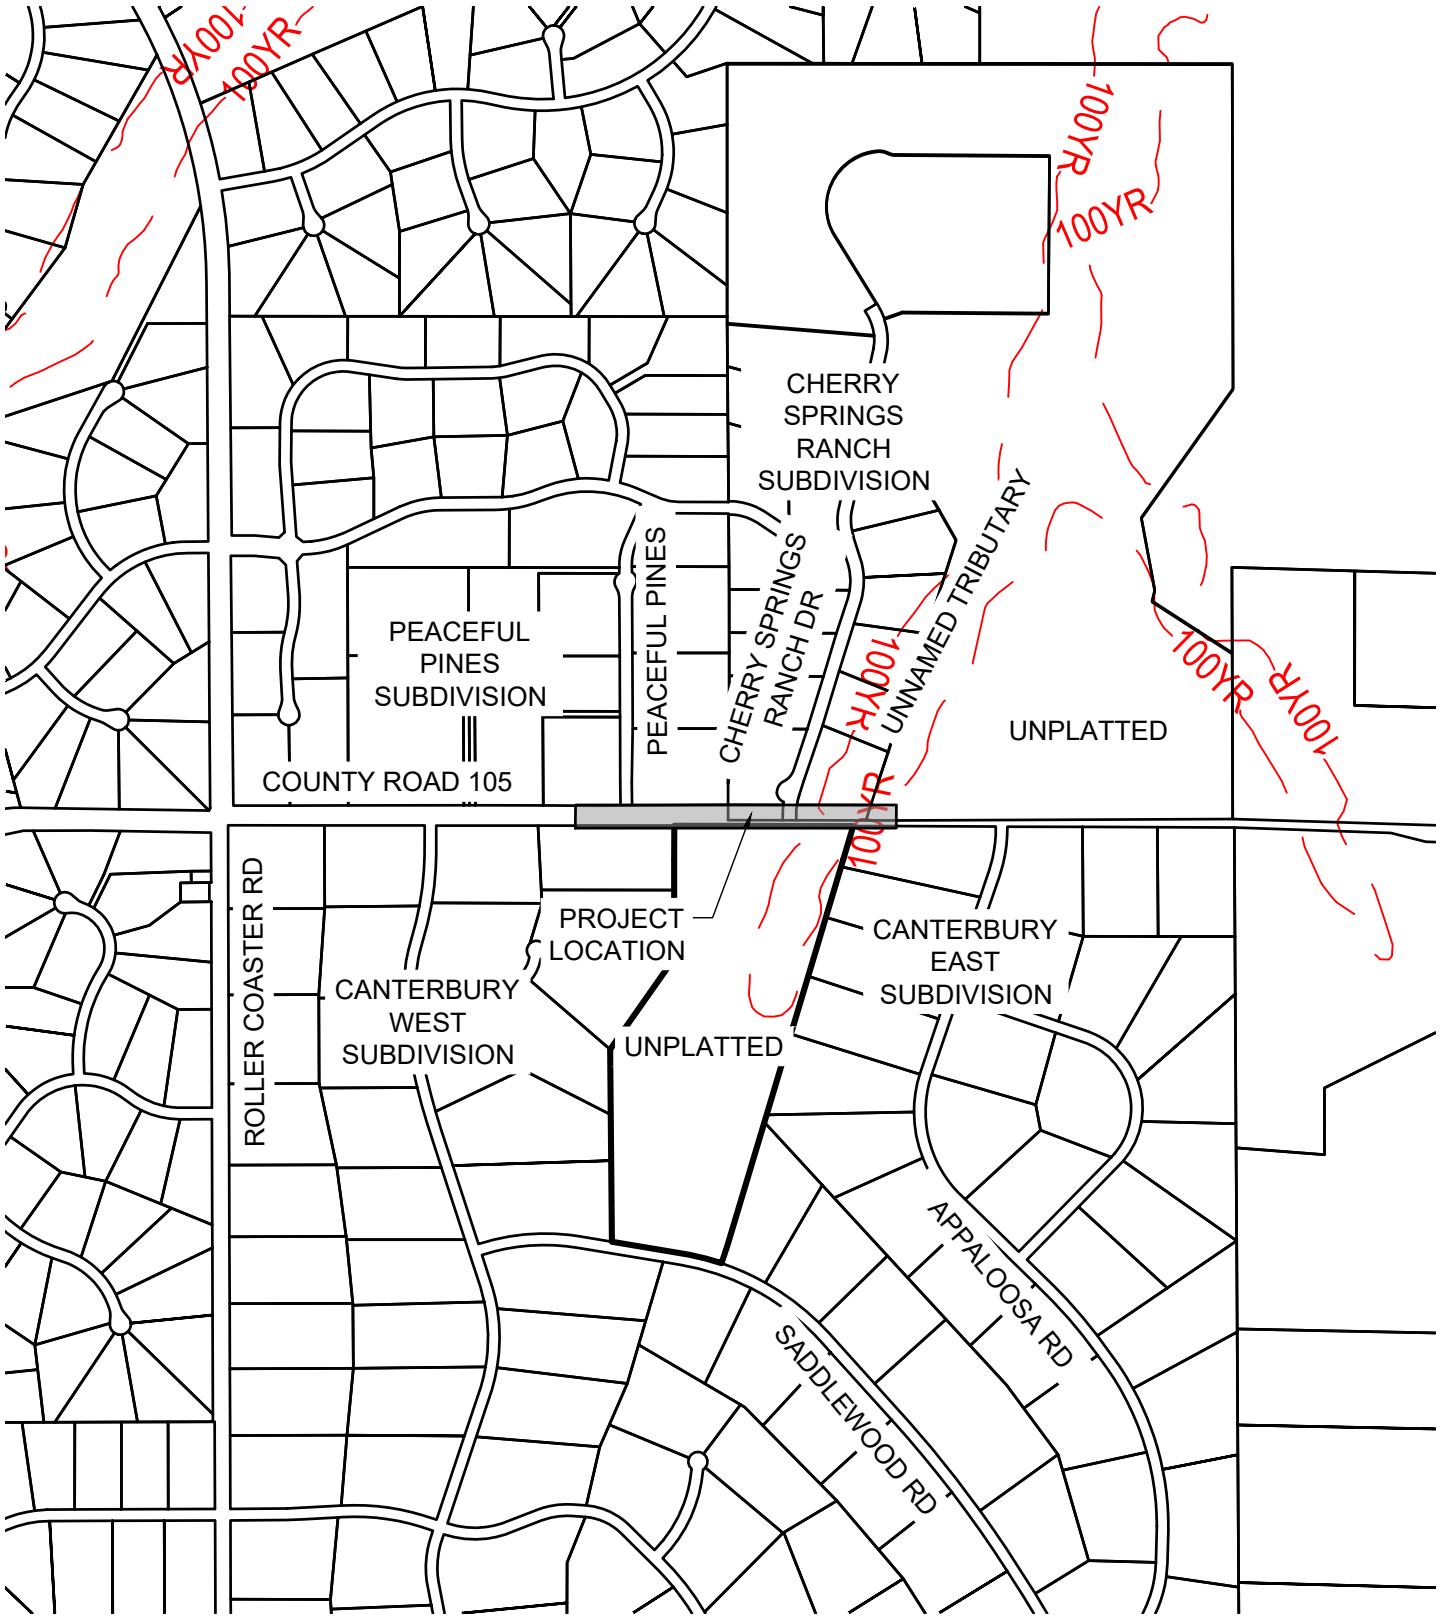

HRGreen

HRGreen.com

COLORADO KIDS RANCH 105 IMPROVEMENTS

VICINITY MAP

NORTH

SHEET

V–1

SCALE: 1"=1000'

DATE: 10/12/26

Xrefs: 8.5x11_Titleblock; xv–flood–3197; xv–row–3197; xc–dsgn–3197

NOTES TO USERS

This map is for use in administering the National Flood Insurance Program. It does not necessarily identify all areas subject to flooding, particularly from local drainage sources of small size. The **community map repository** should be consulted for possible updated or additional flood hazard information.

To obtain more detailed information in areas where **Base Flood Elevations** (BFEs) and/or **floodways** have been determined, users are encouraged to consult the Flood Profiles and Floodway Data and/or Summary of Stillwater Elevations tables contained within the Flood Insurance Study (FIS) report that accompanies this FIRM. Users should be aware that BFEs shown on the FIRM represent rounded whole-foot elevations. These BFEs are intended for flood insurance rating purposes only and should not be used as the sole source of flood elevation information. Accordingly, flood elevation data presented in the FIS report should be utilized in conjunction with the FIRM for purposes of construction and/or floodplain management.

Coastal Base Flood Elevations shown on this map apply only landward of 0.0' North American Vertical Datum of 1988 (NAVD88). Users of this FIRM should be aware that coastal flood elevations are also provided in the Summary of Stillwater Elevations table in the Flood Insurance Study report for this jurisdiction. Elevations shown in the Summary of Stillwater Elevations table should be used for construction and/or floodplain management purposes when they are higher than the elevations shown on this FIRM.

Boundaries of the **floodways** were computed at cross sections and interpolated between cross sections. The floodways were based on hydraulic considerations with regard to requirements of the National Flood Insurance Program. Floodway widths and other pertinent floodway data are provided in the Flood Insurance Study report for this jurisdiction.

Certain areas not in Special Flood Hazard Areas may be protected by **flood control structures**. Refer to section 2.4 "Flood Protection Measures" of the Flood Insurance Study report for information on flood control structures for this jurisdiction.

The **projection** used in the preparation of this map was Universal Transverse Mercator (UTM) zone 13. The **horizontal datum** was NAD83, GRS80 spheroid. Differences in datum, spheroid, projection or UTM zones zones used in the production of FIRMs for adjacent jurisdictions may result in slight positional differences in map features across jurisdiction boundaries. These differences do not affect the accuracy of this FIRM.

Flood elevations on this map are referenced to the **North American Vertical Datum of 1988 (NAVD88)**. These flood elevations must be compared to structure and ground elevations referenced to the same **vertical datum**. For information regarding conversion between the National Geodetic Vertical Datum of 1929 and the North American Vertical Datum of 1988, visit the National Geodetic Survey website at http://www.ngs.noaa.gov/ or contact the National Geodetic Survey at the following address:

NGS Information Services
NOAA, N/NGS12
National Geodetic Survey
SSMC-3, #9202
1315 East-West Highway
Silver Spring, MD 20910-3282

To obtain current elevation, description, and/or location information for **bench marks** shown on this map, please contact the Information Services Branch of the National Geodetic Survey at (301) 713-3242 or visit its website at http://www.ngs.noaa.gov/.

Base Map information shown on this FIRM was provided in digital format by El Paso County, Colorado Springs Utilities, City of Fountain, Bureau of Land Management, National Oceanic and Atmospheric Administration, United States Geological Survey, and Anderson Consulting Engineers, Inc. These data are current as of 2006.

This map reflects more detailed and up-to-date **stream channel configurations and floodplain delineations** than those shown on the previous FIRM for this jurisdiction. The floodplains and floodways that were transferred from the previous FIRM may have been adjusted to conform to these new stream channel configurations. As a result, the Flood Profiles and Floodway Data tables in the Flood Insurance Study Report (which contains authoritative hydraulic data) may reflect stream channel distances that differ from what is shown on this map. The profile baselines depicted on this map represent the hydraulic modeling baselines that match the flood profiles and Floodway Data Tables if applicable, in the FIS report. As a result, the profile baselines may deviate significantly from the new base map channel representation and may appear outside of the floodplain.

Corporate limits shown on this map are based on the best data available at the time of publication. Because changes due to annexations or de-annexations may have occurred after this map was published, map users should contact appropriate community officials to verify current corporate limit locations.

Please refer to the separately printed **Map Index** for an overview map of the county showing the layout of map panels; community map repository addresses; and a Listing of Communities table containing National Flood Insurance Program dates for each community as well as a listing of the panels on which each community is located.


Contact **FEMA Map Service Center** (MSC) via the FEMA Map Information eXchange (FMIX) 1-877-336-2627 for information on available products associated with this FIRM. Available products may include previously issued Letters of Map Change, a Flood Insurance Study Report, and/or digital versions of this map. The MSC may also be reached by Fax at 1-800-358-9620 and its website at http://www.msc.fema.gov/.

If you have **questions about this map** or questions concerning the National Flood Insurance Program in general, please call **1-877-FEMA MAP** (1-877-336-2627) or visit the FEMA website at http://www.fema.gov/business/nfip.

El Paso County Vertical Datum Offset Table


Flooding Source	Vertical Datum Offset (ft)
REFER TO SECTION 3.3 OF THE EL PASO COUNTY FLOOD INSURANCE STUDY FOR STREAM BY STREAM VERTICAL DATUM CONVERSION INFORMATION	

Panel Location Map



This Digital Flood Insurance Rate Map (DFIRM) was produced through a Cooperating Technical Partner (CTP) agreement between the State of Colorado Water Conservation Board (CWCB) and the Federal Emergency Management Agency (FEMA).

Additional Flood Hazard information and resources are available from local communities and the Colorado Water Conservation Board.

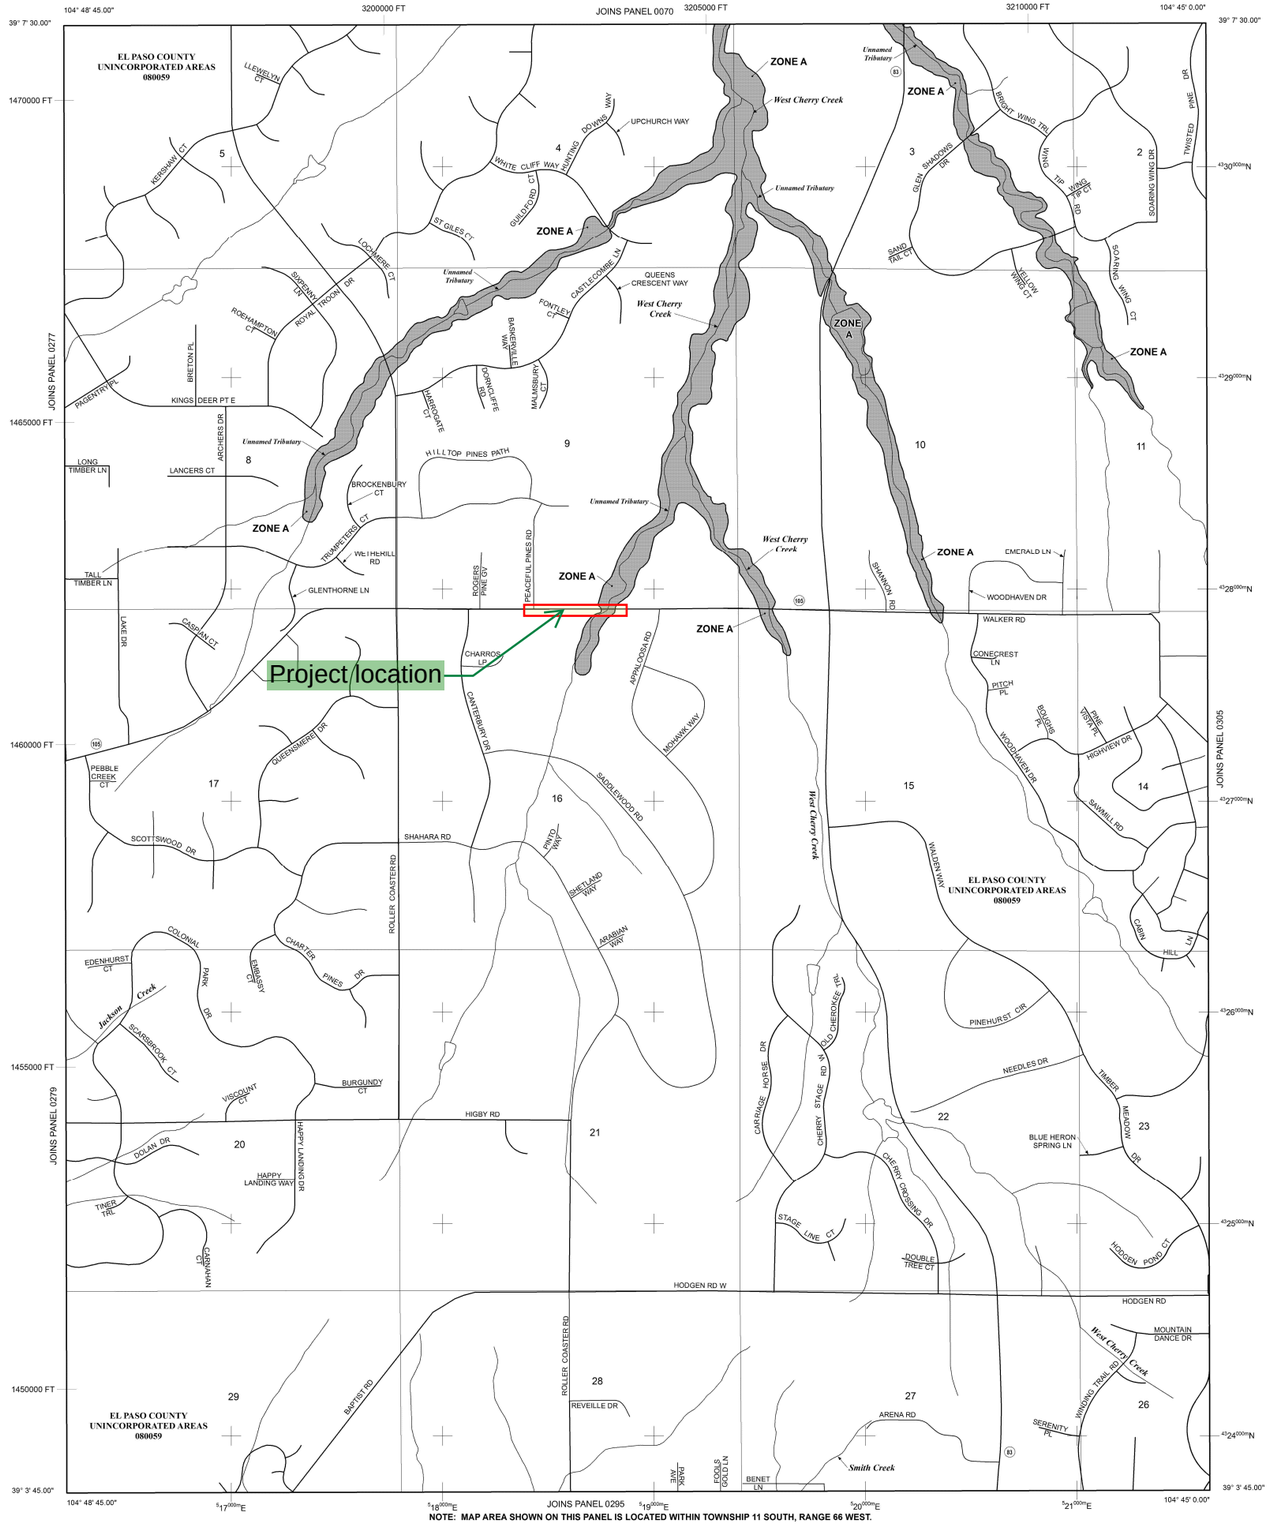

LEGEND

SPECIAL FLOOD HAZARD AREAS (SFHAS) SUBJECT TO INUNDATION BY THE 1% ANNUAL CHANCE FLOOD

The 1% annual chance flood (100-year flood), also known as the base flood, is the flood that has a 1% chance of being equaled or exceeded in any given year. The Special Flood Hazard Area is the area subject to flooding by the 1% annual chance flood. Areas of Special Flood Hazard include Zones A, AE, AH, AO, AR, A99, V, and VE. The Base Flood Elevation is the water-surface elevation of the 1% annual chance flood.

ZONE A No Base Flood Elevations determined.
ZONE AE Base Flood Elevations determined.
ZONE AH Flood depths of 1 to 3 feet (usually areas of ponding); Base Flood Elevations determined.
ZONE AO Flood depths of 1 to 3 feet (usually sheet flow on sloping terrain); average depths determined. For areas of alluvial fan flooding, velocities also determined.
ZONE AR Special Flood Hazard Area Formerly protected from the 1% annual chance flood by a flood control system that was subsequently decertified. Zone AR indicates that the former flood control system is being restored to provide protection from the 1% annual chance or greater flood.
ZONE A99 Area to be protected from 1% annual chance flood by a Federal flood protection system under construction; no Base Flood Elevations determined.
ZONE V Coastal flood zone with velocity hazard (wave action); no Base Flood Elevations determined.
ZONE VE Coastal flood zone with velocity hazard (wave action); Base Flood Elevations determined.

FLOODWAY AREAS IN ZONE AE

The floodway is the channel of a stream plus any adjacent floodplain areas that must be kept free of encroachment so that the 1% annual chance flood can be carried without substantial increases in flood heights.

OTHER FLOOD AREAS

ZONE X Areas of 0.2% annual chance flood; areas of 1% annual chance flood with average depths of less than 1 foot or with drainage areas less than 1 square mile; and areas protected by levees from 1% annual chance flood.

OTHER AREAS

ZONE X Areas determined to be outside the 0.2% annual chance floodplain.
ZONE D Areas in which flood hazards are undetermined, but possible.

COASTAL BARRIER RESOURCES SYSTEM (CBRS) AREAS

OTHERWISE PROTECTED AREAS (OPAs)

CBRS areas and OPAs are normally located within or adjacent to Special Flood Hazard Areas.

Floodplain boundary
Floodway boundary
Zone D Boundary
CBRS and OPA boundary
Boundary dividing Special Flood Hazard Areas of different Base Flood Elevations, flood depths or flood velocities.
513 — Base Flood Elevation line and value; elevation in feet*
(EL 987) — Base Flood Elevation value where uniform within zone; elevation in feet*

* Referenced to the North American Vertical Datum of 1988 (NAVD 88)

A — A Cross section line
23 — 23 Transect line
97° 07' 30.00" / 32° 22' 30.00" Geographic coordinates referenced to the North American Datum of 1983 (NAD 83)
4275000mN 1000-meter Universal Transverse Mercator grid ticks, zone 13
6000000 FT 5000-foot grid ticks: Colorado State Plane coordinate system, central zone (FIPSZONE 0502), Lambert Conformal Conic Projection
DX5510 Bench mark (see explanation in Notes to Users section of this FIRM panel)
M1.5 River Mile

MAP REPOSITORIES
Refer to Map Repositories list on Map Index

EFFECTIVE DATE OF COUNTYWIDE FLOOD INSURANCE RATE MAP
MARCH 17, 1997

EFFECTIVE DATE(S) OF REVISION(S) TO THIS PANEL
DECEMBER 7, 2018 - to update corporate limits, to change Base Flood Elevations and Special Flood Hazard Areas, to update map format, to add roads and road names, and to incorporate previously issued Letters of Map Revision.

For community map revision history prior to countywide mapping, refer to the Community Map History Table located in the Flood Insurance Study report for this jurisdiction.

To determine if flood insurance is available in this community, contact your insurance agent or call the National Flood Insurance Program at 1-800-638-6620.

MAP SCALE 1" = 1000'
500 0 1000 2000 FEET
300 0 300 600 METERS

NFIP

PANEL 0285G

NATIONAL FLOOD INSURANCE PROGRAM

FIRM

FLOOD INSURANCE RATE MAP

EL PASO COUNTY, COLORADO AND INCORPORATED AREAS

PANEL 285 OF 1300

(SEE MAP INDEX FOR FIRM PANEL LAYOUT)

CONTAINS:


COMMUNITY	NUMBER	PANEL	SUFFIX
EL PASO COUNTY	080059	0285	G

Notice to User: The **Map Number** shown below should be used when placing map orders; the **Community Number** shown above should be used on insurance applications for the subject community.

MAP NUMBER 08041C0285G

MAP REVISED DECEMBER 7, 2018

Federal Emergency Management Agency

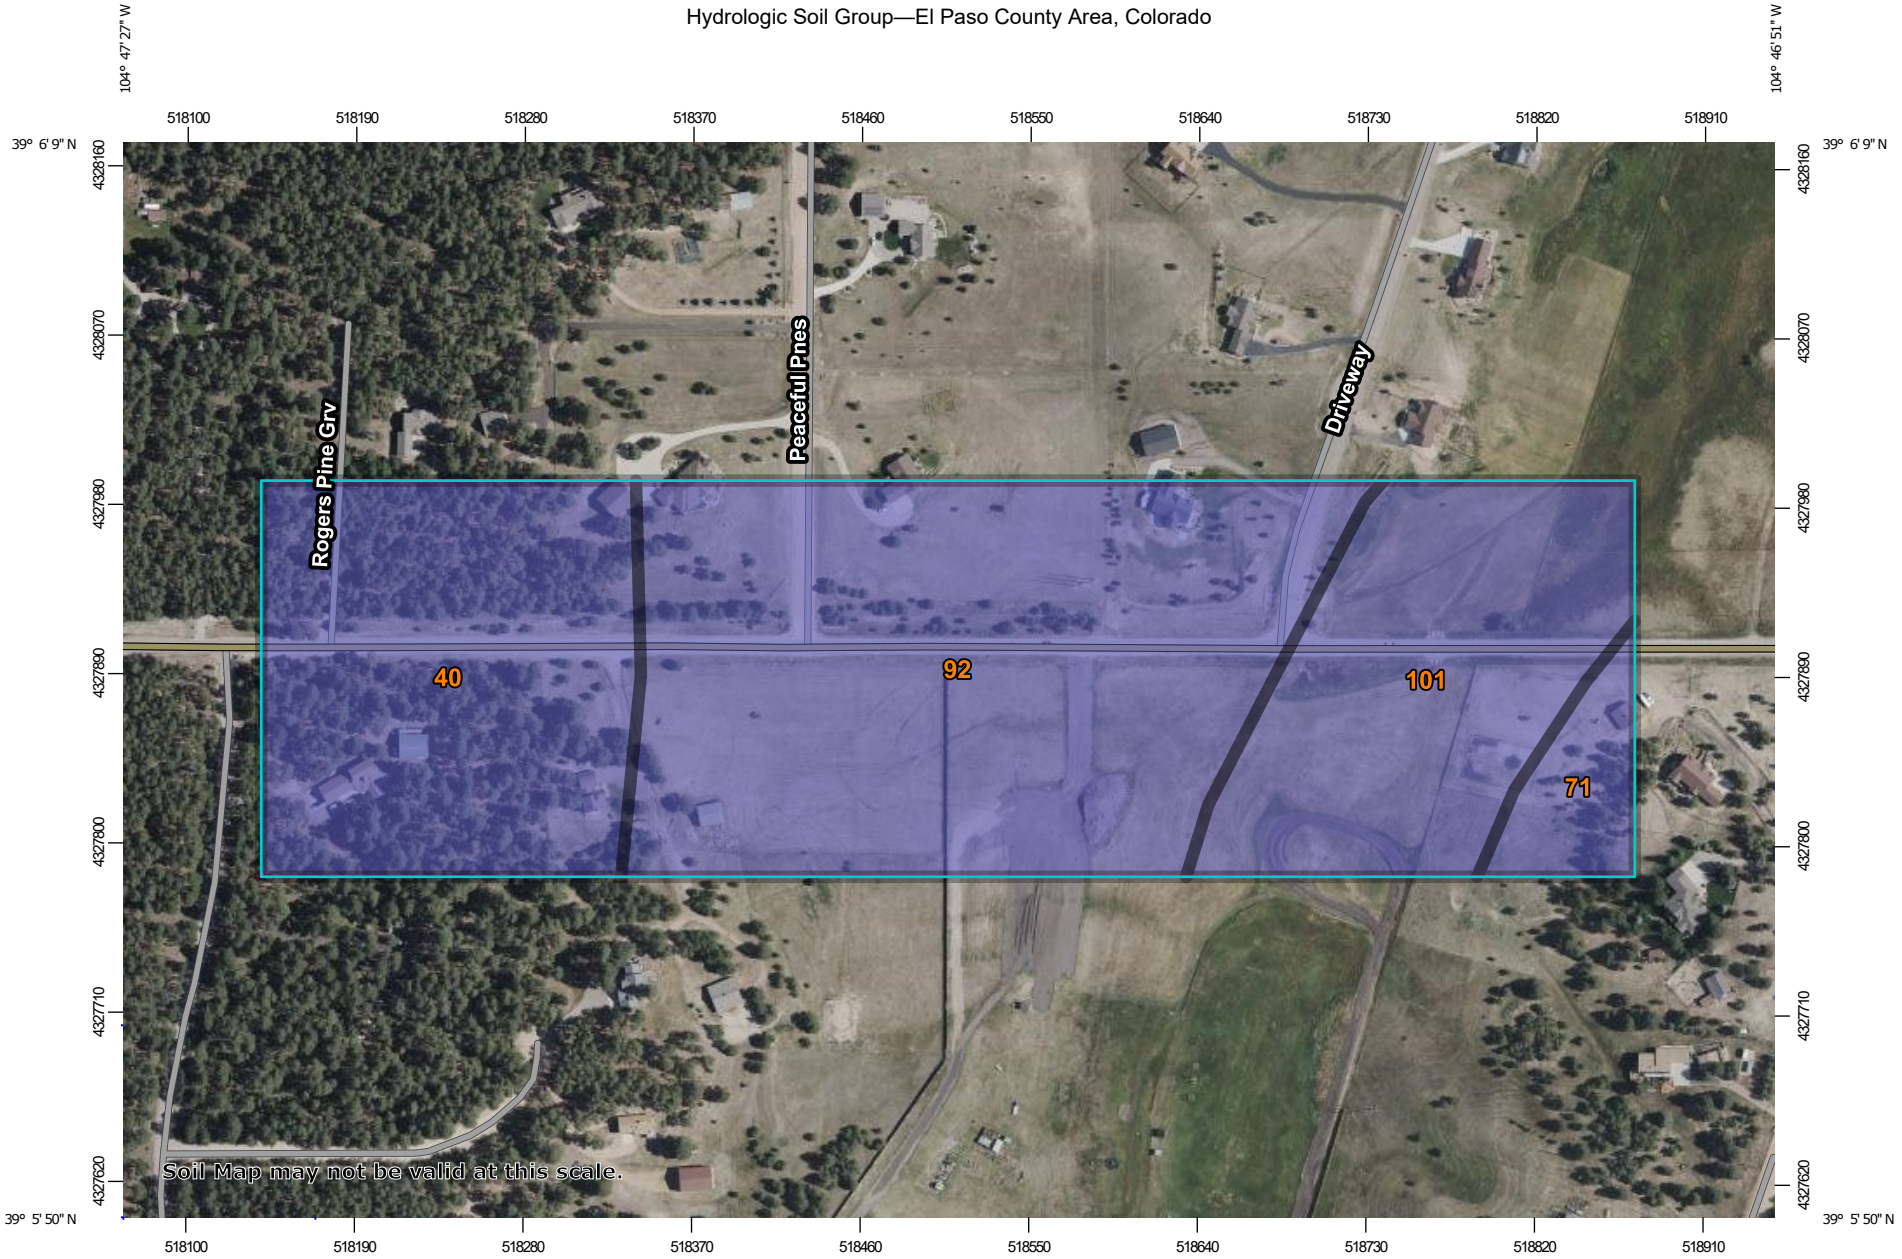

Map Scale: 1:4,030 if printed on A landscape (11" x 8.5") sheet.

N

Meters: 0 50 100 200 300

Feet: 0 150 300 600 900

Map projection: Web Mercator Corner coordinates: WGS84 Edge tics: UTM Zone 13N WGS84

MAP LEGEND

Area of Interest (AOI)

- Area of Interest (AOI)

Soils

Soil Rating Polygons

- A
- A/D
- B
- B/D
- C
- C/D
- D
- Not rated or not available

Soil Rating Lines

- A
- A/D
- B
- B/D
- C
- C/D
- D
- Not rated or not available

Soil Rating Points

- A
- A/D
- B
- B/D
- C
- C/D
- D
- Not rated or not available

Water Features

- Streams and Canals

Transportation

- Rails
- Interstate Highways
- US Routes
- Major Roads
- Local Roads

Background

- Aerial Photography

MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:24,000.

Warning: Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service
Web Soil Survey URL:
Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: El Paso County Area, Colorado
Survey Area Data: Version 23, Aug 29, 2025

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Jul 23, 2024—Aug 4, 2024

The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

Hydrologic Soil Group

Map unit symbol	Map unit name	Rating	Acres in AOI	Percent of AOI
40	Kettle gravelly loamy sand, 3 to 8 percent slopes	B	10.4	27.2%
71	Pring coarse sandy loam, 3 to 8 percent slopes	B	1.6	4.2%
92	Tomah-Crowfoot loamy sands, 3 to 8 percent slopes	B	17.9	46.6%
101	Ustic Torrifluvents, loamy	B	8.4	22.0%
Totals for Area of Interest			**38.3**	**100.0%**

Description

Hydrologic soil groups are based on estimates of runoff potential. Soils are assigned to one of four groups according to the rate of water infiltration when the soils are not protected by vegetation, are thoroughly wet, and receive precipitation from long-duration storms.

The soils in the United States are assigned to four groups (A, B, C, and D) and three dual classes (A/D, B/D, and C/D). The groups are defined as follows:

Group A. Soils having a high infiltration rate (low runoff potential) when thoroughly wet. These consist mainly of deep, well drained to excessively drained sands or gravelly sands. These soils have a high rate of water transmission.

Group B. Soils having a moderate infiltration rate when thoroughly wet. These consist chiefly of moderately deep or deep, moderately well drained or well drained soils that have moderately fine texture to moderately coarse texture. These soils have a moderate rate of water transmission.

Group C. Soils having a slow infiltration rate when thoroughly wet. These consist chiefly of soils having a layer that impedes the downward movement of water or soils of moderately fine texture or fine texture. These soils have a slow rate of water transmission.

Group D. Soils having a very slow infiltration rate (high runoff potential) when thoroughly wet. These consist chiefly of clays that have a high shrink-swell potential, soils that have a high water table, soils that have a claypan or clay layer at or near the surface, and soils that are shallow over nearly impervious material. These soils have a very slow rate of water transmission.


If a soil is assigned to a dual hydrologic group (A/D, B/D, or C/D), the first letter is for drained areas and the second is for undrained areas. Only the soils that in their natural condition are in group D are assigned to dual classes.

Rating Options

Aggregation Method: Dominant Condition

Component Percent Cutoff: None Specified

Tie-break Rule: Higher

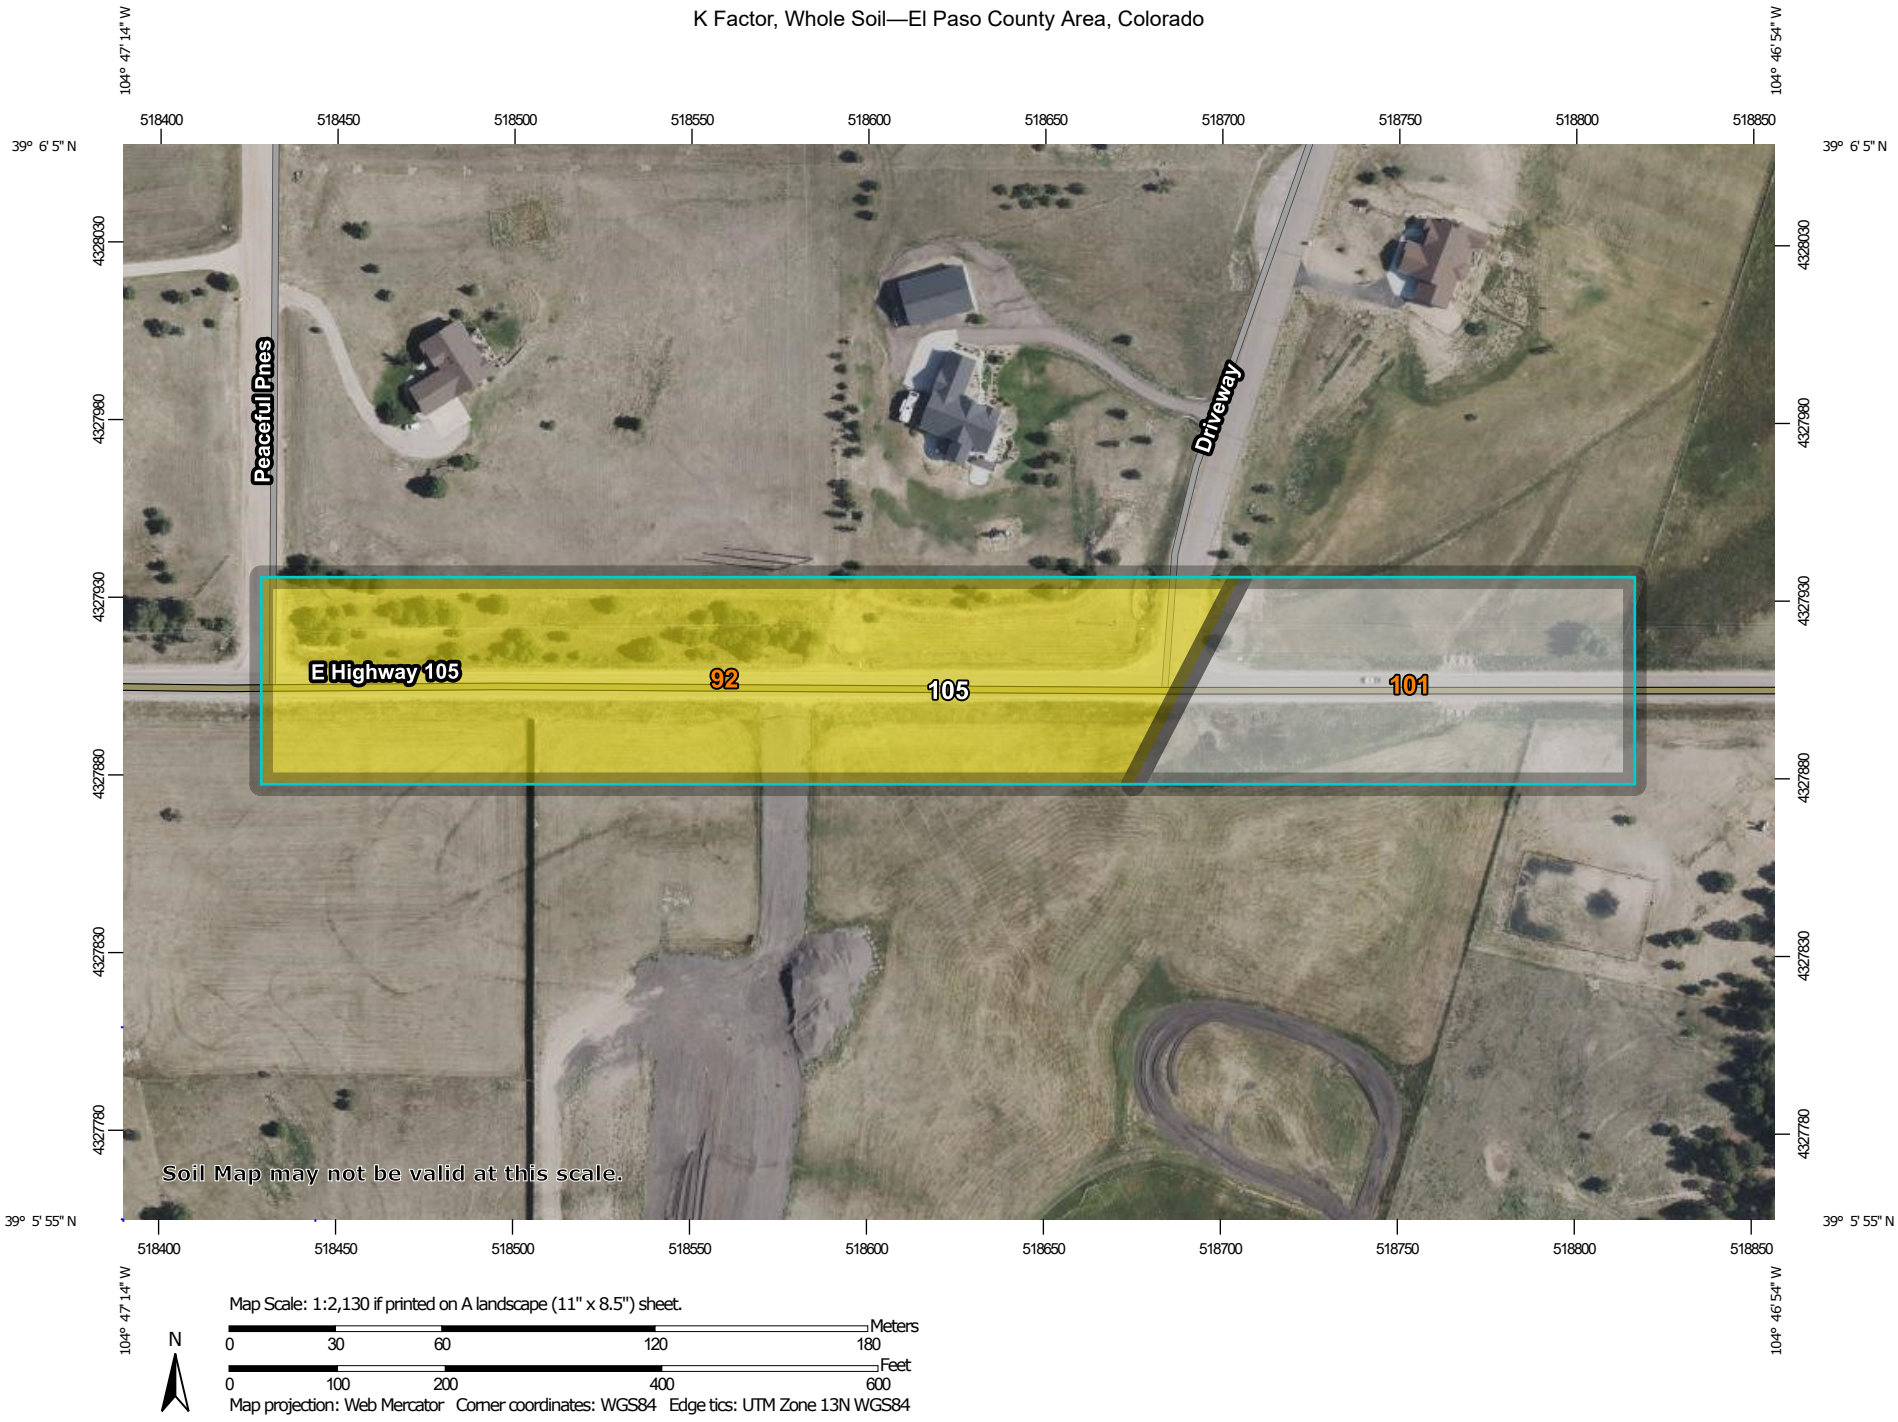

Map Scale: 1:2,130 if printed on A landscape (11" x 8.5") sheet.

N

Meters: 0 30 60 120 180

Feet: 0 100 200 400 600

Map projection: Web Mercator Corner coordinates: WGS84 Edge tics: UTM Zone 13N WGS84

MAP LEGEND

Area of Interest (AOI)

Area of Interest (AOI)

Soils

Soil Rating Polygons

.02
.05
.10
.15
.17
.20
.24
.28
.32
.37
.43
.49
.55
.64
Not rated or not available

Soil Rating Lines

.02
.05
.10
.15
.17
.20
.24
.28
.32
.37
.43
.49
.55
.64
Not rated or not available

Soil Rating Points

.02
.05
.10
.15
.17
.20
.24
.28
.32
.37
.43
.49
.55
.64
Not rated or not available

Water Features

Streams and Canals

Transportation

Rails
Interstate Highways
US Routes
Major Roads
Local Roads

Background

Aerial Photography

MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:24,000.

Warning: Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service
Web Soil Survey URL:
Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: El Paso County Area, Colorado
Survey Area Data: Version 24, Sep 1, 2026

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Jul 23, 2024—Aug 4, 2024

The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

K Factor, Whole Soil

Map unit symbol	Map unit name	Rating	Acres in AOI	Percent of AOI
92	Tomah-Crowfoot loamy sands, 3 to 8 percent slopes	.17	3.8	67.4%
101	Ustic Torrifluvents, loamy		1.8	32.6%
Totals for Area of Interest			**5.6**	**100.0%**

Description

Erosion factor K indicates the susceptibility of a soil to sheet and rill erosion by water. Factor K is one of six factors used in the Universal Soil Loss Equation (USLE) and the Revised Universal Soil Loss Equation (RUSLE) to predict the average annual rate of soil loss by sheet and rill erosion in tons per acre per year. The estimates are based primarily on percentage of silt, sand, and organic matter and on soil structure and saturated hydraulic conductivity (Ksat). Values of K range from 0.02 to 0.69. Other factors being equal, the higher the value, the more susceptible the soil is to sheet and rill erosion by water.

"Erosion factor Kw (whole soil)" indicates the erodibility of the whole soil. The estimates are modified by the presence of rock fragments.

Factor K does not apply to organic horizons and is not reported for those layers.

Rating Options

Aggregation Method: Dominant Condition

Component Percent Cutoff: None Specified

Tie-break Rule: Higher

Layer Options (Horizon Aggregation Method): Surface Layer (Not applicable)

APPENDIX B – GEC PLANS

TO BE INCLUDED AFTER FINAL APPROVAL FROM EPC.

APPENDIX C – GEC DETAILS

Temporary and Permanent Seeding (TS/PS) EC-2

Description

Temporary seeding can be used to stabilize disturbed areas that will be inactive for an extended period. Permanent seeding should be used to stabilize areas at final grade that will not be otherwise stabilized. Effective seeding includes preparation of a seedbed, selection of an appropriate seed mixture, proper planting techniques, and protection of the seeded area with mulch, geotextiles, or other appropriate measures.



Photograph TS/PS -1. Equipment used to drill seed. Photo courtesy of Douglas County.

Appropriate Uses

When the soil surface is disturbed and will remain inactive for an extended period (typically 30 days or longer), proactive stabilization measures should be implemented. If the inactive period is short-lived (on the order of two weeks), techniques such as surface roughening may be appropriate. For longer periods of inactivity, temporary seeding and mulching can provide effective erosion control. Permanent seeding should be used on finished areas that have not been otherwise stabilized.

Typically, local governments have their own seed mixes and timelines for seeding. Check jurisdictional requirements for seeding and temporary stabilization.

Design and Installation

Effective seeding requires proper seedbed preparation, selection of an appropriate seed mixture, use of appropriate seeding equipment to ensure proper coverage and density, and protection with mulch or fabric until plants are established.

The USDCM Volume 2 *Revegetation* Chapter contains detailed seed mix, soil preparations, and seeding and mulching recommendations that may be referenced to supplement this Fact Sheet.

Drill seeding is the preferred seeding method. Hydroseeding is not recommended except in areas where steep slopes prevent use of drill seeding equipment, and even in these instances it is preferable to hand seed and mulch. Some jurisdictions do not allow hydroseeding or hydromulching.

Seedbed Preparation

Prior to seeding, ensure that areas to be revegetated have soil conditions capable of supporting vegetation. Overlot grading can result in loss of topsoil, resulting in poor quality subsoils at the ground surface that have low nutrient value, little organic matter content, few soil microorganisms, rooting restrictions, and conditions less conducive to infiltration of precipitation. As a result, it is typically necessary to provide stockpiled topsoil, compost, or other

Temporary and Permanent Seeding	
Functions	
Erosion Control	Yes
Sediment Control	No
Site/Material Management	No

soil amendments and rototill them into the soil to a depth of 6 inches or more.

Topsoil should be salvaged during grading operations for use and spread on areas to be revegetated later. Topsoil should be viewed as an important resource to be utilized for vegetation establishment, due to its water-holding capacity, structure, texture, organic matter content, biological activity, and nutrient content. The rooting depth of most native grasses in the semi-arid Denver metropolitan area is 6 to 18 inches. At a minimum, the upper 6 inches of topsoil should be stripped, stockpiled, and ultimately respread across areas that will be revegetated.

Where topsoil is not available, subsoils should be amended to provide an appropriate plant-growth medium. Organic matter, such as well digested compost, can be added to improve soil characteristics conducive to plant growth. Other treatments can be used to adjust soil pH conditions when needed. Soil testing, which is typically inexpensive, should be completed to determine and optimize the types and amounts of amendments that are required.

If the disturbed ground surface is compacted, rip or rototill the surface prior to placing topsoil. If adding compost to the existing soil surface, rototilling is necessary. Surface roughening will assist in placement of a stable topsoil layer on steeper slopes, and allow infiltration and root penetration to greater depth.

Prior to seeding, the soil surface should be rough and the seedbed should be firm, but neither too loose nor compacted. The upper layer of soil should be in a condition suitable for seeding at the proper depth and conducive to plant growth. Seed-to-soil contact is the key to good germination.

Seed Mix for Temporary Vegetation

To provide temporary vegetative cover on disturbed areas which will not be paved, built upon, or fully landscaped or worked for an extended period (typically 30 days or more), plant an annual grass appropriate for the time of planting and mulch the planted areas. Annual grasses suitable for the Denver metropolitan area are listed in Table TS/PS-1. These are to be considered only as general recommendations when specific design guidance for a particular site is not available. Local governments typically specify seed mixes appropriate for their jurisdiction.

Seed Mix for Permanent Revegetation

To provide vegetative cover on disturbed areas that have reached final grade, a perennial grass mix should be established. Permanent seeding should be performed promptly (typically within 14 days) after reaching final grade. Each site will have different characteristics and a landscape professional or the local jurisdiction should be contacted to determine the most suitable seed mix for a specific site. In lieu of a specific recommendation, one of the perennial grass mixes appropriate for site conditions and growth season listed in Table TS/PS-2 can be used. The pure live seed (PLS) rates of application recommended in these tables are considered to be absolute minimum rates for seed applied using proper drill-seeding equipment.

If desired for wildlife habitat or landscape diversity, shrubs such as rubber rabbitbrush (*Chrysothamnus nauseosus*), fourwing saltbush (*Atriplex canescens*) and skunkbrush sumac (*Rhus trilobata*) could be added to the upland seedmixes at 0.25, 0.5 and 1 pound PLS/acre, respectively. In riparian zones, planting root stock of such species as American plum (*Prunus americana*), woods rose (*Rosa woodsii*), plains cottonwood (*Populus sargentii*), and willow (*Populus spp.*) may be considered. On non-topsoiled upland sites, a legume such as Ladak alfalfa at 1 pound PLS/acre can be included as a source of nitrogen for perennial grasses.

Seeding dates for the highest success probability of perennial species along the Front Range are generally in the spring from April through early May and in the fall after the first of September until the ground freezes. If the area is irrigated, seeding may occur in summer months, as well. See Table TS/PS-3 for appropriate seeding dates.

Table TS/PS-1. Minimum Drill Seeding Rates for Various Temporary Annual Grasses

Species[a] (Common name)	Growth Season[b]	Pounds of Pure Live Seed (PLS)/acre[c]	Planting Depth (inches)
1. Oats	Cool	35 - 50	1 - 2
2. Spring wheat	Cool	25 - 35	1 - 2
3. Spring barley	Cool	25 - 35	1 - 2
4. Annual ryegrass	Cool	10 - 15	½
5. Millet	Warm	3 - 15	½ - ¾
6. Sudangrass	Warm	5–10	½ - ¾
7. Sorghum	Warm	5–10	½ - ¾
8. Winter wheat	Cool	20–35	1 - 2
9. Winter barley	Cool	20–35	1 - 2
10. Winter rye	Cool	20–35	1 - 2
11. Triticale	Cool	25–40	1 - 2

[a] Successful seeding of annual grass resulting in adequate plant growth will usually produce enough dead-plant residue to provide protection from wind and water erosion for an additional year. This assumes that the cover is not disturbed or mowed closer than 8 inches.

Hydraulic seeding may be substituted for drilling only where slopes are steeper than 3:1 or where access limitations exist. When hydraulic seeding is used, hydraulic mulching should be applied as a separate operation, when practical, to prevent the seeds from being encapsulated in the mulch.

[b] See Table TS/PS-3 for seeding dates. Irrigation, if consistently applied, may extend the use of cool season species during the summer months.

[c] Seeding rates should be doubled if seed is broadcast, or increased by 50 percent if done using a Brillion Drill or by hydraulic seeding.

Table TS/PS-2. Minimum Drill Seeding Rates for Perennial Grasses

Common[a] Name	Botanical Name	Growth Season[b]	Growth Form	Seeds/ Pound	Pounds of PLS/acre
Alakali Soil Seed Mix					
Alkali sacaton	*Sporobolus airoides*	Cool	Bunch	1,750,000	0.25
Basin wildrye	*Elymus cinereus*	Cool	Bunch	165,000	2.5
Sodar streambank wheatgrass	*Agropyron riparium 'Sodar'*	Cool	Sod	170,000	2.5
Jose tall wheatgrass	*Agropyron elongatum 'Jose'*	Cool	Bunch	79,000	7.0
Arriba western wheatgrass	*Agropyron smithii 'Arriba'*	Cool	Sod	110,000	5.5
Total					**17.75**
Fertile Loamy Soil Seed Mix					
Ephriam crested wheatgrass	*Agropyron cristatum 'Ephriam'*	Cool	Sod	175,000	2.0
Dural hard fescue	*Festuca ovina 'duriuscula'*	Cool	Bunch	565,000	1.0
Lincoln smooth brome	*Bromus inermis leyss 'Lincoln'*	Cool	Sod	130,000	3.0
Sodar streambank wheatgrass	*Agropyron riparium 'Sodar'*	Cool	Sod	170,000	2.5
Arriba western wheatgrass	*Agropyron smithii 'Arriba'*	Cool	Sod	110,000	7.0
Total					**15.5**
High Water Table Soil Seed Mix					
Meadow foxtail	*Alopecurus pratensis*	Cool	Sod	900,000	0.5
Redtop	*Agrostis alba*	Warm	Open sod	5,000,000	0.25
Reed canarygrass	*Phalaris arundinacea*	Cool	Sod	68,000	0.5
Lincoln smooth brome	*Bromus inermis leyss 'Lincoln'*	Cool	Sod	130,000	3.0
Pathfinder switchgrass	*Panicum virgatum 'Pathfinder'*	Warm	Sod	389,000	1.0
Alkar tall wheatgrass	*Agropyron elongatum 'Alkar'*	Cool	Bunch	79,000	5.5
Total					**10.75**
Transition Turf Seed Mix[c]					
Ruebens Canadian bluegrass	*Poa compressa 'Ruebens'*	Cool	Sod	2,500,000	0.5
Dural hard fescue	*Festuca ovina 'duriuscula'*	Cool	Bunch	565,000	1.0
Citation perennial ryegrass	*Lolium perenne 'Citation'*	Cool	Sod	247,000	3.0
Lincoln smooth brome	*Bromus inermis leyss 'Lincoln'*	Cool	Sod	130,000	3.0
Total					**7.5**

Table TS/PS-2. Minimum Drill Seeding Rates for Perennial Grasses (cont.)

Common Name	Botanical Name	Growth Season[b]	Growth Form	Seeds/ Pound	Pounds of PLS/acre
Sandy Soil Seed Mix					
Blue grama	*Bouteloua gracilis*	Warm	Sod-forming bunchgrass	825,000	0.5
Camper little bluestem	*Schizachyrium scoparium 'Camper'*	Warm	Bunch	240,000	1.0
Prairie sandreed	*Calamovilfa longifolia*	Warm	Open sod	274,000	1.0
Sand dropseed	*Sporobolus cryptandrus*	Cool	Bunch	5,298,000	0.25
Vaughn sideoats grama	*Bouteloua curtipendula 'Vaughn'*	Warm	Sod	191,000	2.0
Arriba western wheatgrass	*Agropyron smithii 'Arriba'*	Cool	Sod	110,000	5.5
Total					**10.25**
Heavy Clay, Rocky Foothill Seed Mix					
Ephriam crested wheatgrass[d]	*Agropyron cristatum 'Ephriam'*	Cool	Sod	175,000	1.5
Oahe Intermediate wheatgrass	*Agropyron intermedium 'Oahe'*	Cool	Sod	115,000	5.5
Vaughn sideoats grama[e]	*Bouteloua curtipendula 'Vaughn'*	Warm	Sod	191,000	2.0
Lincoln smooth brome	*Bromus inermis leyss 'Lincoln'*	Cool	Sod	130,000	3.0
Arriba western wheatgrass	*Agropyron smithii 'Arriba'*	Cool	Sod	110,000	5.5
Total					**17.5**

[a] All of the above seeding mixes and rates are based on drill seeding followed by crimped straw mulch. These rates should be doubled if seed is broadcast and should be increased by 50 percent if the seeding is done using a Brillion Drill or is applied through hydraulic seeding. Hydraulic seeding may be substituted for drilling only where slopes are steeper than 3:1. If hydraulic seeding is used, hydraulic mulching should be done as a separate operation.

[b] See Table TS/PS-3 for seeding dates.

[c] If site is to be irrigated, the transition turf seed rates should be doubled.

[d] Crested wheatgrass should not be used on slopes steeper than 6H to 1V.

[e] Can substitute 0.5 lbs PLS of blue grama for the 2.0 lbs PLS of Vaughn sideoats grama.

Table TS/PS-3. Seeding Dates for Annual and Perennial Grasses

	Annual Grasses (Numbers in table reference species in Table TS/PS-1)		Perennial Grasses	
Seeding Dates	**Warm**	**Cool**	**Warm**	**Cool**
January 1–March 15			✓	✓
March 16–April 30	4	1,2,3	✓	✓
May 1–May 15	4		✓	
May 16–June 30	4,5,6,7			
July 1–July 15	5,6,7			
July 16–August 31				
September 1–September 30		8,9,10,11		
October 1–December 31			✓	✓

Mulch

Cover seeded areas with mulch or an appropriate rolled erosion control product to promote establishment of vegetation. Anchor mulch by crimping, netting or use of a non-toxic tackifier. See the Mulching BMP Fact Sheet for additional guidance.

Maintenance and Removal

Monitor and observe seeded areas to identify areas of poor growth or areas that fail to germinate. Reseed and mulch these areas, as needed.

An area that has been permanently seeded should have a good stand of vegetation within one growing season if irrigated and within three growing seasons without irrigation in Colorado. Reseed portions of the site that fail to germinate or remain bare after the first growing season.

Seeded areas may require irrigation, particularly during extended dry periods. Targeted weed control may also be necessary.

Protect seeded areas from construction equipment and vehicle access.

Description

Mulching consists of evenly applying straw, hay, shredded wood mulch, rock, bark or compost to disturbed soils and securing the mulch by crimping, tackifiers, netting or other measures. Mulching helps reduce erosion by protecting bare soil from rainfall impact, increasing infiltration, and reducing runoff. Although often applied in conjunction with temporary or permanent seeding, it can also be used for temporary stabilization of areas that cannot be reseeded due to seasonal constraints.

Mulch can be applied either using standard mechanical dry application methods or using hydromulching equipment that hydraulically applies a slurry of water, wood fiber mulch, and often a tackifier.



Photograph MU-1. An area that was recently seeded, mulched, and crimped.

Appropriate Uses

Use mulch in conjunction with seeding to help protect the seedbed and stabilize the soil. Mulch can also be used as a temporary cover on low to mild slopes to help temporarily stabilize disturbed areas where growing season constraints prevent effective reseeding. Disturbed areas should be properly mulched and tacked, or seeded, mulched and tacked promptly after final grade is reached (typically within no longer than 14 days) on portions of the site not otherwise permanently stabilized.

Standard dry mulching is encouraged in most jurisdictions; however, hydromulching may not be allowed in certain jurisdictions or may not be allowed near waterways.

Do not apply mulch during windy conditions.

Design and Installation

Prior to mulching, surface-roughen areas by rolling with a crimping or punching type roller or by track walking. Track walking should only be used where other methods are impractical because track walking with heavy equipment typically compacts the soil.

A variety of mulches can be used effectively at construction sites. Consider the following:

Mulch	
Functions	
Erosion Control	Yes
Sediment Control	Moderate
Site/Material Management	No

- Clean, weed-free and seed-free cereal grain straw should be applied evenly at a rate of 2 tons per acre and must be tacked or fastened by a method suitable for the condition of the site. Straw mulch must be anchored (and not merely placed) on the surface. This can be accomplished mechanically by crimping or with the aid of tackifiers or nets. Anchoring with a crimping implement is preferred, and is the recommended method for areas flatter than 3:1. Mechanical crimpers must be capable of tucking the long mulch fibers into the soil to a depth of 3 inches without cutting them. An agricultural disk, while not an ideal substitute, may work if the disk blades are dull or blunted and set vertically; however, the frame may have to be weighted to afford proper soil penetration.

- Grass hay may be used in place of straw; however, because hay is comprised of the entire plant including seed, mulching with hay may seed the site with non-native grass species which might in turn out-compete the native seed. Alternatively, native species of grass hay may be purchased, but can be difficult to find and are more expensive than straw. Purchasing and utilizing a certified weed-free straw is an easier and less costly mulching method. When using grass hay, follow the same guidelines as for straw (provided above).

- On small areas sheltered from the wind and heavy runoff, spraying a tackifier on the mulch is satisfactory for holding it in place. For steep slopes and special situations where greater control is needed, erosion control blankets anchored with stakes should be used instead of mulch.

- Hydraulic mulching consists of wood cellulose fibers mixed with water and a tackifying agent and should be applied at a rate of no less than 1,500 pounds per acre (1,425 lbs of fibers mixed with at least 75 lbs of tackifier) with a hydraulic mulcher. For steeper slopes, up to 2000 pounds per acre may be required for effective hydroseeding. Hydromulch typically requires up to 24 hours to dry; therefore, it should not be applied immediately prior to inclement weather. Application to roads, waterways and existing vegetation should be avoided.

- Erosion control mats, blankets, or nets are recommended to help stabilize steep slopes (generally 3:1 and steeper) and waterways. Depending on the product, these may be used alone or in conjunction with grass or straw mulch. Normally, use of these products will be restricted to relatively small areas. Biodegradable mats made of straw and jute, straw-coconut, coconut fiber, or excelsior can be used instead of mulch. (See the ECM/TRM BMP for more information.)

- Some tackifiers or binders may be used to anchor mulch. Check with the local jurisdiction for allowed tackifiers. Manufacturer's recommendations should be followed at all times. (See the Soil Binder BMP for more information on general types of tackifiers.)

- Rock can also be used as mulch. It provides protection of exposed soils to wind and water erosion and allows infiltration of precipitation. An aggregate base course can be spread on disturbed areas for temporary or permanent stabilization. The rock mulch layer should be thick enough to provide full coverage of exposed soil on the area it is applied.

Maintenance and Removal

After mulching, the bare ground surface should not be more than 10 percent exposed. Reapply mulch, as needed, to cover bare areas.

Rolled Erosion Control Products (RECP) EC-6

Description



Photograph RECP-1. Erosion control blanket protecting the slope from erosion and providing favorable conditions for revegetation.

Rolled Erosion Control Products (RECPs) include a variety of temporary or permanently installed manufactured products designed to control erosion and enhance vegetation establishment and survivability, particularly on slopes and in channels. For applications where natural vegetation alone will provide sufficient permanent erosion protection, temporary products such as netting, open weave textiles and a variety of erosion control blankets (ECBs) made of biodegradable natural materials (e.g., straw, coconut fiber) can be used. For applications where natural vegetation alone will not be sustainable under expected flow conditions, permanent rolled erosion control products such as turf reinforcement mats (TRMs) can be used. In particular, turf reinforcement mats are designed for discharges that exert velocities and shear stresses that exceed the typical limits of mature natural vegetation.

Appropriate Uses

RECPs can be used to control erosion in conjunction with revegetation efforts, providing seedbed protection from wind and water erosion. These products are often used on disturbed areas on slopes that are 3:1 or steeper, in areas with highly erosive soils, as part of drainageway stabilization, or any location where additional protection is needed. In order to select the appropriate RECP for site conditions, it is important to have a general understanding of the general types of these products, their expected longevity, and general characteristics. The Erosion Control Technology Council (ECTC 2014) characterizes RECPs into these categories:

Temporary RECPs:

- **Mulch control netting**: A planar woven natural fiber or extruded geosynthetic mesh used as a temporary degradable rolled erosion control product to anchor loose fiber mulches.
- **Open weave textile**: A temporary degradable rolled erosion control product composed of processed natural or polymer yarns woven into a matrix, used to provide erosion control and facilitate vegetation establishment.
- **Erosion control blanket (ECB)**: A temporary degradable rolled erosion control product composed of processed natural or polymer fibers which are mechanically, structurally or chemically bound together to form a continuous matrix to provide erosion control and facilitate vegetation establishment. ECBs can be further differentiated into rapidly degrading single-net and double-net types or slowly degrading types.

Rolled Erosion Control Products	
Functions	
Erosion Control	Yes
Sediment Control	No
Site/Material Management	No
Vegetation Protection	Yes

Permanent RECPs:

- **Turf Reinforcement Mat (TRM)**: A rolled erosion control product composed of non-degradable synthetic fibers, filaments, nets, wire mesh, and/or other elements, processed into a permanent, three-dimensional matrix of sufficient thickness. TRMs, which may be supplemented with degradable components, are designed to impart immediate erosion protection, enhance vegetation establishment and provide long-term functionality by permanently reinforcing vegetation during and after maturation. Note: TRMs are typically used in hydraulic applications, such as high flow ditches and channels, steep slopes, stream banks, and shorelines, where erosive forces may exceed the limits of natural, unreinforced vegetation or in areas where limited vegetation establishment is anticipated.

Tables RECP-1 and RECP-2 provide guidelines for selecting RECPs appropriate to site conditions and desired longevity. Table RECP-1 is for conditions where natural vegetation alone will provide permanent erosion control, whereas Table RECP-2 is for conditions where vegetation alone will not be adequately stable to provide long-term erosion protection due to flow or other conditions.

Table RECP-1. ECTC Standard Specification for Temporary Rolled Erosion Control Products
(Adapted from Erosion Control Technology Council 2017)

Product Description	Slope Applications		Channel Applications	Minimum Tensile Strength	Expected Longevity
	Maximum Gradient	C Factor[1]	Max. Shear Stress[2,3]		
Mulch Control Nets & Open Weave Textiles[4]	5:1 (H:V)	≤0.10 @ 5:1	1.0 lbs/ft^2	125 lbs/ft	Up to 12 months
Netless Rolled Erosion Control Blankets	3:1 (H:V)	≤0.10 @ 3:1	1.0 lbs/ft^2	125 lbs/ft	
Single-net Erosion Control Blankets	3:1 (H:V)	≤0.10 @ 3:1	1.5 lbs/ft^2	60 lbs/ft	
Double-net Erosion Control Blankets	2:1 (H:V)	≤0.10 @ 2:1	1.75 lbs/ft^2	75 lbs/ft	
Erosion Control Blankets & Open Weave Textiles (slowly degrading)	2:1 (H:V)	≤0.05 @ 2:1	2.00 lbs/ft^2	100 lbs/ft	24 months
Erosion Control Blankets & Open Weave Textiles (long term)	1.5:1 (H:V)	≤0.05 @ 1:1	2.25 lbs/ft^2	100 lbs/ft	36 months

[1] This value should be the maximum C Factor from standardized large-scale rainfall performance testing,

ASTM D6459 or equivalent deemed acceptable by the engineer.

[2] Required minimum shear stress RECP (unvegetated) can sustain without physical damage or excess erosion (>0.5 in soil loss) during a 30-minute flow event in large-scale performance testing, ASTM d6460 or equivalent deemed acceptable by the engineer.

[3] The permissible shear stress levels established for each performance category are based on historical experience with products characterized by Manning's roughness coefficients in the range of 0.01 - 0.05.

[4] C Factor and shear stress for mulch control nettings must be obtained with netting used in conjunction with pre-applied mulch material. (*See Section 5.3 of Chapter 7 Construction BMPs for more information on the C Factor*.)

Table RECP-2. ECTC Standard Specification for Permanent[1] Rolled Erosion Control Products
(Adapted from: Erosion Control Technology Council 2017)

Product Type	Slope Applications	Channel Applications	
Turf Reinforcement Mats with a minimum thickness of 0.25 inches per ASTM D 6525 and UV stability of 80% per ASTM D 4355 (500 hours exposure).	Maximum Gradient	Maximum Shear Stress[2,3]	Minimum Tensile Strength (ASTM D6818)
	1:1 (H:V)	6.0 lbs/ft^2	150 lbs/ft
	1:1 (H:V)	8.0 lbs/ft^2	175 lbs/ft
	0.5:1 (H:V)	10.0 lbs/ft^2	200 lbs/ft

[1] For TRMs containing degradable components, all property values must be obtained on the non-degradable portion of the matting alone.

[2] Maximum allowable shear stress TRM (fully vegetated) can sustain without physical damage or excess erosion (> 12.7 mm (0.5 in.) soil loss) during a 30-minute flow event in large scale testing.

[3] Acceptable large-scale testing protocols may include ASTM D 6460, or other independent testing deemed acceptable by the engineer. Large scale performance testing typically involves limited soil types and vegetative stands, therefore it is recommended that an appropriate factor of safety be used in design and product selection.

Design and Installation

RECPs should be installed according to manufacturer's specifications and guidelines. Regardless of the type of product used, it is important to ensure no gaps or voids exist under the material and that all corners of the material are secured using stakes and trenching. Continuous contact between the product and the soil is necessary to avoid failure. Never use metal stakes to secure temporary erosion control products. Often wooden stakes are used to anchor RECPs; however, wood stakes may present installation and maintenance challenges and generally take a long time to biodegrade. Some local jurisdictions have had favorable experiences using biodegradable stakes. The designer should consider the differences in strength prior to selecting the appropriate stake material. Wood stakes are generally used in trench applications and areas with the need for additional hold down strength.

This BMP Fact Sheet provides design details for several commonly used ECB applications, including:

ECB-1 Pipe Outlet to Drainageway
ECB-2 Small Ditch or Swale
ECB-3 Outside of Drainageway
ECB-4 Drainageway

Staking patterns are also provided in the design details according to these factors:

- ECB type
- Slope or channel type

These design details are intended to serve as general guidelines for design and installation. Engineers should adhere to manufacturer's installation recommendations.


Maintenance and Removal

Inspection of erosion control blankets and other RECPs includes:


- Check for general signs of erosion, including voids beneath the mat. If voids are apparent, fill the void with suitable soil and replace the erosion control blanket, following the appropriate staking pattern. Good soil to blanket contact throughout the disturbed area is critical for the product to function as intended.
- Check for damaged or loose stakes and secure loose portions of the blanket.
- Check the area to see if additional BMP are needed to prevent recurrence of any erosion issues.
- Check to make sure the installed product is adequate and evaluate the need for modification or replacement of the selected product.

Erosion control blankets and other RECPs that are biodegradable typically do not need to be removed after construction. If they must be removed, then an alternate soil stabilization method should be installed promptly following removal.


Turf reinforcement mats, although generally resistant to biodegradation, are typically left in place as a dense vegetated cover grows in through the mat matrix. The turf reinforcement mat provides long-term stability and helps the established vegetation resist erosive forces.




ECB

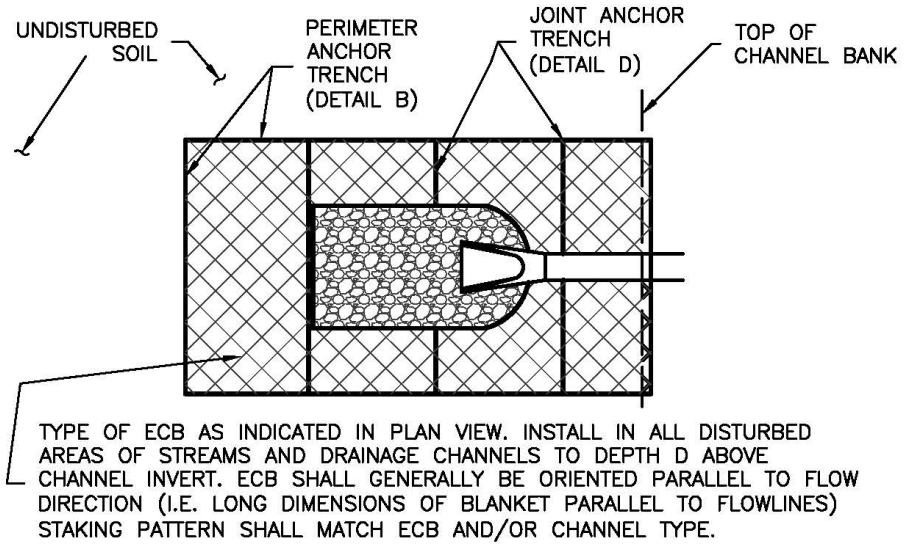


ECB–1. PIPE OUTLET TO DRAINAGEWAY

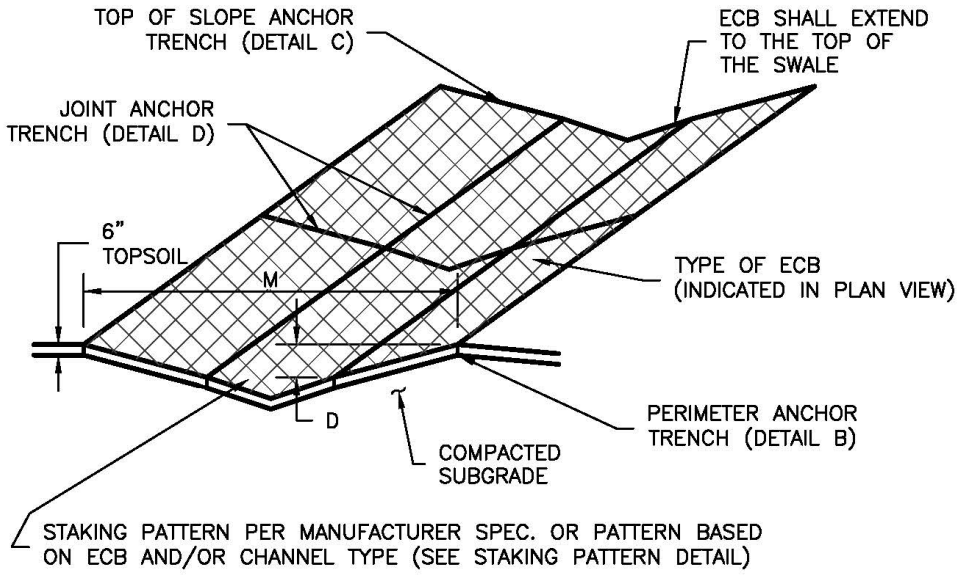

ECB–2. SMALL DITCH OR SWALE

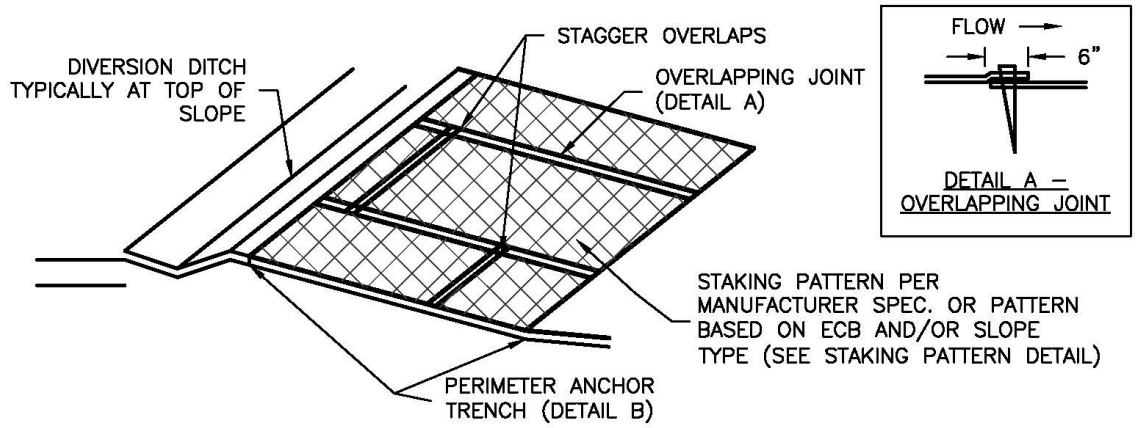

ECB–3. OUTSIDE OF DRAINAGEWAY

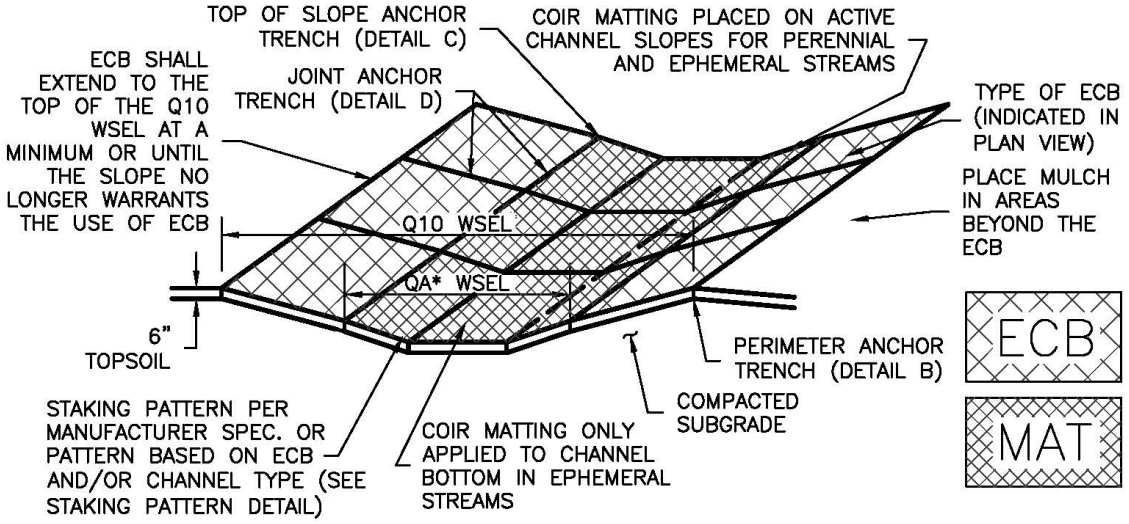

*CONSULT A GEOMORPHOLOGIST TO ASSIST IN DETERMINING ACTIVE CHANNEL FLOW (QA)


ECB–4. DRAINAGEWAY

TABLE ECB–1. ECB MATERIAL SPECIFICATIONS


TYPE	COCONUT CONTENT	STRAW CONTENT	EXCELSIOR CONTENT	RECOMMENDED NETTING**
STRAW*	–	100%	–	DOUBLE/ NATURAL
STRAW–COCONUT	30% MIN	70% MAX	–	DOUBLE/ NATURAL
COIR MAT	100%	–	–	DOUBLE/ NATURAL
EXCELSIOR	–	–	100%	DOUBLE/ NATURAL

*STRAW ECBs MAY ONLY BE USED OUTSIDE OF STREAMS AND DRAINAGE CHANNEL.

**ALTERNATE NETTING INCLUDING SINGLE NETTING AND SYNTHETIC PHOTODEGRADABLE FIBER MAY BE ACCEPTABLE IN SOME JURISDICTIONS

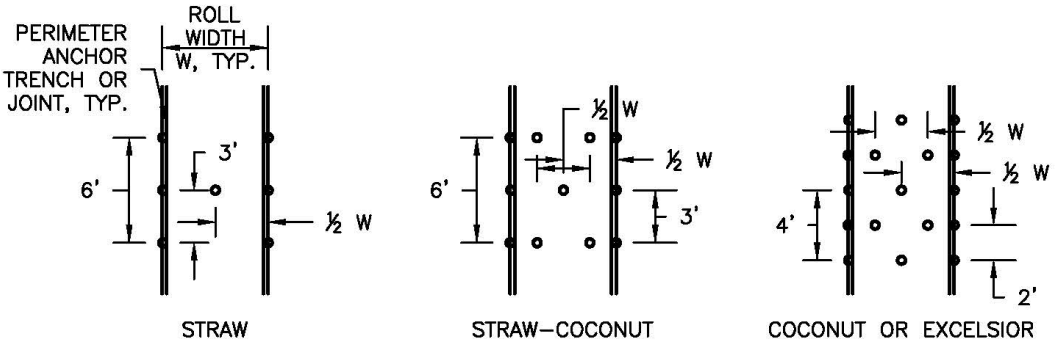


STAKING PATTERNS BY ECB TYPE

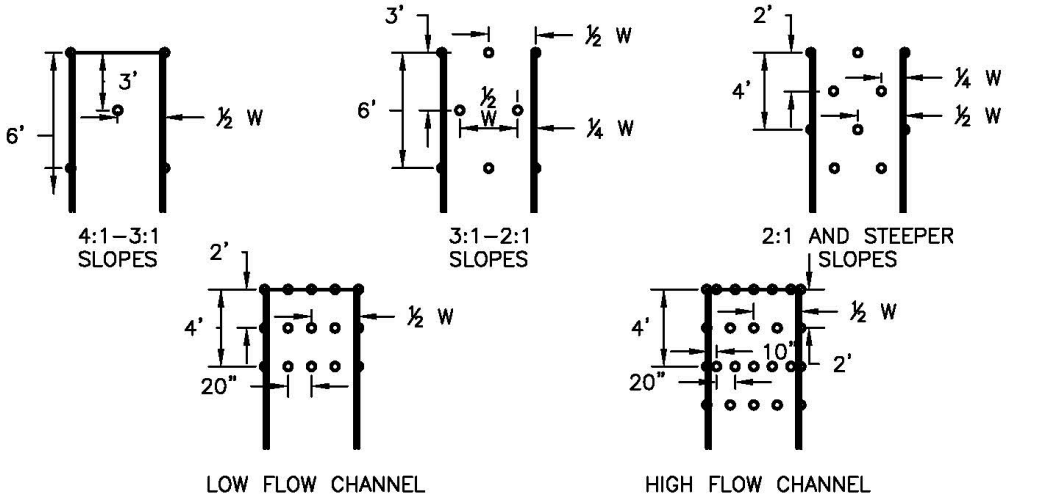


NOTE: IN ADDITION TO FLOW CONDITIONS, THE DESIGNER SHOULD CONSIDER THE PROPERTIES OF THE UNDERLYING SOIL. LESS COHESIVE SOILS MAY WARRANT A TIGHTER STAKING PATTERN.

STAKING PATTERNS BY SLOPE OR CHANNEL TYPE

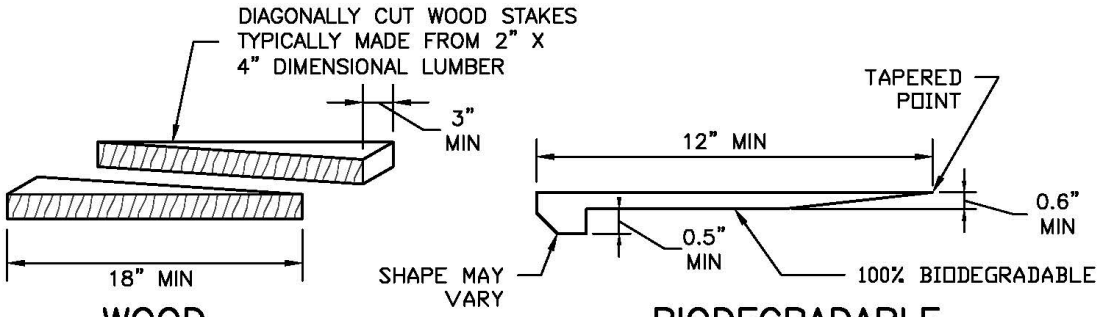

STAKES

NOTES
1. PLACE STAKES 18" O.C. TO 3' ABOVE WATER, THEN 24" O.C. TO UPPER LIMIT OF FABRIC OR AS RECOMMEND BY THE MANUFACTURER.
2. WHEN BLANKETING IS PLACED OVER RIPRAP, USE WOOD STAKES.

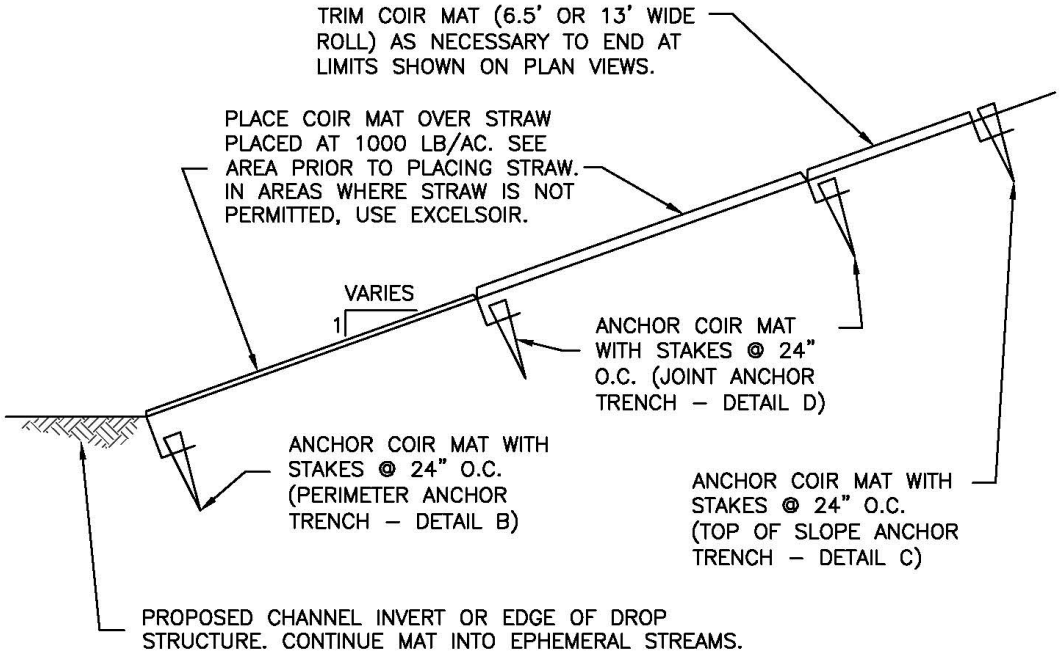

NOTE: USE WOODEN STAKES IN AREAS WHERE MAT IS PLACED OVER RIPRAP.

COIR MAT PLACEMENT DETAIL

EROSION CONTROL BLANKET MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE. REPEATED FAILURE WARRANTS THE NEED FOR REDESIGN OF THE EROSION CONTROL PROTECTION.

4. ECBs SHALL BE LEFT IN PLACE TO BIODEGRADE UNLESS REQUESTED TO BE REMOVED BY THE LOCAL JURISDICTION.

5. ANY ECB PULLED OUT, TORN, OR OTHERWISE DAMAGED SHALL BE REPAIRED OR REINSTALLED. ANY SUBGRADE AREAS BELOW THE GEOTEXTILE THAT HAVE ERODED TO CREATED A VOID UNDER THE BLANKET, OR THAT REMAIN DEVOID OF GRASS SHALL BE REPAIRED, RESEEDED AND MULCHED AND THE ECB REINSTALLED.

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

(DETAILS ADAPTED FROM DOUGLAS COUNTY, COLORADO AND TOWN OF PARKER COLORADO, NOT AVAILABLE IN AUTOCAD)

EROSION CONTROL BLANKET INSTALLATION NOTES

1. SEE PLAN VIEW FOR:
   –LOCATION OF ECB.
   –TYPE OF ECB (STRAW, STRAW–COCONUT, COCONUT/ COIR, OR EXCELSIOR).
   –AREA, A, IN SQUARE YARDS OF EACH TYPE OF ECB.

2. ALL RECPs MUST BE 100% NATURAL AND BIODEGRADABLE MATERIALS.

3. IN AREAS WHERE ECBs ARE SHOWN ON THE PLANS, THE PERMITTEE SHALL PLACE TOPSOIL AND PERFORM FINAL GRADING, SURFACE PREPARATION, AND SEEDING AND MULCHING. SUBGRADE SHALL BE SMOOTH AND MOIST PRIOR TO ECB INSTALLATION AND THE ECB SHALL BE IN FULL CONTACT WITH SUBGRADE. NO GAPS OR VOIDS SHALL EXIST UNDER THE BLANKET.

4. FOR MATS THAT HAVE OPENINGS LARGER THAN THE SOIL, ADD STRAW UNDER (RATE OF 1000# PER ACRE) TO HOLD SOIL AND SEED FROM MIGRATING THROUGH OPENINGS.

5. INSTALL MATS AND BLANKETS PARALLEL TO THE DIRECTION OF STREAM FLOW.

6. PERIMETER ANCHOR TRENCH SHALL BE USED ALONG THE OUTSIDE PERIMETER OF ALL BLANKET AREAS.

7. JOINT ANCHOR TRENCH SHALL BE USED TO JOIN ROLLS OF ECBs TOGETHER (LONGITUDINALLY AND TRANSVERSELY) FOR ALL ECBs EXCEPT STRAW WHICH MAY USE AN OVERLAPPING JOINT.

8. INTERMEDIATE ANCHOR TRENCH SHALL BE USED AT SPACING OF ONE–HALF ROLL LENGTH FOR COCONUT AND EXCELSIOR ECBs.

9. OVERLAPPING JOINT DETAIL SHALL BE USED TO JOIN ROLLS OF ECBs TOGETHER FOR ECBs ON SLOPES AND WITHIN DRAINAGEWAYS. OVERLAP SEAMS SO THAT UPSTREAM RECPs IS ON TOP OF DOWNSTREAM RECPs SO THAT EXPOSED EDGE IS NOT LIFTED BY STREAM FLOWS.


10. MATERIAL SPECIFICATIONS OF ECBs SHALL CONFORM TO TABLE ECB–1.

11. ALL EXPOSED ROOTS SHALL BE TRIMMED TO BELOW THE SOIL SURFACE. ECB/TRM SHALL NOT BE INSTALLED OVER ROCKS OR SOIL CLODS GREATER THAN 4 INCHES.

11. ANY AREAS OF SEEDING AND MULCHING DISTURBED IN THE PROCESS OF INSTALLING ECBS SHALL BE RESEEDED AND MULCHED.

12. DETAILS ON DESIGN PLANS FOR MAJOR DRAINAGEWAY STABILIZATION WILL GOVERN IF DIFFERENT FROM THOSE SHOWN HERE.

13. ADDITIONAL BANK PROTECTION AND/OR TOE REINFORCEMENT MAY BE NEEDED BASED ON CHANNEL GEOMETRY AND HYDRAULICS.

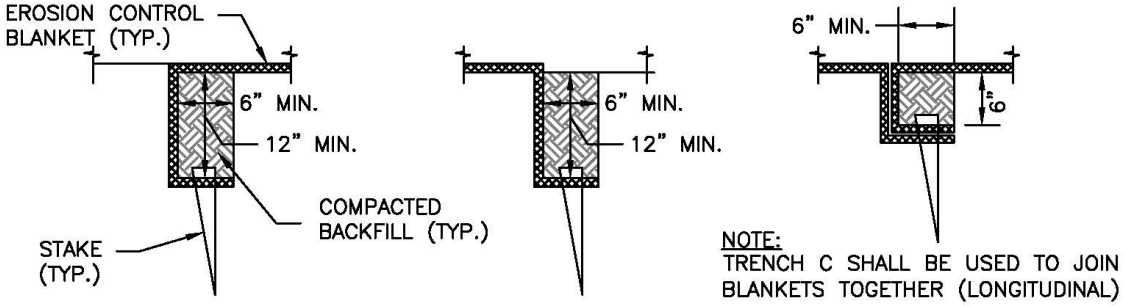

DETAIL B – PERIMETER ANCHOR TRENCH

DETAIL C – TOP OF SLOPE ANCHOR TRENCH

DETAIL D – JOINT ANCHOR TRENCH

ANCHOR TRENCH DETAILS FOR EROSION CONTROL BLANKETS

Check Dams (CD) EC-12

Description

Check dams are temporary grade control structures placed in drainage channels to limit the erosivity of stormwater by reducing flow velocity. Check dams are typically constructed from rock, gravel bags, sand bags, or sometimes, proprietary devices. Reinforced check dams are typically constructed from rock and wire gabion. Although the primary function of check dams is to reduce the velocity of concentrated flows, a secondary benefit is sediment trapping upstream of the structure.



Photograph CD-1. Rock check dams in a roadside ditch. Photo courtesy of WWE.

Appropriate Uses

Use as a grade control for temporary drainage ditches or swales until final soil stabilization measures are established upstream and downstream. Check dams can be used on mild or moderately steep slopes. Check dams may be used under the following conditions:

- As temporary grade control facilities along waterways until final stabilization is established.
- Along permanent swales that need protection prior to installation of a non-erodible lining.
- Along temporary channels, ditches or swales that need protection where construction of a non-erodible lining is not practicable.
- Reinforced check dams should be used in areas subject to high flow velocities.

Design and Installation

Place check dams at regularly spaced intervals along the drainage swale or ditch. Check dams heights should allow for pools to develop upstream of each check dam, extending to the downstream toe of the check dam immediately upstream.

When rock is used for the check dam, place rock mechanically or by hand. Do not dump rocks into the drainage channel. Where multiple check dams are used, the top of the lower dam should be at the same elevation as the toe of the upper dam.

When reinforced check dams are used, install erosion control fabric under and around the check dam to prevent erosion on the upstream and downstream sides. Each section of the dam should be keyed in to reduce the potential for washout or undermining. A rock apron upstream and downstream of the dam may be necessary to further control erosion.

Check Dams	
Functions	
Erosion Control	Yes
Sediment Control	Moderate
Site/Material Management	No

Design details with notes are provided for the following types of check dams:

- Rock Check Dams (CD-1)
- Reinforced Check Dams (CD-2)


Sediment control logs may also be used as check dams; however, silt fence is not appropriate for use as a check dam. Many jurisdictions also prohibit or discourage use of straw bales for this purpose.

Maintenance and Removal

Replace missing rocks causing voids in the check dam. If gravel bags or sandbags are used, replace or repair torn or displaced bags.

Remove accumulated sediment, as needed to maintain BMP effectiveness, typically before the sediment depth upstream of the check dam is within ½ of the crest height. Remove accumulated sediment prior to mulching, seeding, or chemical soil stabilization. Removed sediment can be incorporated into the earthwork with approval from the Project Engineer, or disposed of at an alternate location in accordance with the standard specifications.

Check dams constructed in permanent swales should be removed when perennial grasses have become established, or immediately prior to installation of a non-erodible lining. All of the rock and accumulated sediment should be removed, and the area seeded and mulched, or otherwise stabilized.

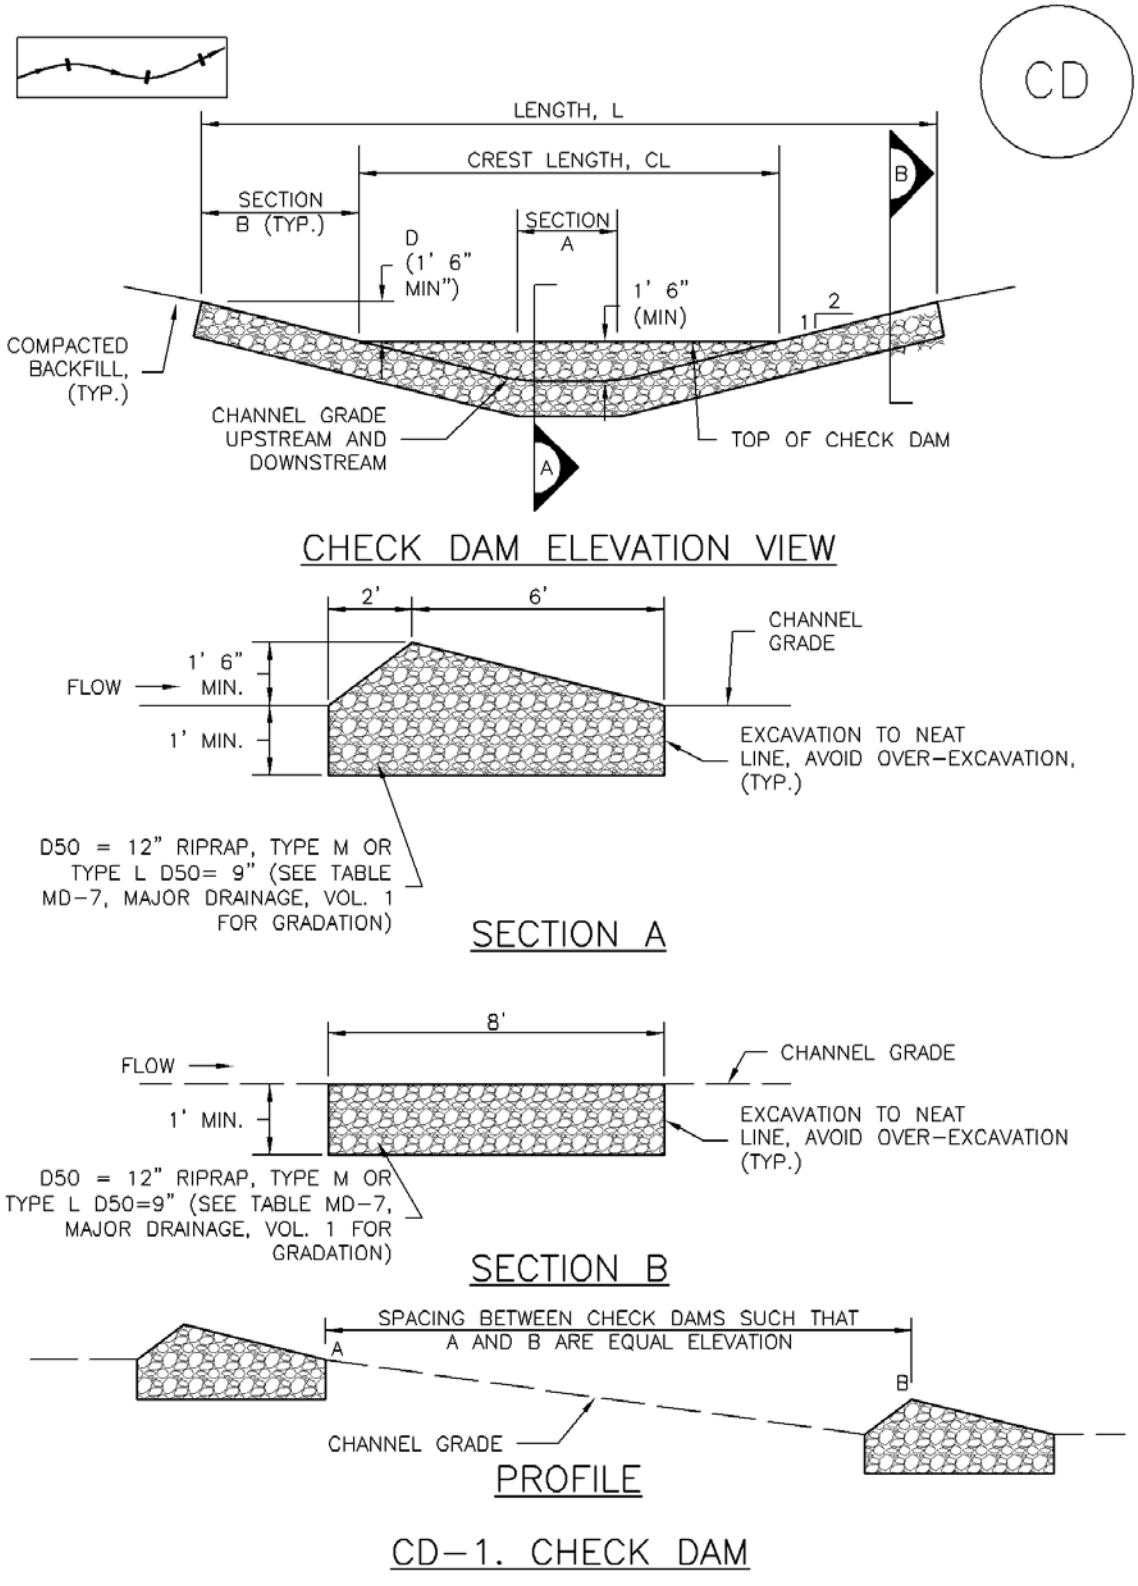
CD
LENGTH, L
CREST LENGTH, CL
SECTION B (TYP.)
SECTION A
D (1' 6" MIN")
1' 6" (MIN)
2
1
B
A
COMPACTED BACKFILL, (TYP.)
CHANNEL GRADE UPSTREAM AND DOWNSTREAM
TOP OF CHECK DAM
CHECK DAM ELEVATION VIEW
2'
6'
CHANNEL GRADE
FLOW
1' 6" MIN.
1' MIN.
EXCAVATION TO NEAT LINE, AVOID OVER-EXCAVATION, (TYP.)
D50 = 12" RIPRAP, TYPE M OR TYPE L D50= 9" (SEE TABLE MD-7, MAJOR DRAINAGE, VOL. 1 FOR GRADATION)
SECTION A
8'
FLOW
CHANNEL GRADE
1' MIN.
EXCAVATION TO NEAT LINE, AVOID OVER-EXCAVATION (TYP.)
D50 = 12" RIPRAP, TYPE M OR TYPE L D50=9" (SEE TABLE MD-7, MAJOR DRAINAGE, VOL. 1 FOR GRADATION)
SECTION B
SPACING BETWEEN CHECK DAMS SUCH THAT A AND B ARE EQUAL ELEVATION
A
B
CHANNEL GRADE
PROFILE
CD-1. CHECK DAM

CHECK DAM INSTALLATION NOTES

1. SEE PLAN VIEW FOR:
   –LOCATION OF CHECK DAMS.
   –CHECK DAM TYPE (CHECK DAM OR REINFORCED CHECK DAM).
   –LENGTH (L), CREST LENGTH (CL), AND DEPTH (D).

2. CHECK DAMS INDICATED ON INITIAL SWMP SHALL BE INSTALLED AFTER CONSTRUCTION FENCE, BUT PRIOR TO ANY UPSTREAM LAND DISTURBING ACTIVITIES.

3. RIPRAP UTILIZED FOR CHECK DAMS SHOULD BE OF APPROPRIATE SIZE FOR THE APPLICATION. TYPICAL TYPES OF RIPRAP USED FOR CHECK DAMS ARE TYPE M (D50 12") OR TYPE L (D50 9").

4. RIPRAP PAD SHALL BE TRENCHED INTO THE GROUND A MINIMUM OF 1'.

5. THE ENDS OF THE CHECK DAM SHALL BE A MINIMUM OF 1' 6" HIGHER THAN THE CENTER OF THE CHECK DAM.

CHECK DAM MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE.


4. SEDIMENT ACCUMULATED UPSTREAM OF THE CHECK DAMS SHALL BE REMOVED WHEN THE SEDIMENT DEPTH IS WITHIN ½ OF THE HEIGHT OF THE CREST.

5. CHECK DAMS ARE TO REMAIN IN PLACE UNTIL THE UPSTREAM DISTURBED AREA IS STABILIZED AND APPROVED BY THE LOCAL JURISDICTION.


6. WHEN CHECK DAMS ARE REMOVED, EXCAVATIONS SHALL BE FILLED WITH SUITABLE COMPACTED BACKFILL. DISTURBED AREA SHALL BE SEEDED AND MULCHED AND COVERED WITH GEOTEXTILE OR OTHERWISE STABILIZED IN A MANNER APPROVED BY THE LOCAL JURISDICTION.

(DETAILS ADAPTED FROM DOUGLAS COUNTY, COLORADO, NOT AVAILABLE IN AUTOCAD)

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

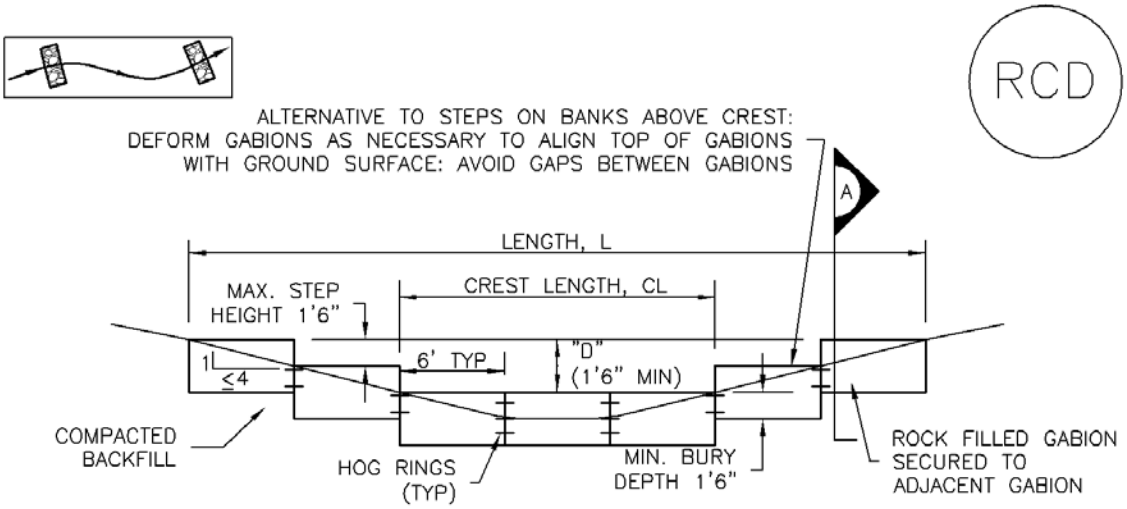

REINFORCED CHECK DAM ELEVATION VIEW



SECTION A

REINFORCED CHECK DAM INSTALLATION NOTES

1. SEE PLAN VIEW FOR:
   - –LOCATIONS OF CHECK DAMS.
   - –CHECK DAM TYPE (CHECK DAM OR REINFORCED CHECK DAM).
   - –LENGTH (L), CREST LENGTH (CL), AND DEPTH (D).

2. CHECK DAMS INDICATED ON THE SWMP SHALL BE INSTALLED PRIOR TO AN UPSTREAM LAND–DISTURBING ACTIVITIES.

3. REINFORCED CHECK DAMS, GABIONS SHALL HAVE GALVANIZED TWISTED WIRE NETTING WITH A MAXIMUM OPENING DIMENSION OF 4½" AND A MINIMUM WIRE THICKNESS OF 0.10". WIRE "HOG RINGS" AT 4" SPACING OR OTHER APPROVED MEANS SHALL BE USED AT ALL GABION SEAMS AND TO SECURE THE GABION TO THE ADJACENT SECTION.

4. THE CHECK DAM SHALL BE TRENCHED INTO THE GROUND A MINIMUM OF 1' 6".

5. GEOTEXTILE BLANKET SHALL BE PLACED IN THE REINFORCED CHECK DAM TRENCH EXTENDING A MINIMUM OF 1' 6" ON BOTH THE UPSTREAM AND DOWNSTREAM SIDES OF THE REINFORCED CHECK DAM.

CD–2. REINFORCED CHECK DAM

REINFORCED CHECK DAM MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE.

4. SEDIMENT ACCUMULATED UPSTREAM OF REINFORCED CHECK DAMS SHALL BE REMOVED AS NEEDED TO MAINTAIN THE EFFECTIVENESS OF BMP, TYPICALLY WHEN THE UPSTREAM SEDIMENT DEPTH IS WITHIN ½ THE HEIGHT OF THE CREST.

5. REPAIR OR REPLACE REINFORCED CHECK DAMS WHEN THERE ARE SIGNS OF DAMAGE SUCH AS HOLES IN THE GABION OR UNDERCUTTING.

6. REINFORCED CHECK DAMS ARE TO REMAIN IN PLACE UNTIL THE UPSTREAM DISTURBED AREA IS STABILIZED AND APPROVED BY THE LOCAL JURISDICTION.

7. WHEN REINFORCED CHECK DAMS ARE REMOVED, ALL DISTURBED AREAS SHALL BE COVERED WITH TOPSOIL, SEEDED AND MULCHED, AND COVERED WITH A GEOTEXTILE BLANKET, OR OTHERWISE STABILIZED AS APPROVED BY LOCAL JURISDICTION.

(DETAIL ADAPTED FROM DOUGLAS COUNTY, COLORADO AND CITY OF AURORA, COLORADO, NOT AVAILABLE IN AUTOCAD)

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

Concrete Washout Area (CWA) MM-1

Description

Concrete waste management involves designating and properly managing a specific area of the construction site as a concrete washout area. A concrete washout area can be created using one of several approaches designed to receive wash water from washing of tools and concrete mixer chutes, liquid concrete waste from dump trucks, mobile batch mixers, or pump trucks. Three basic approaches are available: excavation of a pit in the ground, use of an above ground storage area, or use of prefabricated haul-away concrete washout containers. Surface discharges of concrete washout water from construction sites are prohibited.



Photograph CWA-1. Example of concrete washout area. Note gravel tracking pad for access and sign.

Appropriate Uses

Concrete washout areas must be designated on all sites that will generate concrete wash water or liquid concrete waste from onsite concrete mixing or concrete delivery.

Because pH is a pollutant of concern for washout activities, when unlined pits are used for concrete washout, the soil must have adequate buffering capacity to result in protection of state groundwater standards; otherwise, a liner/containment must be used. The following management practices are recommended to prevent an impact from unlined pits to groundwater:

- The use of the washout site should be temporary (less than 1 year), and
- The washout site should be not be located in an area where shallow groundwater may be present, such as near natural drainages, springs, or wetlands.

Design and Installation

Concrete washout activities must be conducted in a manner that does not contribute pollutants to surface waters or stormwater runoff. Concrete washout areas may be lined or unlined excavated pits in the ground, commercially manufactured prefabricated washout containers, or aboveground holding areas constructed of berms, sandbags or straw bales with a plastic liner.

Although unlined washout areas may be used, lined pits may be required to protect groundwater under certain conditions.

Do not locate an unlined washout area within 400 feet of any natural drainage pathway or waterbody or within 1,000 feet of any wells or drinking water sources. Even for lined concrete washouts, it is advisable to locate the facility away from waterbodies and drainage paths. If site constraints make these

Concrete Washout Area	
Functions	
Erosion Control	No
Sediment Control	No
Site/Material Management	Yes

setbacks infeasible or if highly permeable soils exist in the area, then the pit must be installed with an impermeable liner (16 mil minimum thickness) or surface storage alternatives using prefabricated concrete washout devices or a lined aboveground storage area should be used.

Design details with notes are provided in Detail CWA-1 for pits and CWA-2 for aboveground storage areas. Pre-fabricated concrete washout container information can be obtained from vendors.

Maintenance and Removal

A key consideration for concrete washout areas is to ensure that adequate signage is in place identifying the location of the washout area. Part of inspecting and maintaining washout areas is ensuring that adequate signage is provided and in good repair and that the washout area is being used, as opposed to washout in non-designated areas of the site.

Remove concrete waste in the washout area, as needed to maintain BMP function (typically when filled to about two-thirds of its capacity). Collect concrete waste and deliver offsite to a designated disposal location.


Upon termination of use of the washout site, accumulated solid waste, including concrete waste and any contaminated soils, must be removed from the site to prevent on-site disposal of solid waste. If the wash water is allowed to evaporate and the concrete hardens, it may be recycled.



Photograph CWA-2. Prefabricated concrete washout. Photo courtesy of CDOT.



Photograph CWA-3. Earthen concrete washout. Photo courtesy of CDOT.

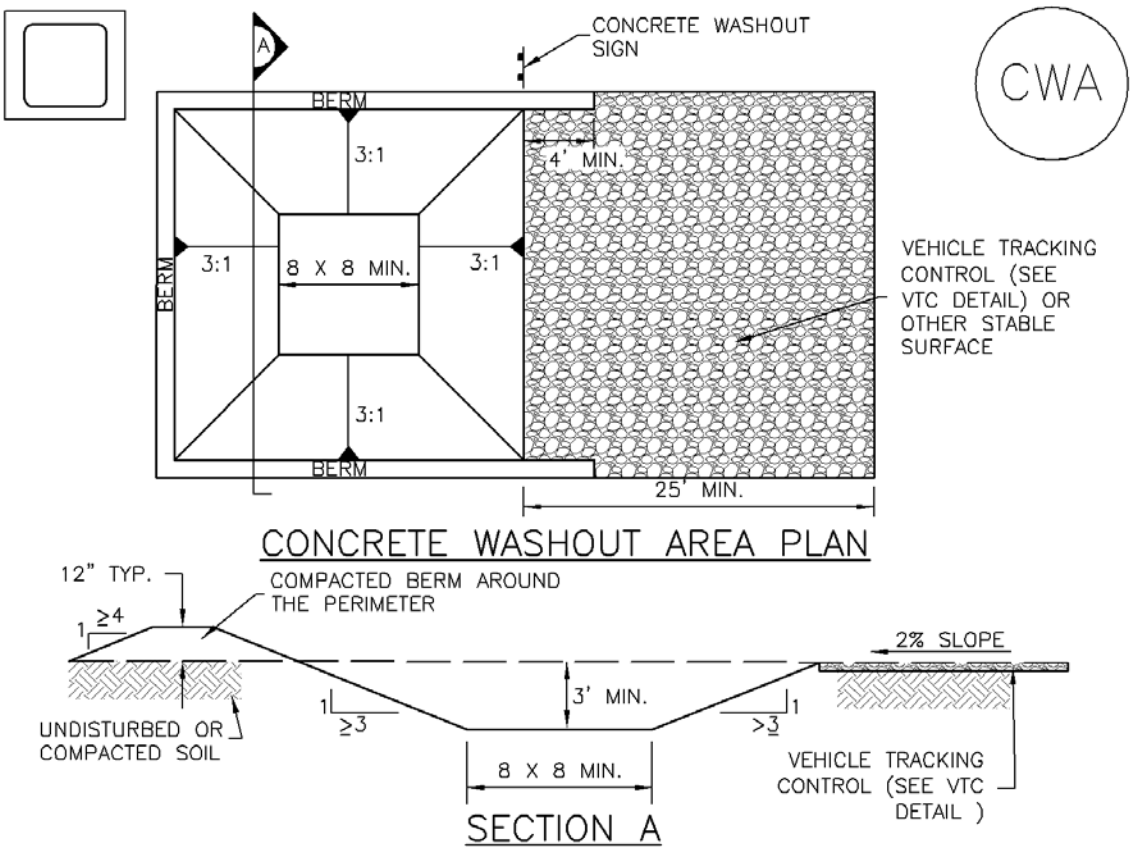

CWA–1. CONCRETE WASHOUT AREA

CWA INSTALLATION NOTES

1. SEE PLAN VIEW FOR:
   –CWA INSTALLATION LOCATION.

2. DO NOT LOCATE AN UNLINED CWA WITHIN 400' OF ANY NATURAL DRAINAGE PATHWAY OR WATERBODY. DO NOT LOCATE WITHIN 1,000' OF ANY WELLS OR DRINKING WATER SOURCES. IF SITE CONSTRAINTS MAKE THIS INFEASIBLE, OR IF HIGHLY PERMEABLE SOILS EXIST ON SITE, THE CWA MUST BE INSTALLED WITH AN IMPERMEABLE LINER (16 MIL MIN. THICKNESS) OR SURFACE STORAGE ALTERNATIVES USING PREFABRICATED CONCRETE WASHOUT DEVICES OR A LINED ABOVE GROUND STORAGE ARE SHOULD BE USED.

3. THE CWA SHALL BE INSTALLED PRIOR TO CONCRETE PLACEMENT ON SITE.

4. CWA SHALL INCLUDE A FLAT SUBSURFACE PIT THAT IS AT LEAST 8' BY 8' SLOPES LEADING OUT OF THE SUBSURFACE PIT SHALL BE 3:1 OR FLATTER. THE PIT SHALL BE AT LEAST 3' DEEP.

5. BERM SURROUNDING SIDES AND BACK OF THE CWA SHALL HAVE MINIMUM HEIGHT OF 1'.

6. VEHICLE TRACKING PAD SHALL BE SLOPED 2% TOWARDS THE CWA.

7. SIGNS SHALL BE PLACED AT THE CONSTRUCTION ENTRANCE, AT THE CWA, AND ELSEWHERE AS NECESSARY TO CLEARLY INDICATE THE LOCATION OF THE CWA TO OPERATORS OF CONCRETE TRUCKS AND PUMP RIGS.

8. USE EXCAVATED MATERIAL FOR PERIMETER BERM CONSTRUCTION.

CWA MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE.

4. THE CWA SHALL BE REPAIRED, CLEANED, OR ENLARGED AS NECESSARY TO MAINTAIN CAPACITY FOR CONCRETE WASTE. CONCRETE MATERIALS, ACCUMULATED IN PIT, SHALL BE REMOVED ONCE THE MATERIALS HAVE REACHED A DEPTH OF 2'.

5. CONCRETE WASHOUT WATER, WASTED PIECES OF CONCRETE AND ALL OTHER DEBRIS IN THE SUBSURFACE PIT SHALL BE TRANSPORTED FROM THE JOB SITE IN A WATER–TIGHT CONTAINER AND DISPOSED OF PROPERLY.

6. THE CWA SHALL REMAIN IN PLACE UNTIL ALL CONCRETE FOR THE PROJECT IS PLACED.

7. WHEN THE CWA IS REMOVED, COVER THE DISTURBED AREA WITH TOP SOIL, SEED AND MULCH OR OTHERWISE STABILIZED IN A MANNER APPROVED BY THE LOCAL JURISDICTION.

(DETAIL ADAPTED FROM DOUGLAS COUNTY, COLORADO AND THE CITY OF PARKER, COLORADO, NOT AVAILABLE IN AUTOCAD).

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

Silt Fence (SF) SC-1

Description

A silt fence is a woven geotextile fabric attached to wooden posts and trenched into the ground. It is designed as a sediment barrier to intercept sheet flow runoff from disturbed areas.



Photograph SF-1. Silt fence creates a sediment barrier, forcing sheet flow runoff to evaporate or infiltrate.

Appropriate Uses

A silt fence can be used where runoff is conveyed from a disturbed area as sheet flow. Silt fence is not designed to receive concentrated flow or to be used as a filter fabric. Typical uses include:

- Down slope of a disturbed area to accept sheet flow.
- Along the perimeter of a receiving water such as a stream, pond or wetland.
- At the perimeter of a construction site.

Design and Installation

Silt fence should be installed along the contour of slopes so that it intercepts sheet flow. The maximum recommended tributary drainage area per 100 lineal feet of silt fence, installed along the contour, is approximately 0.25 acres with a disturbed slope length of up to 150 feet and a tributary slope gradient no steeper than 3:1. Longer and steeper slopes require additional measures. This recommendation only applies to silt fence installed along the contour. Silt fence installed for other uses, such as perimeter control, should be installed in a way that will not produce concentrated flows. For example, a "J-hook" installation may be appropriate to force runoff to pond and evaporate or infiltrate in multiple areas rather than concentrate and cause erosive conditions parallel to the silt fence.

See Detail SF-1 for proper silt fence installation, which involves proper trenching, staking, securing the fabric to the stakes, and backfilling the silt fence. Properly installed silt fence should not be easily pulled out by hand and there should be no gaps between the ground and the fabric.

Silt fence must meet the minimum allowable strength requirements, depth of installation requirement, and other specifications in the design details. Improper installation of silt fence is a common reason for silt fence failure; however, when properly installed and used for the appropriate purposes, it can be highly effective.

Silt Fence	
Functions	
Erosion Control	No
Sediment Control	Yes
Site/Material Management	No


Maintenance and Removal

Inspection of silt fence includes observing the material for tears or holes and checking for slumping fence and undercut areas bypassing flows. Repair of silt fence typically involves replacing the damaged section with a new section. Sediment accumulated behind silt fence should be removed, as needed to maintain BMP effectiveness, typically before it reaches a depth of 6 inches.


Silt fence may be removed when the upstream area has reached final stabilization.



Photograph SF-2. When silt fence is not installed along the contour, a "J-hook" installation may be appropriate to ensure that the BMP does not create concentrated flow parallel to the silt fence. Photo courtesy of Tom Gore.

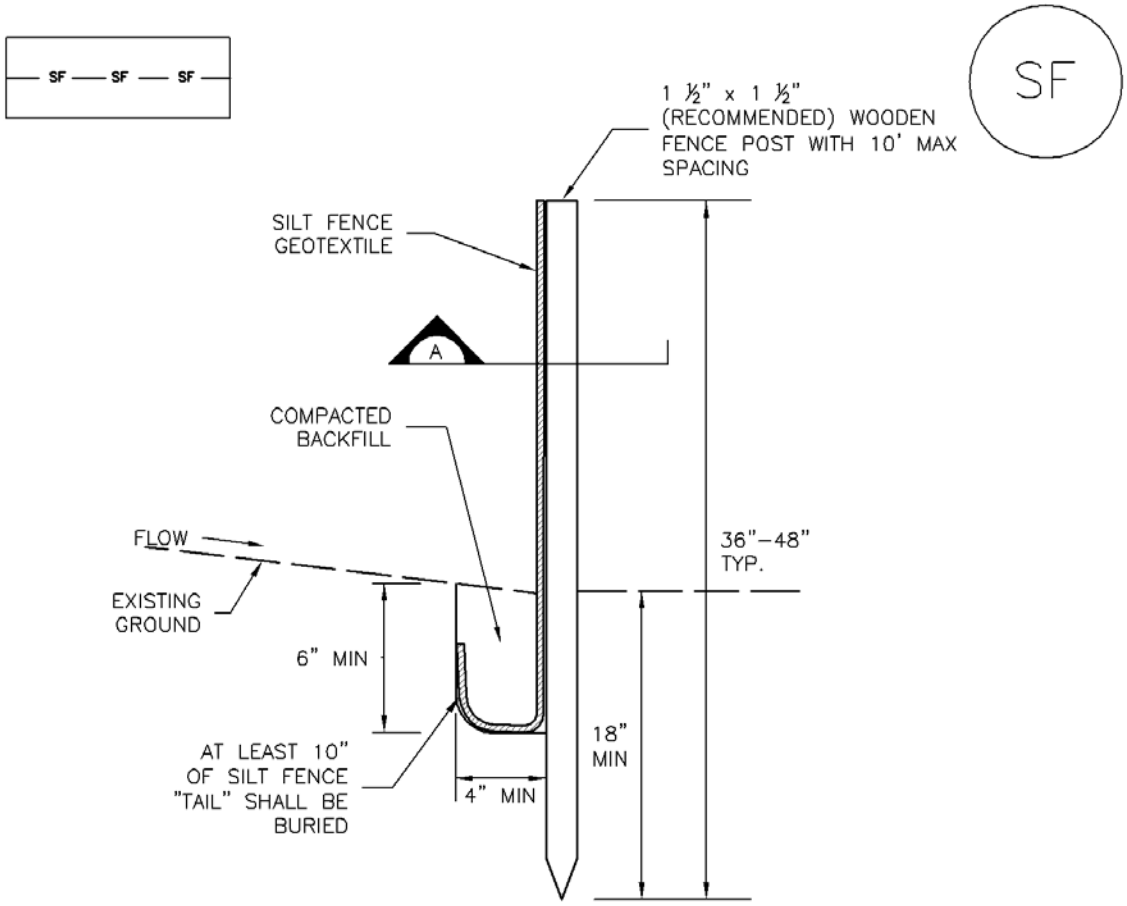

SILT FENCE

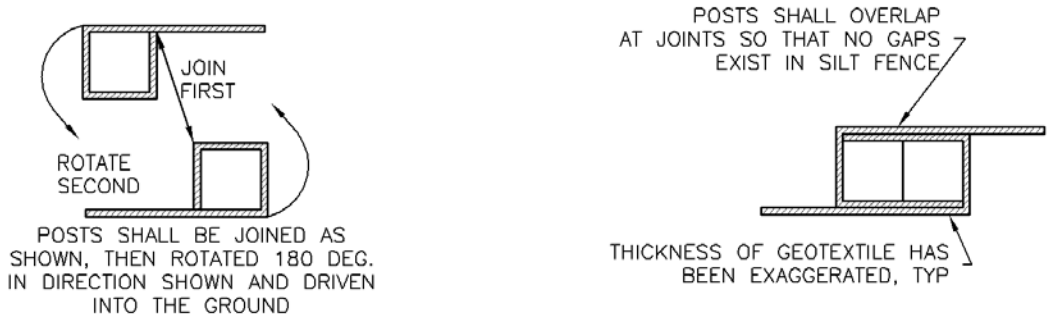

SECTION A

SF–1. SILT FENCE

SILT FENCE INSTALLATION NOTES

1. SILT FENCE MUST BE PLACED AWAY FROM THE TOE OF THE SLOPE TO ALLOW FOR WATER PONDING. SILT FENCE AT THE TOE OF A SLOPE SHOULD BE INSTALLED IN A FLAT LOCATION AT LEAST SEVERAL FEET (2–5 FT) FROM THE TOE OF THE SLOPE TO ALLOW ROOM FOR PONDING AND DEPOSITION.

2. A UNIFORM 6" X 4" ANCHOR TRENCH SHALL BE EXCAVATED USING TRENCHER OR SILT FENCE INSTALLATION DEVICE. NO ROAD GRADERS, BACKHOES, OR SIMILAR EQUIPMENT SHALL BE USED.

3. COMPACT ANCHOR TRENCH BY HAND WITH A "JUMPING JACK" OR BY WHEEL ROLLING. COMPACTION SHALL BE SUCH THAT SILT FENCE RESISTS BEING PULLED OUT OF ANCHOR TRENCH BY HAND.

4. SILT FENCE SHALL BE PULLED TIGHT AS IT IS ANCHORED TO THE STAKES. THERE SHOULD BE NO NOTICEABLE SAG BETWEEN STAKES AFTER IT HAS BEEN ANCHORED TO THE STAKES.

5. SILT FENCE FABRIC SHALL BE ANCHORED TO THE STAKES USING 1" HEAVY DUTY STAPLES OR NAILS WITH 1" HEADS. STAPLES AND NAILS SHOULD BE PLACED 3" ALONG THE FABRIC DOWN THE STAKE.

6. AT THE END OF A RUN OF SILT FENCE ALONG A CONTOUR, THE SILT FENCE SHOULD BE TURNED PERPENDICULAR TO THE CONTOUR TO CREATE A "J–HOOK." THE "J–HOOK" EXTENDING PERPENDICULAR TO THE CONTOUR SHOULD BE OF SUFFICIENT LENGTH TO KEEP RUNOFF FROM FLOWING AROUND THE END OF THE SILT FENCE (TYPICALLY 10' – 20').

7. SILT FENCE SHALL BE INSTALLED PRIOR TO ANY LAND DISTURBING ACTIVITIES.

SILT FENCE MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE.

4. SEDIMENT ACCUMULATED UPSTREAM OF THE SILT FENCE SHALL BE REMOVED AS NEEDED TO MAINTAIN THE FUNCTIONALITY OF THE BMP, TYPICALLY WHEN DEPTH OF ACCUMULATED SEDIMENTS IS APPROXIMATELY 6".

5. REPAIR OR REPLACE SILT FENCE WHEN THERE ARE SIGNS OF WEAR, SUCH AS SAGGING, TEARING, OR COLLAPSE.

6. SILT FENCE IS TO REMAIN IN PLACE UNTIL THE UPSTREAM DISTURBED AREA IS STABILIZED AND APPROVED BY THE LOCAL JURISDICTION, OR IS REPLACED BY AN EQUIVALENT PERIMETER SEDIMENT CONTROL BMP.

7. WHEN SILT FENCE IS REMOVED, ALL DISTURBED AREAS SHALL BE COVERED WITH TOPSOIL, SEEDED AND MULCHED OR OTHERWISE STABILIZED AS APPROVED BY LOCAL JURISDICTION.

(DETAIL ADAPTED FROM TOWN OF PARKER, COLORADO AND CITY OF AURORA, NOT AVAILABLE IN AUTOCAD)

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

Inlet Protection (IP) SC-6

Description

Inlet protection consists of permeable barriers installed around an inlet to filter runoff and remove sediment prior to entering a storm drain inlet. Inlet protection can be constructed from rock socks, sediment control logs, silt fence, block and rock socks, or other materials approved by the local jurisdiction. Area inlets can also be protected by over-excavating around the inlet to form a sediment trap.



Photograph IP-1. Inlet protection for a curb opening inlet.

Appropriate Uses

Install protection at storm sewer inlets that are operable during construction. Consider the potential for tracked-out sediment or temporary stockpile areas to contribute sediment to inlets when determining which inlets must be protected. This may include inlets in the general proximity of the construction area, not limited to downgradient inlets. Inlet protection is not a stand-alone BMP and should be used in conjunction with other upgradient BMPs.

Design and Installation

To function effectively, inlet protection measures must be installed to ensure that flows do not bypass the inlet protection and enter the storm drain without treatment. However, designs must also enable the inlet to function without completely blocking flows into the inlet in a manner that causes localized flooding. When selecting the type of inlet protection, consider factors such as type of inlet (e.g., curb or area, sump or on-grade conditions), traffic, anticipated flows, ability to secure the BMP properly, safety and other site-specific conditions. For example, block and rock socks will be better suited to a curb and gutter along a roadway, as opposed to silt fence or sediment control logs, which cannot be properly secured in a curb and gutter setting, but are effective area inlet protection measures.

Several inlet protection designs are provided in the Design Details. Additionally, a variety of proprietary products are available for inlet protection that may be approved for use by local governments. If proprietary products are used, design details and installation procedures from the manufacturer must be followed. Regardless of the type of inlet protection selected, inlet protection is most effective when combined with other BMPs such as curb socks and check dams. Inlet protection is often the last barrier before runoff enters the storm sewer or receiving water.

Design details with notes are provided for these forms of inlet protection:

IP-1. Block and Rock Sock Inlet Protection for Sump or On-grade Inlets

IP-2. Curb (Rock) Socks Upstream of Inlet Protection, On-grade Inlets

Inlet Protection (various forms)	
Functions	
Erosion Control	No
Sediment Control	Yes
Site/Material Management	No

IP-3. Rock Sock Inlet Protection for Sump/Area Inlet

IP-4. Silt Fence Inlet Protection for Sump/Area Inlet

IP-5. Over-excavation Inlet Protection

IP-6. Straw Bale Inlet Protection for Sump/Area Inlet

CIP-1. Culvert Inlet Protection

Propriety inlet protection devices should be installed in accordance with manufacturer specifications.

More information is provided below on selecting inlet protection for sump and on-grade locations.

Inlets Located in a Sump

When applying inlet protection in sump conditions, it is important that the inlet continue to function during larger runoff events. For curb inlets, the maximum height of the protective barrier should be lower than the top of the curb opening to allow overflow into the inlet during larger storms without excessive localized flooding. If the inlet protection height is greater than the curb elevation, particularly if the filter becomes clogged with sediment, runoff will not enter the inlet and may bypass it, possibly causing localized flooding, public safety issues, and downstream erosion and damage from bypassed flows.

Area inlets located in a sump setting can be protected through the use of silt fence, concrete block and rock socks (on paved surfaces), sediment control logs/straw wattles embedded in the adjacent soil and stacked around the area inlet (on pervious surfaces), over-excavation around the inlet, and proprietary products providing equivalent functions.

Inlets Located on a Slope

For curb and gutter inlets on paved sloping streets, block and rock sock inlet protection is recommended in conjunction with curb socks in the gutter leading to the inlet. For inlets located along unpaved roads, also see the Check Dam Fact Sheet.

Maintenance and Removal


Inspect inlet protection frequently. Inspection and maintenance guidance includes:

- Inspect for tears that can result in sediment directly entering the inlet, as well as result in the contents of the BMP (e.g., gravel) washing into the inlet.
- Check for improper installation resulting in untreated flows bypassing the BMP and directly entering the inlet or bypassing to an unprotected downstream inlet. For example, silt fence that has not been properly trenched around the inlet can result in flows under the silt fence and directly into the inlet.
- Look for displaced BMPs that are no longer protecting the inlet. Displacement may occur following larger storm events that wash away or reposition the inlet protection. Traffic or equipment may also crush or displace the BMP.
- Monitor sediment accumulation upgradient of the inlet protection.

- Remove sediment accumulation from the area upstream of the inlet protection, as needed to maintain BMP effectiveness, typically when it reaches no more than half the storage capacity of the inlet protection. For silt fence, remove sediment when it accumulates to a depth of no more than 6 inches. Remove sediment accumulation from the area upstream of the inlet protection as needed to maintain the functionality of the BMP.

- Propriety inlet protection devices should be inspected and maintained in accordance with manufacturer specifications. If proprietary inlet insert devices are used, sediment should be removed in a timely manner to prevent devices from breaking and spilling sediment into the storm drain.

Inlet protection must be removed and properly disposed of when the drainage area for the inlet has reached final stabilization.

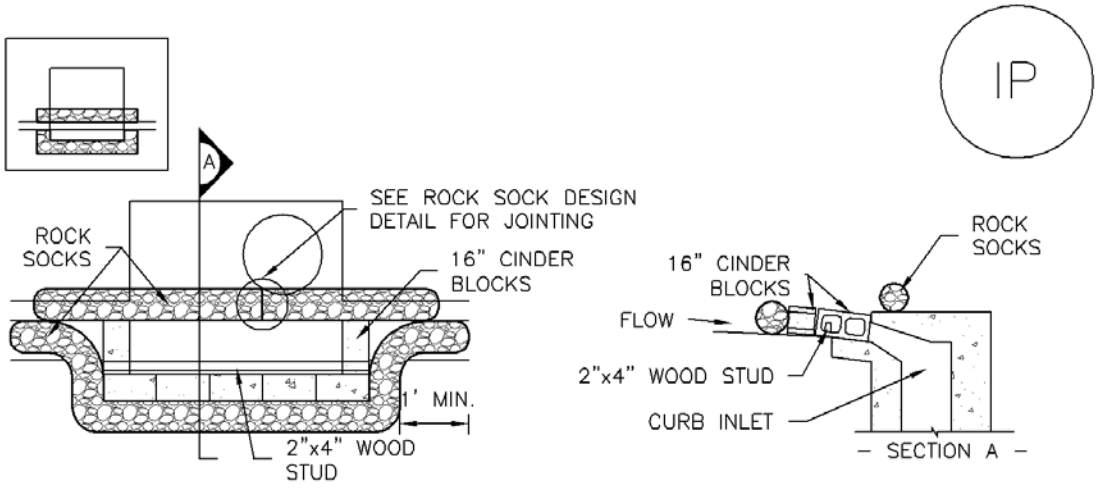


IP–1. BLOCK AND ROCK SOCK SUMP OR ON GRADE INLET PROTECTION

BLOCK AND CURB SOCK INLET PROTECTION INSTALLATION NOTES

1. SEE ROCK SOCK DESIGN DETAIL FOR INSTALLATION REQUIREMENTS.

2. CONCRETE "CINDER" BLOCKS SHALL BE LAID ON THEIR SIDES AROUND THE INLET IN A SINGLE ROW, ABUTTING ONE ANOTHER WITH THE OPEN END FACING AWAY FROM THE CURB.

3. GRAVEL BAGS SHALL BE PLACED AROUND CONCRETE BLOCKS, CLOSELY ABUTTING ONE ANOTHER AND JOINTED TOGETHER IN ACCORDANCE WITH ROCK SOCK DESIGN DETAIL.

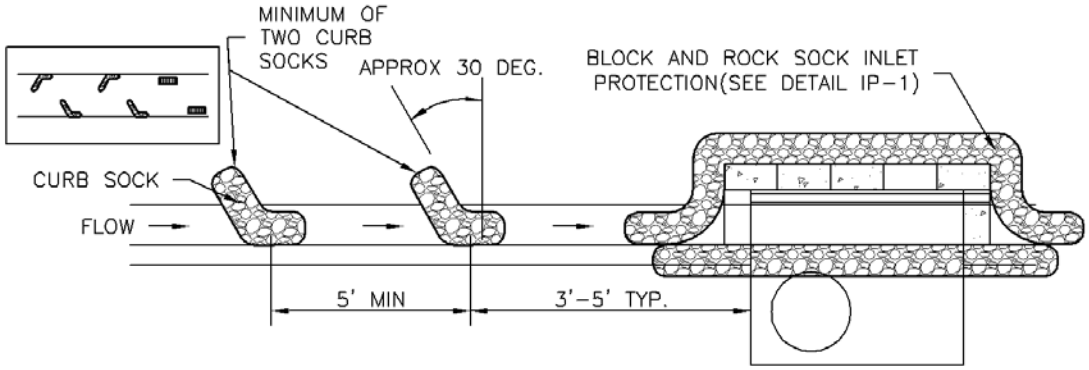

IP–2. CURB ROCK SOCKS UPSTREAM OF INLET PROTECTION


CURB ROCK SOCK INLET PROTECTION INSTALLATION NOTES

1. SEE ROCK SOCK DESIGN DETAIL INSTALLATION REQUIREMENTS.

2. PLACEMENT OF THE SOCK SHALL BE APPROXIMATELY 30 DEGREES FROM PERPENDICULAR IN THE OPPOSITE DIRECTION OF FLOW.

3. SOCKS ARE TO BE FLUSH WITH THE CURB AND SPACED A MINIMUM OF 5 FEET APART.

4. AT LEAST TWO CURB SOCKS IN SERIES ARE REQUIRED UPSTREAM OF ON–GRADE INLETS.

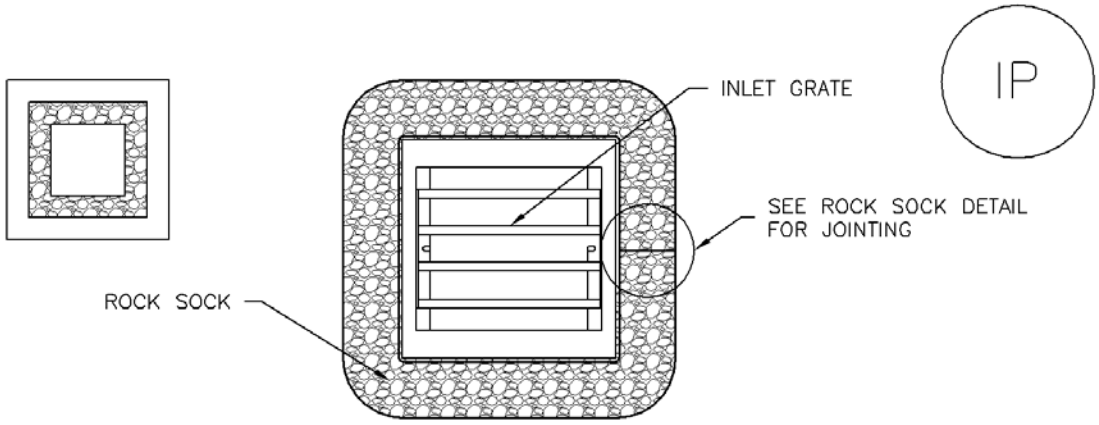


IP–3. ROCK SOCK SUMP/AREA INLET PROTECTION

ROCK SOCK SUMP/AREA INLET PROTECTION INSTALLATION NOTES

1. SEE ROCK SOCK DESIGN DETAIL FOR INSTALLATION REQUIREMENTS.

2. STRAW WATTLES/SEDIMENT CONTROL LOGS MAY BE USED IN PLACE OF ROCK SOCKS FOR INLETS IN PERVIOUS AREAS. INSTALL PER SEDIMENT CONTROL LOG DETAIL.

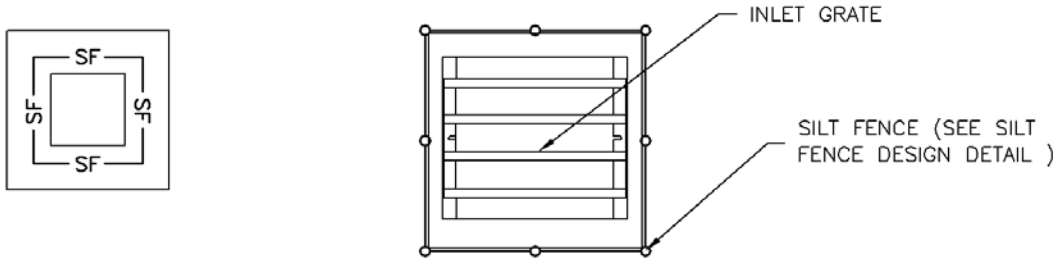


IP–4. SILT FENCE FOR SUMP INLET PROTECTION

SILT FENCE INLET PROTECTION INSTALLATION NOTES

1. SEE SILT FENCE DESIGN DETAIL FOR INSTALLATION REQUIREMENTS.

2. POSTS SHALL BE PLACED AT EACH CORNER OF THE INLET AND AROUND THE EDGES AT A MAXIMUM SPACING OF 3 FEET.

3. STRAW WATTLES/SEDIMENT CONTROL LOGS MAY BE USED IN PLACE OF SILT FENCE FOR INLETS IN PERVIOUS AREAS. INSTALL PER SEDIMENT CONTROL LOG DETAIL.

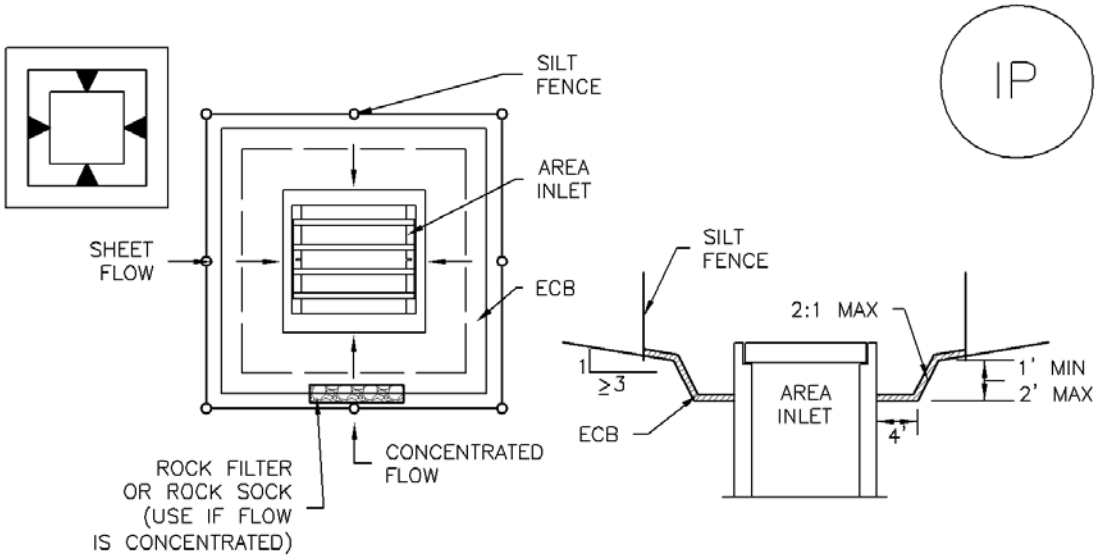


IP–5. OVEREXCAVATION INLET PROTECTION

OVEREXCAVATION INLET PROTECTION INSTALLATION NOTES

1. THIS FORM OF INLET PROTECTION IS PRIMARILY APPLICABLE FOR SITES THAT HAVE NOT YET REACHED FINAL GRADE AND SHOULD BE USED ONLY FOR INLETS WITH A RELATIVELY SMALL CONTRIBUTING DRAINAGE AREA.

2. WHEN USING FOR CONCENTRATED FLOWS, SHAPE BASIN IN 2:1 RATIO WITH LENGTH ORIENTED TOWARDS DIRECTION OF FLOW.

3. SEDIMENT MUST BE PERIODICALLY REMOVED FROM THE OVEREXCAVATED AREA.

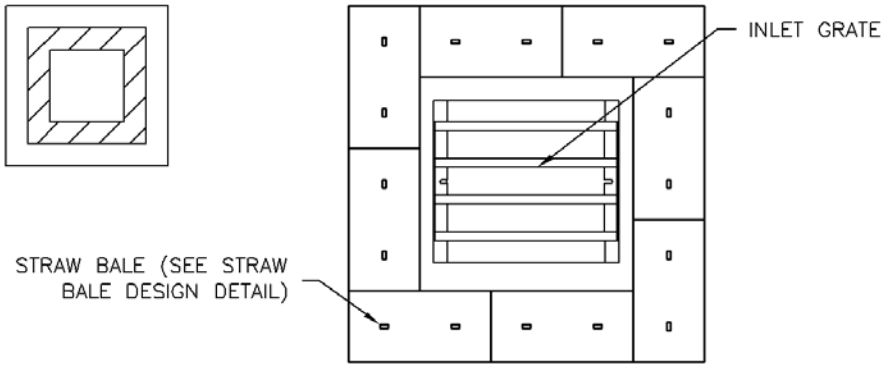


IP–6. STRAW BALE FOR SUMP INLET PROTECTION

STRAW BALE BARRIER INLET PROTECTION INSTALLATION NOTES

1. SEE STRAW BALE DESIGN DETAIL FOR INSTALLATION REQUIREMENTS.

2. BALES SHALL BE PLACED IN A SINGLE ROW AROUND THE INLET WITH ENDS OF BALES TIGHTLY ABUTTING ONE ANOTHER.

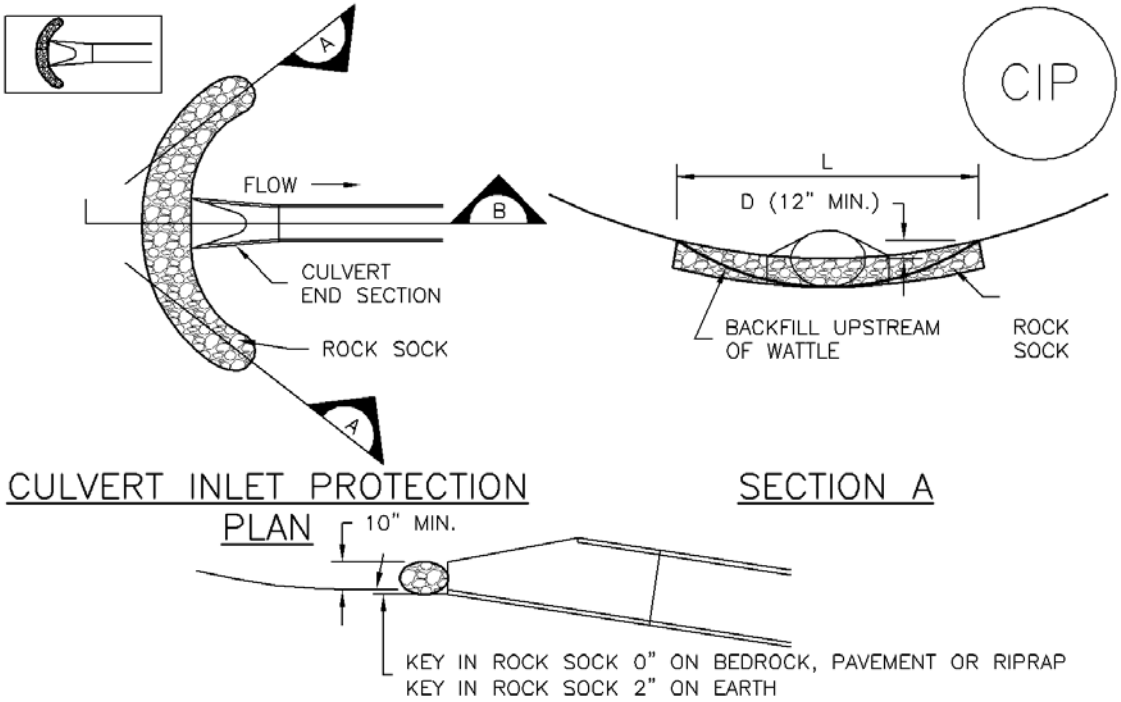

CIP–1. CULVERT INLET PROTECTION

CULVERT INLET PROTECTION INSTALLATION NOTES

1. SEE PLAN VIEW FOR
   –LOCATION OF CULVERT INLET PROTECTION.

2. SEE ROCK SOCK DESIGN DETAIL FOR ROCK GRADATION REQUIREMENTS AND JOINTING DETAIL.

CULVERT INLET PROTECTION MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE.

4. SEDIMENT ACCUMULATED UPSTREAM OF THE CULVERT SHALL BE REMOVED WHEN THE SEDIMENT DEPTH IS ½ THE HEIGHT OF THE ROCK SOCK.

5. CULVERT INLET PROTECTION SHALL REMAIN IN PLACE UNTIL THE UPSTREAM DISTURBED AREA IS PERMANENTLY STABILIZED AND APPROVED BY THE LOCAL JURISDICTION.

(DETAILS ADAPTED FROM AURORA, COLORADO, NOT AVAILABLE IN AUTOCAD)

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

GENERAL INLET PROTECTION INSTALLATION NOTES

1. SEE PLAN VIEW FOR:
   –LOCATION OF INLET PROTECTION.
   –TYPE OF INLET PROTECTION (IP.1, IP.2, IP.3, IP.4, IP.5, IP.6)

2. INLET PROTECTION SHALL BE INSTALLED PROMPTLY AFTER INLET CONSTRUCTION OR PAVING IS COMPLETE (TYPICALLY WITHIN 48 HOURS). IF A RAINFALL/RUNOFF EVENT IS FORECAST, INSTALL INLET PROTECTION PRIOR TO ONSET OF EVENT.

3. MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

INLET PROTECTION MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE.

4. SEDIMENT ACCUMULATED UPSTREAM OF INLET PROTECTION SHALL BE REMOVED AS NECESSARY TO MAINTAIN BMP EFFECTIVENESS, TYPICALLY WHEN STORAGE VOLUME REACHES 50% OF CAPACITY, A DEPTH OF 6" WHEN SILT FENCE IS USED, OR ¼ OF THE HEIGHT FOR STRAW BALES.

5. INLET PROTECTION IS TO REMAIN IN PLACE UNTIL THE UPSTREAM DISTURBED AREA IS PERMANENTLY STABILIZED, UNLESS THE LOCAL JURISDICTION APPROVES EARLIER REMOVAL OF INLET PROTECTION IN STREETS.

6. WHEN INLET PROTECTION AT AREA INLETS IS REMOVED, THE DISTURBED AREA SHALL BE COVERED WITH TOP SOIL, SEEDED AND MULCHED, OR OTHERWISE STABILIZED IN A MANNER APPROVED BY THE LOCAL JURISDICTION.

(DETAIL ADAPTED FROM TOWN OF PARKER, COLORADO AND CITY OF AURORA, COLORADO, NOT AVAILABLE IN AUTOCAD)

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

NOTE: THE DETAILS INCLUDED WITH THIS FACT SHEET SHOW COMMONLY USED, CONVENTIONAL METHODS OF INLET PROTECTION IN THE DENVER METROPOLITAN AREA. THERE ARE MANY PROPRIETARY INLET PROTECTION METHODS ON THE MARKET. UDFCD NEITHER ENDORSES NOR DISCOURAGES USE OF PROPRIETARY INLET PROTECTION; HOWEVER, IN THE EVENT PROPRIETARY METHODS ARE USED, THE APPROPRIATE DETAIL FROM THE MANUFACTURER MUST BE INCLUDED IN THE SWMP AND THE BMP MUST BE INSTALLED AND MAINTAINED AS SHOWN IN THE MANUFACTURER'S DETAILS.

NOTE: SOME MUNICIPALITIES DISCOURAGE OR PROHIBIT THE USE OF STRAW BALES FOR INLET PROTECTION. CHECK WITH LOCAL JURISDICTION TO DETERMINE IF STRAW BALE INLET PROTECTION IS ACCEPTABLE.

Stabilized Staging Area (SSA) SM-6

Description

A stabilized staging area is a clearly designated area where construction equipment and vehicles, stockpiles, waste bins, and other construction-related materials are stored. The contractor office trailer may also be located in this area. Depending on the size of the construction site, more than one staging area may be necessary.



Photograph SSA-1. Example of a staging area with a gravel surface to prevent mud tracking and reduce runoff. Photo courtesy of Douglas County.

Appropriate Uses

Most construction sites will require a staging area, which should be clearly designated in SWMP drawings. The layout of the staging area may vary depending on the type of construction activity. Staging areas located in roadways due to space constraints require special measures to avoid materials being washed into storm inlets.

Design and Installation

Stabilized staging areas should be completed prior to other construction activities beginning on the site. Major components of a stabilized staging area include:

- Appropriate space to contain storage and provide for loading/unloading operations, as well as parking if necessary.
- A stabilized surface, either paved or covered, with 3-inch diameter aggregate or larger.
- Perimeter controls such as silt fence, sediment control logs, or other measures.
- Construction fencing to prevent unauthorized access to construction materials.
- Provisions for Good Housekeeping practices related to materials storage and disposal, as described in the Good Housekeeping BMP Fact Sheet.
- A stabilized construction entrance/exit, as described in the Vehicle Tracking Control BMP Fact Sheet, to accommodate traffic associated with material delivery and waste disposal vehicles.

Over-sizing the stabilized staging area may result in disturbance of existing vegetation in excess of that required for the project. This increases costs, as well as requirements for long-term stabilization following the construction period. When designing the stabilized staging area, minimize the area of disturbance to the extent practical.

Stabilized Staging Area	
Functions	
Erosion Control	Yes
Sediment Control	Moderate
Site/Material	Yes

Minimizing Long-Term Stabilization Requirements


- Utilize off-site parking and restrict vehicle access to the site.
- Use construction mats in lieu of rock when staging is provided in an area that will not be disturbed otherwise.
- Consider use of a bermed contained area for materials and equipment that do not require a stabilized surface.
- Consider phasing of staging areas to avoid disturbance in an area that will not be otherwise disturbed.

See Detail SSA-1 for a typical stabilized staging area and SSA-2 for a stabilized staging area when materials staging in roadways is required.

Maintenance and Removal

Maintenance of stabilized staging areas includes maintaining a stable surface cover of gravel, repairing perimeter controls, and following good housekeeping practices.

When construction is complete, debris, unused stockpiles and materials should be recycled or properly disposed. In some cases, this will require disposal of contaminated soil from equipment leaks in an appropriate landfill. Staging areas should then be permanently stabilized with vegetation or other surface cover planned for the development.

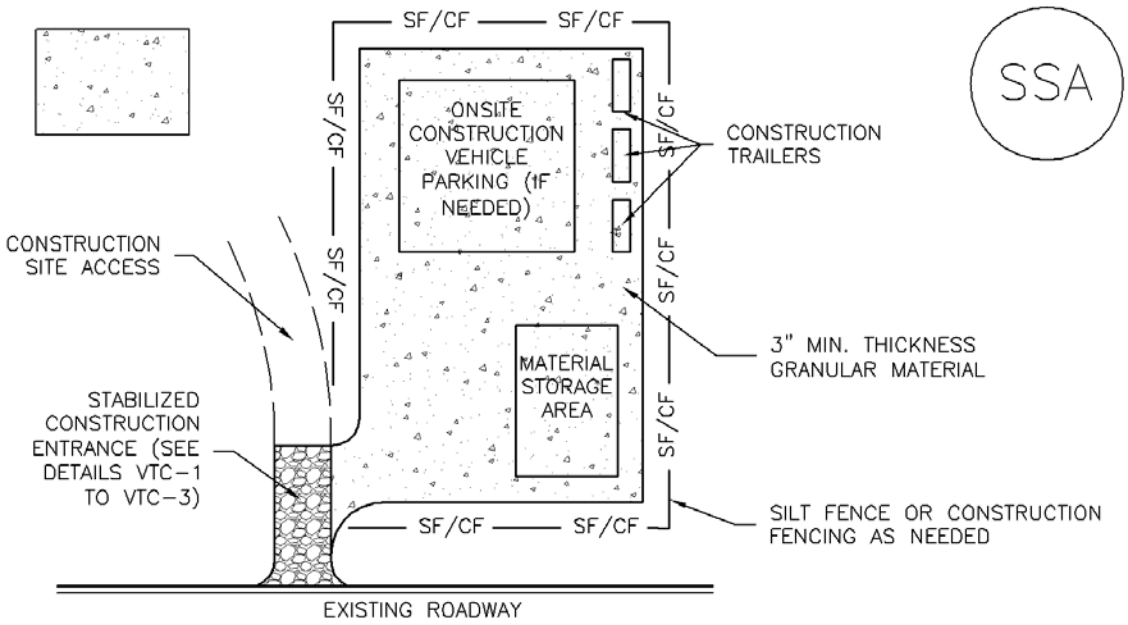

SSA–1. STABILIZED STAGING AREA

STABILIZED STAGING AREA INSTALLATION NOTES

1. SEE PLAN VIEW FOR
   –LOCATION OF STAGING AREA(S).
   –CONTRACTOR MAY ADJUST LOCATION AND SIZE OF STAGING AREA WITH APPROVAL FROM THE LOCAL JURISDICTION.

2. STABILIZED STAGING AREA SHOULD BE APPROPRIATE FOR THE NEEDS OF THE SITE. OVERSIZING RESULTS IN A LARGER AREA TO STABILIZE FOLLOWING CONSTRUCTION.

3. STAGING AREA SHALL BE STABILIZED PRIOR TO OTHER OPERATIONS ON THE SITE.

4. THE STABILIZED STAGING AREA SHALL CONSIST OF A MINIMUM 3" THICK GRANULAR MATERIAL.

5. UNLESS OTHERWISE SPECIFIED BY LOCAL JURISDICTION, ROCK SHALL CONSIST OF DOT SECT. #703, AASHTO #3 COARSE AGGREGATE OR 6" (MINUS) ROCK.

6. ADDITIONAL PERIMETER BMPs MAY BE REQUIRED INCLUDING BUT NOT LIMITED TO SILT FENCE AND CONSTRUCTION FENCING.

STABILIZED STAGING AREA MAINTENANCE NOTES

1. INSPECT BMPs EACH WORKDAY, AND MAINTAIN THEM IN EFFECTIVE OPERATING CONDITION. MAINTENANCE OF BMPs SHOULD BE PROACTIVE, NOT REACTIVE. INSPECT BMPs AS SOON AS POSSIBLE (AND ALWAYS WITHIN 24 HOURS) FOLLOWING A STORM THAT CAUSES SURFACE EROSION, AND PERFORM NECESSARY MAINTENANCE.

2. FREQUENT OBSERVATIONS AND MAINTENANCE ARE NECESSARY TO MAINTAIN BMPs IN EFFECTIVE OPERATING CONDITION. INSPECTIONS AND CORRECTIVE MEASURES SHOULD BE DOCUMENTED THOROUGHLY.

3. WHERE BMPs HAVE FAILED, REPAIR OR REPLACEMENT SHOULD BE INITIATED UPON DISCOVERY OF THE FAILURE.

4. ROCK SHALL BE REAPPLIED OR REGRADED AS NECESSARY IF RUTTING OCCURS OR UNDERLYING SUBGRADE BECOMES EXPOSED.

STABILIZED STAGING AREA MAINTENANCE NOTES

5. STABILIZED STAGING AREA SHALL BE ENLARGED IF NECESSARY TO CONTAIN PARKING, STORAGE, AND UNLOADING/LOADING OPERATIONS.

6. THE STABILIZED STAGING AREA SHALL BE REMOVED AT THE END OF CONSTRUCTION. THE GRANULAR MATERIAL SHALL BE REMOVED OR, IF APPROVED BY THE LOCAL JURISDICTION, USED ON SITE, AND THE AREA COVERED WITH TOPSOIL, SEEDED AND MULCHED OR OTHERWISE STABILIZED IN A MANNER APPROVED BY LOCAL JURISDICTION.

NOTE: MANY MUNICIPALITIES PROHIBIT THE USE OF RECYCLED CONCRETE AS GRANULAR MATERIAL FOR STABILIZED STAGING AREAS DUE TO DIFFICULTIES WITH RE-ESTABLISHMENT OF VEGETATION IN AREAS WHERE RECYCLED CONCRETE WAS PLACED.

NOTE: MANY JURISDICTIONS HAVE BMP DETAILS THAT VARY FROM UDFCD STANDARD DETAILS. CONSULT WITH LOCAL JURISDICTIONS AS TO WHICH DETAIL SHOULD BE USED WHEN DIFFERENCES ARE NOTED.

(DETAILS ADAPTED FROM DOUGLAS COUNTY, COLORADO, NOT AVAILABLE IN AUTOCAD)

Table 5-1. El Paso County Conservation District All-Purpose Mix for Upland, Transition and Permanent Control Measure Areas

Common Name	Scientific Name	Growth Season / Form	% of Mix	Pounds PLS		
				• Irrigated broadcast • Irrigated hydroseeded 80 seeds/sq ft	• Non-irrigated broadcast • Non-irrigated hydroseeded • Irrigated drilled 40 seeds/sq ft	• Non-irrigated drilled 20 seeds/sq ft
Bluestem, big	*Andropogon gerardii*	Warm, sod	20	4.4	2.2	1.1
Grama, blue	*Bouteloua gracilis*	Warm, bunch	10	0.5	0.25	0.13
Green needlegrass[2]	*Nassella viridula*	Cool, bunch	10	2	1	0.5
Wheatgrass, western[2]	*Pascopyrum smithii*	Cool, sod	20	6.4	3.2	1.6
Grama, sideoats	*Bouteloua curtipendula*	Warm, bunch	10	2	1	0.5
Switchgrass[2]	*Panicum virgatum*	Warm, bunch/sod	10	0.8	0.4	0.2
Prairie sandreed	*Calimovilfa longifolia*	Warm, sod	10	1.2	0.6	0.3
Yellow indiangrass[2]	*Sorghastrum nutans*	Warm, sod	10	2	1	0.5
			Seed rate (lbs PLS/acre)	19.3	9.7	4.8

[1]For portions of facilities located near or on the bottom or where wet soil conditions occur. Planting of potted nursery stock wetland plants 2-foot on-center is recommended for sites with wetland hydrology.

[2]Species that will do well in the bottom of pond areas.

Table 5-2. El Paso County All-Purpose Low Grow Mix for Upland and Transition Areas

Common Name	Scientific Name	Growth Season / Form	% of Mix	Pounds PLS		
				• Irrigated broadcast • Irrigated hydroseeded 80 seeds/sq ft	• Non-irrigated broadcast • Non-irrigated hydroseeded • Irrigated drilled 40 seeds/sq ft	• Non-irrigated drilled 20 seeds/sq ft
Buffalograss	*Buchloe dactyloides*	Warm, sod	25	9.6	4.8	2.4
Grama, blue	*Bouteloua gracilis*	Warm, bunch	20	10.8	5.4	2.7
Grama, sideoats	*Bouteloua curtipendula*	Warm, bunch	29	5.6	2.8	1.4
Green needlegrass	*Nassella viridula*	Cool, bunch	5	3.2	1.6	0.8
Wheatgrass, western	*Pascopyrum smithii*	Cool, sod	20	12	6	3
Dropseed, sand	*Sporobolus cryptandrus*	Warm, bunch	1	0.8	0.4	0.2
Seed rate (lbs PLS/acre)				42	21	10.3


MATERIAL PROPERTY DATA SHEET

WESTERN GREEN

TMAX™

Permanent • 3-D Woven • UV Stable •
High Performance Turf Reinforcement Mat

DESCRIPTION



TMAX is a High-Performance Turf Reinforcement Mat (HP-TRM) produced by weaving 100% UV-stabilized, high denier synthetic mono-filament yarns woven into permanent, high-strength, three-dimensional structure. The optimized properties of the material provide immediate erosion control with excellent vegetation establishment and class-leading long-term turf reinforcement. Additionally, the high strength at low elongation is ideal for slope stability applications (when paired with deep-seated, high strength anchors) and is unique compared to other HPTRMs. The design life of TMAX is rated at fifty years in typical installations, however, can vary based on conditions. TMAX is made in the USA and monitored by quality assurance testing at a GAI-LAP accredited laboratory.

Material Content	
Woven , Single Layer	Green or Tan

Standard Roll Sizes				
Width	11.5 ft	(3.5 m)	11.5 ft	(3.5 m)
Length	78 ft	(24.0 m)	156 ft	(47.5 m)
Weight ± 10%	75 lb	(35.0 kg)	150 lb	(70.0 kg)
Area	100 sy	(83.6 m^2)	200 SY	(167.0 m^2)

Material available in custom roll sizes

Approvals & Classification	
Classification	FHWA: Type 5.C / ECTC: 5.F
TTI Approvals	N/A
NTPEP Number	N/A

Index Property	Test Method	MARV	
Thickness	ASTM D6525	0.4 in.	(9 mm)
Mass/Unit Area	ASTM D6566	10.0 oz/sy	(350 g/sm)
Tensile Strength – MD	ASTM D6818	4,400 lbs/ft	(64.2 kN/m)
Tensile Strength – TD	ASTM D6818	3,300 lbs/ft	(48.2 kN/m)
Elongation - MD	ASTM D6818	35%	
Elongation – TD	ASTM D6818	30%	
UV Stability	ASTM D4355	90% @6000 hr	
UV Stability	ASTM D7238	90% @6000 hr	
Resiliency	ASTM D6524	75%	
Light Penetration	ASTM D6567	25%	
Biomass Improvement	ASTM D7322	300%	
Specific Gravity	ASTM D792	57.4 lb/ft^3	(0.92 g/cm^3)
Porosity	ECTC	96%	
Carbon Footprint	GHG*	1.9 kg CO_2 e/m^2	

Design Parameters		
Property	**Unvegetated**	**Vegetated[3]**
RUSLE C Factor[2]	N/A	N/A
Slope Maximum Gradient[1]	0.5H:1V	0.5H:1V
Permissible Shear Stress[2]	2.3 psf	16.0 psf (765 Pa)
Permissible Velocity[2]	8.0 fps	25.0 fps (7.6 m/s)
τ_{veg} / τ_{TRM} (HEC-15)	N/A	0.47

Manning's n Roughness (HEC-15)		
τ_{lower}	τ_{mid}	τ_{upper}
0.041	0.031	0.027

1 Maximum Gradient a recomendation for typical installations.
2 Hydraulic thresholds compliant with ASTM D6459/D6460 but generalized for typical applications.
3 Vegetated values dependent on established stand of vegetation
*WRI/WBCSD Greenhouse Gas Protocol: Product Life Cycle Accounting and Reporting Standard, 2013.

DIsclaimer: The information contained herein may represent product index data, performance ratings, bench scale testing or other material utility quantifications. Each representation may have unique utility and limitations. Every effort has been made to ensure accuracy, however, no warranty is claimed and no liability shall be assumed by Western Green or its affiliates regarding the completeness, accuracy or fitness of these values for any particular application or interpretation. While testing methods are provided for reference, values shown may be derived from interpolation or adjustment to be representative of intended use. For further information, please feel free to contact Western Green.

©2023, North American Green is a registered trademark from Western Green. Certain products and/or applications described or illustrated herein are protected under one or more U.S. patents. Other U.S. patents are pending, and certain foreign patents and patent applications may also exist. Trademark rights also apply as indicated herein. Final determination of the suitability of any information or material for the use contemplated, and its manner of use, is the sole responsibility of the user. Printed in the U.S.A.

Rev. 4.2023
Scan for additional and updated product information, or click here.

NORTH AMERICAN GREEN®

Western Green • 4609 E. Boonville-New Harmony Rd.
Evansville, IN 47725 • (800) 772-2040

APPENDIX D – ESQCP FORM

2880 International Circle, Suite 110
Colorado Springs, CO 80910
Phone: 719-520-6300
Email: Stormwater@elpasoco.com
publicworks.elpasoco.com/stormwater/

Stormwater Permit Number: ESQ_____

EL PASO COUNTY
STORMWATER PERMIT FORM
Erosion and Stormwater Quality Control Permit (ESQCP)

EPC Project Number: XXXX_____

There are multiple Stormwater Permits. Please refer to Engineering Criteria Manual (ECM) Appendix I to determine which permit is applicable to your project.

This form initially acts as the permit application. Only once this form has been signed & approved, all other required documents have been submitted & approved, and the Notice to Proceed has been issued, does this form become an active permit.

Part I. Property Owner or Authorized Representative (Co-Permit Holder)	
Company/Organization	Colorado Pumpkin Patch LLC
Name or Name of Representative	JD Chapman
Title	Owner
Physical Address (not PO Box)	
Street Number and Street Name	18065 Saddlewood Road
City, State, Zip Code	Monument, CO 80132
Mailing Address (if differs from above)	
Street Number and Street Name	
City, State, Zip Code	
Phone Number - Office	(719) 799-6708
Phone Number - Cell	
Email Address	Hello@coloradokidsranch.com

Part II. Contractor/Operator (Co-Permit Holder)*	
Company/Organization	
Name or Name of Representative	
Title	
Physical Address (not PO Box)	
Street Number and Street Name	
City, State, Zip Code	
Mailing Address (if differs from above)	
Street Number and Street Name	
City, State, Zip Code	
Phone Number - Office	
Phone Number - Cell	
Email Address	

*This section can be left blank through design review but must be filled in no later than at the Pre-Con Meeting.

2880 International Circle, Suite 110
Colorado Springs, CO 80910
Phone: 719-520-6300
Email: Stormwater@elpasoco.com
publicworks.elpasoco.com/stormwater/

Stormwater Permit Number: ESQ_____

EL PASO COUNTY
STORMWATER PERMIT FORM
Erosion and Stormwater Quality Control Permit (ESQCP)

EPC Project Number: XXXX

Part III. Qualified Stormwater Manager (QSM)*	
Company/Organization	
Name	
Phone Number - Office	
Phone Number - Cell	
Email Address	

*This section can be left blank through design review but must be filled in no later than at the Pre-Con Meeting.

Part IV. Project Information	
Project Name	Colorado Kids Ranch 105 Access Improvements
Address (or nearest major cross streets)	County Road 105 & Cherry Springs Ranch Drive
Acreage	Total: 1.78 acres Proposed Disturbance: 1.65 acres
Description of Project	Construction of County Road 105 improvements (widening, roadside ditch, storm sewer) for permanent access to the Colorado Kids Ranch property.
Schedule (input estimated month or season)	Start of Construction: SPRING 2027 Completion of Construction: SUMMER 2027 Final Stabilization: SUMMER 2027

2880 International Circle, Suite 110
Colorado Springs, CO 80910
Phone: 719-520-6300
Email: Stormwater@elpasoco.com
publicworks.elpasoco.com/stormwater/

Stormwater Permit Number: ESQ_____

EL PASO COUNTY
STORMWATER PERMIT FORM
Erosion and Stormwater Quality Control Permit (ESQCP)

EPC Project Number: XXXX_____

REQUIRED SUBMISSIONS

See ECM Appendix I for the documentation required to be submitted, reviewed, and approved in conjunction with this Stormwater Permit Form.

RESPONSIBILITY FOR DAMAGE

The County and its officers and employees, including but not limited to the ECM Administrator, shall not be answerable or accountable in any manner for damage to property or for injury to or death of any person, including but not limited to the Permit Holder(s), persons employed by the Permit Holder(s), or persons acting on behalf of the Permit Holder(s), from any cause. The Permit Holder(s) shall be responsible for any liability imposed by law and for damage to property or injuries to or death of any person, including but not limited to the Permit Holder(s), persons employed by the Permit Holder(s), and persons acting on behalf of the Permit Holder(s), arising out of work or other activity permitted and done under a permit, or arising out of the failure to perform the obligations under any permit with respect to maintenance or any other obligations, or resulting from defects or obstructions, or from any cause whatsoever during the progress of the work or other activity, or at any subsequent time work or other activity is being performed under the obligations provided by and contemplated by the permit.

The Permit Holder(s) shall indemnify, save, and hold harmless the County and its officers and employees, including but not limited to the Board of County Commissioners (BoCC) and ECM Administrator, from all claims, suits or actions of every name, kind and description brought for or on account of damage to property or injuries to or death of any person, including but not limited to the Permit Holder(s), persons employed by the Permit Holder(s), persons acting in behalf of the Permit Holder(s) and the public, resulting from the performance of work or other activity under the permit, or arising out of the failure to perform obligations under any permit with respect to maintenance or any other obligations, or resulting from defects or obstructions, or from any cause whatsoever during the progress of the work or other activity, or at any subsequent time work or other activity is being performed under the obligations provided by and contemplated by the permit, except as otherwise provided by state law. The Permit Holder(s) waives any and all rights to any type of expressed or implied indemnity against the County, its officers or employees. It is the intent of the parties that the Permit Holder(s) will indemnify, save, and hold harmless the County, its officers and employees from any and all claims, suits or actions as set forth above regardless of the existence or degree of fault of or negligence, whether active or passive, primary or secondary, on the part of the County, the Permit Holder(s), persons employed by the Permit Holder(s), or persons acting in behalf of the Permit Holder(s).

2880 International Circle, Suite 110
Colorado Springs, CO 80910
Phone: 719-520-6300
Email: Stormwater@elpasoco.com
publicworks.elpasoco.com/stormwater/

Stormwater Permit Number: ESQ_____

EL PASO COUNTY
STORMWATER PERMIT FORM
Erosion and Stormwater Quality Control Permit (ESQCP)

EPC Project Number: XXXX_____

APPLICATION AND PERMIT CERTIFICATION – PERMIT HOLDERS

We, as the Permit Holder(s), hereby certify that this application is correct and complete as per the requirements presented in the El Paso County Engineering Criteria Manual (ECM) and Drainage Criteria Manual (DCM) Volume 2. We, as the Permit Holder(s), have read and will comply with all of the requirements of the submitted Stormwater Management Plan (SWMP), Grading & Erosion Control (GEC) Plan, and any other documents specifying construction control measures to be used on the site, including permit conditions that may be required by the ECM Administrator. We understand that the approved plans are an enforceable part of the ESQCP. We further understand that we are to comply with all requirements set forth by the ECM and DCM Volume 2. We understand that the permitted area is that which is shown as the Limits of Disturbance on the GEC Plans. We further understand that a Construction Permit must be obtained and all necessary construction control measures are to be installed in accordance with the SWMP, GEC Plan, ECM, and DCM Volume 2 before land disturbance begins and that failure to comply will result in a Stop Work Order and may result in other penalties as allowed by law. We understand that the construction control measures are to be maintained on the site and be modified as necessary to protect stormwater quality as the project progresses. We further understand and agree to indemnify, save, and hold harmless the County and its officers and employees, including but not limited to the BoCC and ECM Administrator, from all claims, suits or actions of every name, kind and description as outlined in Responsibility for Damage section above.

_____ _____
Signature of Owner or Representative Date

_____
Print Name of Owner or Representative

_____ _____
Signature of Contractor/Operator or Representative* Date
*If signed by a Rep, an Affidavit of Signature Authority must be included

_____
Print Name of Contractor/Operator or Representative

APPLICATION AND PERMIT CERTIFICATION – EL PASO COUNTY

The following signature from the ECM Administrator signifies the approval of this ESQCP Application.

_____ _____
Signature of ECM Administrator Date

APPENDIX E – CDPS DISCHARGE PERMIT COR400000 CERTIFICATION AND COPY OF THE GENERAL PERMIT

COLORADO
Department of Public Health & Environment

Dedicated to protecting and improving the health and environment of the people of Colorado

CDPS GENERAL PERMIT COR400000

STORMWATER DISCHARGES ASSOCIATED WITH CONSTRUCTION ACTIVITY

AUTHORIZATION TO DISCHARGE UNDER THE

COLORADO DISCHARGE PERMIT SYSTEM (CDPS)

In compliance with the provisions of the Colorado Water Quality Control Act, (25-8-101 et seq., CRS, 1973 as amended) and the Federal Water Pollution Control Act, as amended (33 U.S.C. 1251 et seq.; the "Act"), this permit authorizes the discharge of stormwater associated with construction activities, as defined in this permit, to be certified under this permit from those locations authorized to discharge from authorized locations throughout the State of Colorado to specified surface waters of the state, in accordance with the eligibility and permit application requirements, effluent limitations, monitoring requirements, inspection requirements, and other conditions set forth in this general permit.

This permit specifically authorizes the facility listed on the certification to discharge in accordance with permit requirements and conditions set forth in Parts I and II hereof. All discharges authorized herein must be consistent with the terms and conditions of this permit.

This permit becomes effective on, 04/01/2024 and will expire at midnight 03/31/2029.

Issued and signed this 31st day of January, 2024 and Effective April 1, 2024.

Andrew Sayers-Fay, Permits Section Manager Water Quality Control Division

COLORADO DEPARTMENT OF PUBLIC HEALTH AND ENVIRONMENT

PERMITS ACTION SUMMARY

Issued January 31, 2024, Effective April 1, 2024

Table of Contents

PART I 2
A. COVERAGE UNDER THIS PERMIT 2
1. Authorized Discharges 2
2. Limitations on Coverage 2
3. Permit Certification and Submittal Procedures 3
B. EFFLUENT LIMITATIONS 7
1. Requirements for Control Measures Used to Meet Effluent Limitations 7
2. Discharges to an Impaired Waterbody or Outstanding Water 10
3. General Requirements 11
C. STORMWATER MANAGEMENT PLAN REQUIREMENTS 11
1. Stormwater Management Plan General Requirements 11
2. Stormwater Management Plan Content 12
3. Stormwater Management Plan Review and Revisions 14
4. Stormwater Management Plan Availability 15
D. SITE INSPECTIONS 15
1. Person Responsible for Conducting Inspections 15
2. Inspection Frequency 15
3. Inspection Frequency for Discharges to Outstanding Waters 16
4. Reduced Inspection Frequency 16
5. Inspection Scope 16
E. DEFINITIONS 18
F. MONITORING 21
G. OIL AND GAS CONSTRUCTION 21
PART II 22
A. DUTY TO COMPLY 22
B. DUTY TO REAPPLY 22
C. NEED TO HALT OR REDUCE ACTIVITY NOT A DEFENSE 22
D. DUTY TO MITIGATE 23
E. PROPER OPERATION AND MAINTENANCE 23
F. PERMIT ACTIONS 23
G. PROPERTY RIGHTS 23
H. DUTY TO PROVIDE INFORMATION 23
I. INSPECTION AND ENTRY 23
J. MONITORING AND RECORDS 24
K. SIGNATORY REQUIREMENTS 24
L. REPORTING REQUIREMENTS 25
M. BYPASS 27
N. UPSET 27
O. REOPENER CLAUSE 28
P. OTHER INFORMATION 28
Q. SEVERABILITY 28
R. NOTIFICATION REQUIREMENTS 28
S. RESPONSIBILITIES 29
T. OIL AND HAZARDOUS SUBSTANCES LIABILITY 29
U. EMERGENCY POWERS 29
V. CONFIDENTIALITY 29
W. FEES 29
X. DURATION OF PERMIT 29
Y. SECTION 307 TOXICS 29

PART I

Note: At the first mention of terminology that has a specific connotation for the purposes of this permit, the terminology is electronically linked to the definitions section of the permit in Part I.E.

A. COVERAGE UNDER THIS PERMIT

1. Authorized Discharges

This general permit authorizes permittee(s) to discharge the following to state waters: stormwater associated with construction activity and specified non-stormwater associated with construction activity. The following types of stormwater and non-stormwater discharges are authorized under this permit:

a. Stormwater Discharges

i. Stormwater discharges associated with construction activity.

ii. Stormwater discharges associated with producing earthen materials, such as soils, sand, and gravel dedicated to providing material to a single contiguous site, or within ¼ mile of the construction site covered by this permit (e.g. borrow or fill areas).

iii. Stormwater discharges associated with dedicated asphalt, concrete batch plants, and masonry mixing stations (Coverage under this permit is not required if alternative coverage has been obtained).

b. Non-Stormwater Discharges

The following non-stormwater discharges are allowable under this permit if the discharges are identified in the stormwater management plan in accordance with Part I.C and if they have appropriate control measures in accordance with Part I.B.1.

i. Discharges from uncontaminated springs that do not originate from an area of land disturbance.

ii. Discharges to the ground of concrete or masonry washout water associated with the washing of concrete or masonry tools and concrete or masonry mixer chutes, and water used to wash vehicles, equipment and external buildings. Discharges of concrete or masonry washout water must not leave the site as surface runoff or reach receiving waters as defined by this permit. The addition of soaps, solvents and detergents is prohibited. Concrete or masonry on-site waste disposal is not authorized by this permit except in accordance with Part I.B.1.a.ii(c).

iii. Discharges of landscape irrigation return flow.

iv. Discharges from diversions of state waters within the permitted site.

c. Emergency Fire Fighting

Discharges resulting from emergency firefighting activities during the active emergency response are authorized by this permit.

2. Limitations on Coverage

Discharges not authorized by this permit include, but are not limited to, the discharges and activities listed below. Permittees may seek individual or alternate general permit coverage for the discharges, or utilize low risk discharge guidance (i.e. Surface Cosmetic Power Washing Operations to Land) or clean water policy documents (i.e. Clean Water Policy #14) as appropriate and available.

a. Discharges of non-stormwater

Discharges of non-stormwater, except the authorized non-stormwater discharges listed in Part I.A.1.b., are not eligible for coverage under this permit. Note: The prohibited discharges listed here are not an exhaustive list.

i. Discharges to surface water from water used to wash vehicles, equipment and external building washdown water. The addition of soaps, solvents and detergents is prohibited.

ii. Discharges from washout water for paint, form release oils, curing compounds, or other similar

construction materials. See Part I.B.1.a.ii(f).

iii. Discharges of fuels, oils, or other pollutants used in vehicle and equipment operation and maintenance.

iv. Discharges of reclaimed water, as defined in Regulation 84, that are approved for the use of construction dust suppression but are not applied in accordance with Regulation 84.

v. Discharges related to the application of potable water for dust suppression. See Part I.B.1.a.i(j).

b. Discharges currently covered by another individual or general permit.

c. Discharges currently covered by a Water Quality Control Division (division) Low Risk Guidance document or Clean Water Policy.

d. Discharges to outstanding waters that are long-term and/or have no or only short-term ecological or water quality benefit or clear public interest. See Part I.B.2.b.

e. Chemical additions.

Any chemical addition for the treatment of stormwater associated with construction activities is not authorized. This includes but is not limited to flocculants, polymers, and coagulants.

3. Permit Certification and Submittal Procedures

a. Duty to Apply

The owner(s)/operator(s) must apply for coverage under this permit for discharges from the following activities:

i. Construction activity that will disturb one acre or more; or

ii. Construction activity that is part of a common plan of development or sale; or

iii. Stormwater discharges that are designated by the division as needing a stormwater permit because the discharge:

(a) Contributes to a violation of a water quality standard; or

(b) Is a significant contributor of pollutants to state waters.

b. Application Requirements

To obtain authorization to discharge under this permit, applicants applying for coverage following the effective date of the renewal permit must meet the following requirements:

i. Owners and operators submitting an application for permit coverage will be co-permittees subject to the same benefits, duties, and obligations under this permit.

ii. Signature requirements: Both the owner and operator (permittees) of the construction site, as defined in Part I.E., must agree to the terms and conditions of the permit and submit a completed application that includes the signature of both the owner and the operator. In cases where the duties of the owner and operator are managed by the owner, both application signatures may be completed by the owner. Both the owner and operator are responsible for ensuring compliance with all terms and conditions of the permit, including implementation of the stormwater management plan.

iii. The applicant(s) must develop a stormwater management plan in accordance with the requirements of Part I.C. The applicant(s) must also certify that the stormwater management plan is complete, or will be complete, prior to commencement of any construction activity.

iv. In order to apply for certification under this general permit, the applicant(s) must submit a complete, accurate, and signed permit application form as provided by the division by electronic delivery at least 10 days prior to the commencement of construction activity, except those construction activities that are in response to a public emergency related site. Public emergency related sites must apply for coverage no later than 14 days after the commencement of construction activities. The provisions of this part in no way remove a violation of the Colorado Water Quality Control Act if a point source discharge occurs prior to the issuance of a CDPS permit.

v. The application in its entirety must be submitted via the division's online permitting system unless a waiver is granted by the division. If a waiver is granted, the application in its entirety, including signatures by both the owner and operator, must be submitted to:

Colorado Department of Public Health and Environment

Water Quality Control Division

Permits Section, WQCD-PS-B2

4300 Cherry Creek Drive South

Denver, CO 80246

vi. The applicant(s) must receive written notification that the division granted permit coverage prior to conducting construction activities, except for construction activities that are in response to a public emergency related site.

c. Division Review of Permit Application

Within 10 days of receipt of the application, and following review of the application, the division may:

i. Issue a certification of coverage under this general permit;

ii. Request additional information necessary to evaluate the discharge;

iii. Delay the authorization to discharge pending further review;

iv. Notify the applicant that additional terms and conditions are necessary; or

v. Deny the authorization to discharge under this general permit.

d. Alternative Permit Coverage

i. Division Required Alternative Permit Coverage:

The division may require an applicant or permittee to apply for an individual permit or an alternative general permit if it determines the discharge does not fall under the scope of this general permit, including if any additional terms and conditions are necessary in order to ensure that discharges authorized by this permit will not cause, have the reasonable potential to cause, or measurably contribute to an exceedance of any applicable water quality standard, including narrative standards for water quality. In this case, the division will notify the applicant or permittee that an individual permit application is required.

ii. Permittee Request for Alternative Permit Coverage:

A permittee authorized to discharge stormwater under this permit may request to be excluded from coverage under this general permit by applying for an individual permit. In this case, the permittee must submit an individual application, with reasons supporting the request, to the division at least 180 days prior to any discharge. When an individual permit is issued, the permittee's authorization to discharge under this permit is terminated on the effective date of the individual permit.

e. Submittal Signature Requirements

Documents required for submittal to the division in accordance with this permit, including applications for permit coverage and other documents as requested by the division, must include signatures by **both** the owner and the operator, except for instances where the duties of the owner and operator are managed by the owner.

Signatures on all documents submitted to the division as required by this permit must meet the Standard Signatory Requirements in Part II.K of this permit in accordance with 40 C.F.R.122.41(k).

i. Signature Certification

Any person(s) signing documents required for submittal to the division must make the following certification:

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

f. Field Wide Permit Coverage for Oil and Gas Construction

At the discretion of the division, a single permit certification may be issued to a single oil and gas permittee to cover construction activity related discharges from an oil and gas field at multiple locations that are not necessarily contiguous.

g. Permit Coverage without Application

Qualifying Local Program: When a small construction site is within the jurisdiction of a qualifying local program, the owner and operator of the construction activity are authorized to discharge stormwater associated with small construction activity under this general permit without the submittal of an application to the division. Sites covered by a qualifying local program are exempt from the following sections of this general permit: Part I.A.3.a.; Part I.A.3.b. (division application requirements); Part I.A.3.c. (division review); Part I.A.3.d. (division alternate permit coverage); Part I.A.3.f. (oil and gas field wide coverage); Part I.A.3.h. (permittee initiated actions); Part I.A.3.i. (residential lot coverage); Part I.A.3.j. (permit expiration and continuation of coverage); Part II.L.3 (transfer of ownership or control); II.W (fees).

Sites covered by a qualifying local program are subject to the following requirements:

i. Local Agency Authority: This permit does not pre-empt or supersede the authority of local agencies to prohibit, restrict, or control discharges of stormwater to storm drain systems or other water courses within their jurisdiction.

ii. Permit Coverage Termination: When a site under a Qualifying Local Program is finally stabilized, coverage under this permit is automatically terminated.

iii. Compliance with Qualifying Local Program: Qualifying Local Program requirements that are equivalent to the requirements of this permit are incorporated by reference. Permittees authorized to discharge under this permit must comply with the equivalent requirements of the Qualifying Local Program that has jurisdiction over the site as a condition of this permit.

iv. Compliance with Remaining Permit Conditions. Requirements of this permit that are in addition to or more stringent than the requirements of the Qualifying Local Program apply in addition to the requirements of the Qualifying Local Program.

v. Written Authorization of Coverage: The division or local municipality may require any owner/operator within the jurisdiction of a Qualifying Local Program covered under this permit to apply for, and obtain written authorization of coverage under this permit. The permittee must be notified in writing that an application for written authorization of coverage is required.

h. Permittee Initiated Permit Actions

Permittee initiated permit actions, including but not limited to modifications, contact changes, transfers, and terminations, must be conducted following Part II.L, Part I.A.3.e, division guidance and using appropriate division-provided forms.

i. When a permittee modifies or terminates all or portions of permit coverage to another permittee, the "old" permittee completing the modification or termination must provide to the division the new permittee's certification number(s) (ie. a land developer selling lots to home builders, etc.).

ii. When a permittee transfers permit coverage to another permittee, the "new" permittee completing the transfer must provide to the division an agreement completed and signed by the "old" permittee.

iii. When a permittee transfers permit coverage or modifies or terminates all or portions of permit coverage to another permittee, the "old" permittee completing the transfer, modification, or termination must provide to the division documentation of due diligence when the new permittee is not obtaining permit coverage. Documentation of due diligence may include certified letters, multiple attempts at email and phone contact.

i. Sale of Residence to Homeowner

Residential construction sites only: The permittee may remove residential lots from permit coverage once the lot(s) meets all of the following criteria:

i. The residential lot(s) has(have) been sold to the homeowner(s) for private residential use;

ii. A certificate of occupancy, or equivalent, is maintained on-site or electronically and is available during division inspections;

iii. The lot(s) is (are) less than one acre of disturbance;

iv. All construction activity conducted on the lot(s) by the permittee is complete, including the installation of sediment or erosion control measures that minimize sediment from exiting the lot, or the installation of temporary stabilization on remaining disturbance where the permittee is not responsible for final stabilization (i.e. backyard of single family home, etc.);

v. The permittee is not responsible for final stabilization of the lot(s); and

vi. The stormwater management plan was modified to indicate the lot(s) is (are) no longer part of the construction activity.

If the residential lot(s) meets the criteria listed above, then activities occurring on the lot(s) are no longer considered to be construction activities with a duty to apply and maintain permit coverage. Therefore, the permittee is not required to meet the final stabilization requirements and may terminate permit coverage for the lot(s).

j. Permit Expiration and Continuation of Permit Coverage

Authorization to discharge under this general permit will expire at midnight on March 31, 2029. While Regulation 61.4 requires the permittee to submit an application for continuing permit coverage 180 days before the permit expires, the division requires that a permittee or permittees desiring continued coverage under this general permit must reapply at least 90 days in advance of this permit expiration. The division will determine if the permittee(s) may continue to discharge stormwater under the terms of the general permit. An individual permit may be required for any facility not reauthorized to discharge under the reissued general permit.

If this permit is not reissued or replaced prior to the expiration date, it will be administratively continued and remain in force and effect. For permittees that have applied for continued permit coverage, discharges authorized under this permit prior to the expiration date will automatically remain covered by this permit until the earliest of:

i. An authorization to discharge under a reissued permit, or a replacement of this permit, following the timely and appropriate submittal of a complete application requesting authorization to discharge under the new permit and compliance with the requirements of the new permit. (Note: the division may not reissue a permit certification if there are outstanding past due fees per Regulation 61.15(d)); or

ii. The issuance and effect of a termination issued by the division; or

iii. The issuance or denial of an individual permit for the facility's discharges; or

iv. A formal permit decision by the division not to reissue this general permit, at which time the division will identify a reasonable time period for covered dischargers to seek coverage under an alternative general permit or an individual permit. Coverage under this permit will cease when coverage under another permit is granted/authorized; or

v. The division has informed the permittee that discharges previously authorized under this permit are no longer covered under this permit.

B. EFFLUENT LIMITATIONS

1. Requirements for Control Measures Used to Meet Effluent Limitations

The permittee must implement control measures to minimize the discharge of pollutants from all potential pollutant sources at the site which, if applicable, includes run-on. Control measures used to meet effluent limitations must be installed prior to commencement of construction activities and prior to each phase of construction that introduces new potential pollutant sources. Control measures must be selected, designed, installed and maintained in accordance with good engineering, hydrologic and pollution control practices. Control measures implemented at the site must be designed to prevent pollution or degradation of state waters.

a. Stormwater Pollution Prevention

The permittee must implement structural and/or nonstructural control measures that effectively minimize erosion, sediment transport, and the release of other pollutants related to construction activity.

i. Control Measures for Erosion and Sediment Control

Structural and non-structural control measures for erosion and sediment control may include, but are not limited to, wattles/sediment control logs, silt fences, earthen dikes, drainage swales, sediment traps, filter bags, subsurface drains, pipe slope drains, inlet protection, outlet protection, gabions, sediment basins, temporary vegetation, permanent vegetation, mulching, geotextiles, sod stabilization, and slope roughening, maintaining existing vegetation, preserving native topsoil, protection of trees, preservation of mature vegetation, phasing of site development, preserving natural topography, minimizing soil compaction in areas of vegetative final stabilization, and minimizing site access.

Specific control measures must meet the requirements listed below.

(a) Vehicle tracking controls must be implemented to minimize vehicle tracking of sediment from disturbed areas. Vehicle tracking controls must include a structural control measure (e.g. tracking pad or wash rack) and may include a non-structural control measure (e.g. sweeping or restricting vehicle traffic to paved areas).

(b) Stormwater runoff from all disturbed areas and soil storage areas must utilize or flow to one or more control measures to minimize erosion or sediment in the discharge. The control measure(s) must be selected, designed, installed and adequately sized in accordance with good engineering, hydrologic and pollution control practices for the intended application. The control measure(s) must contain or filter flows in order to prevent the bypass of flows without treatment and must be appropriate for stormwater runoff from disturbed areas and for the expected flow rate, duration, and flow conditions (e.g. sheet or concentrated flow).

(c) Selection of control measures should prioritize the use of control measures that minimize the potential for erosion (i.e. covering materials). Selection should also prioritize phasing construction activities to minimize the amount of soil disturbance at any point in time throughout the duration of construction.

(d) Outlets that withdraw water from or near the surface must be installed when discharging from basins and impoundments, unless infeasible.

(e) Maintain pre-existing vegetation for areas within 50 horizontal feet of receiving waters as defined by this permit, unless infeasible. In addition to maintaining 50 horizontal feet of pre-existing vegetation upgradient of a receiving water (unless infeasible), the permittee must install control measures upgradient of the vegetative buffer that meets the requirements of this section, Part I.B.1.a.i.

(f) Soil compaction must be minimized for areas where infiltration control measures are implemented or where final stabilization will be achieved through vegetative cover. If compaction does occur in areas where final stabilization will be achieved through vegetative cover, then decompaction of the soil must be completed prior to planting.

(g) Unless infeasible, topsoil must be preserved for those areas of a site that will utilize vegetative final stabilization. Preserved topsoil can be left in place or stockpiled.

(h) Minimize the amount of soil exposed during construction activity, including the disturbance of steep slopes.

(i) Diversion control measures used for clean water diversions must minimize soil transport and erosion within the entire diversion, minimize erosion during discharge, and minimize run-on into the diversion. The permittee must minimize the discharge of pollutants throughout the installation, implementation and removal of the diversion. Diversions must meet one or more of the following conditions:

(1) Lined or piped structures that result in no erosion for anticipated flow conditions.

(2) Diversion channels, berms, and coffer dams must be lined or composed of a material that minimizes potential for soil loss in the entire wetted perimeter during anticipated flow conditions (e.g. vegetated swale, non-erosive soil substrate). The entire length of the diversion channel must be designed such that the maximum flow velocity for the type of material(s) exposed to the anticipated flows ensures the calculated maximum shear stress of flows in the channel is not expected to result in physical damage to the channel or liner nor result in discharge of pollutants. Additionally, the conditions relied on to minimize soil loss must be maintained for the projected life of the diversion (e.g. use of a vegetated swale must be limited to a period of time that ensures vegetative growth, minimizes erosion and maintains stable conditions).

(3) An alternative diversion criteria, approved by the division prior to implementation. The diversion method must be designed to minimize the discharge of pollutants and to prevent the potential for pollution or degradation to state waters as a result of the diverted flow through the diversion structure. In addition, the alternative diversion method must minimize the discharge of pollutants throughout the installation, implementation and removal of the diversion.

(j) Minimize dust. On areas of exposed soil, minimize dust through the appropriate application of water or other dust suppression techniques. Water application must be conducted in a manner to prevent discharge offsite unless authorized by a separate CDPS or NPDES permit.

(k) Control stormwater discharges, including both peak flowrates and total stormwater volume, to minimize channel and streambank erosion and scour in the immediate vicinity of discharge points.

ii. Practices for Other Common Pollutants

(a) Bulk storage (individual containers of 55 gallons or greater) for petroleum products and other liquid chemicals must have secondary containment, or equivalent protection, in order to contain spills and to prevent spilled material from entering state waters.

(b) Spills and leaks must be minimized. Upon identification, spills and leaks must immediately be contained and mitigated per the spill prevention and response plan, as applicable (i.e. oil, grease, fluids associated with vehicle and equipment maintenance, toxic chemicals, hazardous substances, etc.).

(c) Control measures designed for concrete washout waste, masonry operations, stucco waste, vehicle/equipment washing, and external building washdown must be implemented. This includes washout waste discharged to the ground as authorized under this permit and washout waste from concrete trucks and masonry operations contained on site. The permittee must ensure washing activities do not contribute pollutants to stormwater runoff, or receiving waters in accordance Part I.A.1.b.ii. Discharges that may reach groundwater must flow through soil that has buffering capacity prior to reaching groundwater, as necessary to meet the effluent limits in this permit, including Part I.B.3.a. The concrete or masonry washout location (including vehicle/equipment and external building washdown water, if applicable) must not be located in an area where shallow groundwater may be present and would result in buffering capacity not being adequate, such as near natural drainages, springs, or wetlands. This permit authorizes discharges to the ground of

concrete washout waste, but does not authorize on-site waste disposal per Part I.B.3.d.

(d) In the event that water remains onsite and contains pollutants either from firefighting activities or picked up from the site (i.e. in a gutter, sediment basin, etc.) after active emergency response is complete, the permittee must ensure the remaining water containing pollutants is properly removed and disposed of in order to minimize pollutants from discharging from the site, unless infeasible.

(e) Minimize the exposure of fertilizers, pesticides, and herbicides to stormwater during storage. Store and apply fertilizers, pesticides, and herbicides per manufacturer's directions.

(f) For washing applicators and containers used for paint, form release oils, curing compounds, or other similar construction materials, the wash water must be directed into a leak-proof container or leak-proof and lined pit designed so no discharges to groundwater occur or overflows occur due to inadequate sizing or precipitation. Liquid and hardened wastes must be appropriately disposed.

iii. Stabilization Requirements

The following requirements must be implemented for each site.

(a) Temporary stabilization must be implemented for earth disturbing activities on any portion of the site where ground disturbing construction activity has permanently ceased, or temporarily ceased for more than 14 calendar days. Temporary stabilization methods may include, but are not limited to, tarps, soil tackifier, and hydromulch. The permittee may exceed the 14-day schedule when either the function of the specific area of the site requires it to remain disturbed or physical characteristics of the terrain and climate prevent stabilization. The stormwater management plan must document the constraints necessitating the alternative schedule, provide the alternate stabilization schedule, and identify all locations where the alternative schedule is applicable on the site map. Minimum inspection frequency and scope, as directed in Part I.D., must be followed for temporarily stabilized areas.

(b) Final stabilization must be implemented for all construction sites covered under this permit. Final stabilization is reached when the following are complete:

(1) All construction activities are complete.

(2) Permanent stabilization methods are complete. Permanent stabilization methods include, but are not limited to, permanent pavement or concrete, hardscape, xeriscape, stabilized driving surfaces and storage areas, vegetative cover, or equivalent permanent alternative stabilization methods. The division may approve alternative final stabilization criteria for specific operations. Vegetative cover must include the following criteria:

a. Evenly distributed perennial vegetation, which may include trees and shrubs;

b. Vegetation coverage, at a minimum, equal to 70 percent of what would have been provided by native vegetation in a local, undisturbed area or adequate reference site; and

c. If applicable, adherence to stabilization requirements does not negate the permittee's requirement to comply with the local jurisdiction's plant species requirements.

(c) Final stabilization must be designed and installed as a permanent feature. All control measures must be removed from the construction site, except when the control measure specifications allow the control measure to be left in place (i.e. bio-degradable control measures, permanent sedimentation basin, etc). Final stabilization measures for obtaining a vegetative cover or alternative stabilization methods include, but are not limited to, the following as appropriate:

(1) Seed mix selection and application methods;

(2) Soil preparation and amendments;

(3) Soil stabilization methods to provide adequate protection to minimize erosion (e.g. crimped straw, hydro mulch or rolled erosion control products);

(4) Appropriate sediment control measures as needed until final stabilization is achieved;

(5) Permanent pavement, hardscape, xeriscape, stabilized driving surfaces;

(6) Conversion of construction site back to prior cropland use. The permittee is not required to plant the crop prior to termination; and

(7) Other alternative stabilization practices as applicable.

b. Routine Maintenance

The permittee must ensure that all control measures remain in effective operating condition and are protected from activities that would reduce their effectiveness. Control measures must be routinely maintained in accordance with good engineering, hydrologic and pollution control practices. Observations leading to the required routine maintenance of control measures can be made during a site inspection, or during general observations of site conditions. The necessary repairs or modifications to a control measure requiring routine maintenance, as defined in Part I.E., must be conducted to maintain an effective operating condition. Control measures requiring routine maintenance are not subject to the requirements in Part I.B.1.c below.

c. Corrective Actions

The permittee must assess the adequacy of control measures at the construction site, and the need for changes to those control measures, to ensure continued effective performance.

When an inadequate control measure, as defined in Part I.E., is identified, the following corrective action requirements apply. The permittee is not in compliance with the permit until the inadequate control measure is replaced or corrected and returned to effective operating condition in compliance with Part I.B.1 and the general requirements in Part I.B.3. If the inadequate control measure results in noncompliance that meets the conditions of Part II.L, the permittee must also meet the requirements of that section.

i. The permittee must take all necessary steps to minimize or prevent the discharge of pollutants from the permitted area and manage any stormwater run-on onto the site until a control measure is implemented and made operational and/or an inadequate control measure is replaced or corrected and returned to effective operating condition. If it is infeasible to install or repair the control measure immediately after discovering the deficiency, the following must be documented in the stormwater management plan in Part I.D.5.c and kept on record in accordance with the recordkeeping requirements in Part II.

(a) Describe why it is infeasible to initiate the installation or repair immediately; and

(b) Provide a schedule for installing or repairing the control measure and returning it to an effective operating condition as soon as possible.

ii. If applicable, the permittee must remove and properly dispose of any unauthorized release or discharge within and from the permitted area (e.g., discharge of non-stormwater, untreated stormwater containing pollutants such as sediment, spill, or leak not authorized by this permit.) The permittee must clean up any contaminated surfaces, if feasible, to minimize discharges of the material in subsequent storm events, including water remaining from the response that contains pollutants after active emergency firefighting response is complete. Permittees are prohibited from hosing down an area to clean surface spills or leaks unless the wash water is adequately captured to not discharge off the site or to land and the captured water is properly disposed. In addition, the permittee must mitigate any accumulation of sediment outside of the site boundaries.

2. Discharges to an Impaired Waterbody or Outstanding Water

a. Total Maximum Daily Load (TMDL)

If the discharge from the site of permit coverage flows to or could reasonably be expected to flow to any water body for which a TMDL has been approved, and stormwater discharges associated with construction activity were assigned a pollutant-specific Wasteload Allocation (WLA) under the TMDL, the division may:

i. Ensure the WLA is implemented properly through alternative local requirements, such as by a municipal stormwater permit; or

ii. Notify the permittee of the WLA and amend the permittee's certification to add specific effluent limits, other requirements, and compliance schedules, as necessary and appropriate. The permittee may be required to do the following:

(a) Under the permittee's stormwater management plan, implement specific control measures based on requirements of the WLA, and evaluate whether the requirements are met through implementation of existing stormwater control measures or if additional control measures are necessary. Document the calculations or other evidence demonstrating that the requirements are expected to be met; and

(b) If the evaluation shows that additional or modified control measures are necessary, describe the type and schedule for the control measure additions or modifications.

iii. Discharge monitoring may also be required. The permittee may maintain coverage under the general permit provided they comply with the applicable requirements outlined above.

b. Outstanding Waters

i. Discharges to outstanding waters must be short-term and have a long-term ecological or water quality benefit or clear public interest. A state outstanding waters map can be found here.

ii. Sites that discharge to outstanding waters are required to have an increased inspection frequency found in Part I.D.3.

c. The division may require individual or alternate general permit coverage per Part I.A.3.d.i.

3. General Requirements

a. Discharges authorized by this permit must not cause, have the reasonable potential to cause, or measurably contribute to an exceedance of any applicable water quality standard, including narrative standards for water quality.

b. The division may require sampling and testing, on a case-by-case basis, in the event that there is reason to suspect that the stormwater management plan is not adequately minimizing pollutants in stormwater or in order to measure the effectiveness of the control measures in removing pollutants in the effluent. Such monitoring may include Whole Effluent Toxicity testing.

c. The permittee must comply with the lawful requirements of federal agencies, municipalities, counties, drainage districts and other local agencies including applicable requirements in Municipal Stormwater Management Programs developed to comply with CDPS permits. The permittee must comply with local stormwater management requirements, policies and guidelines including those for erosion and sediment control.

d. The division may include additional requirements as specified in the applicable watershed protection Control Regulations 71-74.

e. All construction site wastes must be properly managed to prevent potential pollution of state waters. This permit does not authorize on-site waste disposal.

f. This permit does not relieve the permittee of the reporting requirements in 40 CFR 110, 40 CFR 117 or 40 CFR 302. Any discharge of hazardous material must be handled in accordance with the division's Noncompliance Notification Requirements (see Part II.L of the permit).

C. STORMWATER MANAGEMENT PLAN REQUIREMENTS

1. Stormwater Management Plan General Requirements

a. The permittee must develop, implement, and maintain a stormwater management plan for each construction site listed under Part I.A.3.a, including, but not limited to, construction activity that will disturb one acre or more and/or are part of a common plan of development or sale covered by this permit.

i. The plan must be prepared in accordance with good engineering, hydrologic and pollution control practices.

ii. For public emergency related sites, the plan must be created no later than 14 days after the commencement of construction activities.

b. The permittee must implement the provisions of the plan as written and updated, from commencement of construction activity until final stabilization is complete. The division may review the plan.

c. A copy of the plan must be retained onsite or be onsite when construction activities are occurring at the site unless the permittee specifies another location and obtains written approval from the division. The plan and inspection reports may be prepared, signed, and kept electronically, rather than in paper form, if the records are:

i. In a format that can be read in a similar manner as a paper record; and

ii. Immediately accessible to the inspector during an inspection to the same extent as a paper copy stored at the site would be.

2. Stormwater Management Plan Content

The stormwater management plan, at a minimum, must include the following elements.

a. Qualified Stormwater Manager. The plan must list individual(s) by title and name who are designated as responsible for implementing the stormwater management plan in its entirety and meet the definition of a Qualified Stormwater Manager. This role may be filled by more than one individual.

b. Other Permits. The plan must list the applicable CDPS permits and low-risk discharge guidance documents associated with the permitted site (including the COR400000 general permit and the certification associated with the site) and the activities occurring on the permitted site (e.g. a CDPS Dewatering Permit). The plan must also list applicable US Army Corps of Engineers Section 404 permits. A copy of this general permit, applicable permit certification, and any applicable low-risk discharge guidance documents must be included in the stormwater management plan for each construction site.

c. Site Description. The plan must include a site description which includes, at a minimum, the following:

i. The nature of the construction activity at the site, including if it is a public emergency related site;

ii. The proposed schedule for the sequence for major construction activities and the planned implementation of control measures for each phase. (e.g. clearing, grading, utilities, vertical, etc.);

iii. Estimates of the total acreage of the site, and the acreage expected to be disturbed by clearing, excavation, grading, or any other construction activities;

iv. A summary of any existing data and sources used in the development of the construction site plans or stormwater management plan that describe the soil types found in the permitted area and the erodibility of the identified soil types;

v. A description of the percent cover from native vegetation on the site if the site is undisturbed, or the percent cover from native vegetation in a similar, local undisturbed area or adequate reference area if the site is disturbed. Include the source or methodology for determining the percentage. If a percent cover is not appropriate for the site location (i.e. arid), describe the technique and justification for the identified cover of native vegetation;

vi. A description of any allowable non-stormwater discharges at the site, including those being discharged under a separate CDPS permit, discharges under Part I.A.1.b, or a division low risk discharge guidance, and applicable control measures installed;

vii. A description of the general flow direction and where or how the discharge leaves the site, including a description of the immediate conveyance or area receiving the discharge and the receiving water(s) of the discharge, if different than the immediate conveyance or area. If the stormwater discharge is to a municipal separate storm sewer system, include the name of the entity owning that system, the location(s) of the stormwater discharge, and the receiving water(s);

viii. A description of all stream crossings located within the construction site boundary, if applicable;

ix. A description of the alternate temporary stabilization schedule, if applicable (Part I.B.1.a.iii(a); and

x. A description of the alternative diversion criteria as approved by the division, if applicable (Part I.B.1.a.i(i)(3)).

xi. A description of any effluent limitations that the permittees determines are infeasible and why they are infeasible, if applicable (Part I.B.1.a.i.(d, e, and g) and I.B.1.a.ii.(d).

d. Site Map. The plan must include a site map which includes, at a minimum, the following:

i. Construction site boundaries;

ii. Flow arrows that depict stormwater flow directions on and off-site;

iii. All areas of ground disturbance including areas of borrow and fill;

iv. Areas used for storage of soil;

v. Locations of all waste accumulation areas, including areas for liquid, concrete, masonry, and asphalt;

vi. Locations of dedicated asphalt, concrete batch plants and masonry mixing stations;

vii. Locations of other potential sources of pollution not listed in iii. through vi.

viii. Locations of all structural control measures;

ix. Locations of all non-structural control measures (e.g. temporary stabilization);

x. Locations and names, as listed in Part I.C.2.c.vii, of springs, streams, wetlands, diversions and other state waters within or bordering the site, including areas that require pre-existing vegetation be maintained within 50 feet of a receiving water, where determined feasible in accordance with Part I.B.1.a.i(e) (e.g. MS4 to unnamed tributary to the South Platte River);

xi. Locations of all stream crossings located within the construction site boundary;

xii. Locations where alternative temporary stabilization schedules apply; and

e. Potential Sources of Pollution. The plan must list all potential sources of pollution which may reasonably be expected to affect the quality of stormwater discharges associated with construction activity from the site.

i. The plan must include the following pollutant sources as these pollutants relate to every construction site:

(a) Disturbed and stored soils;

(b) Vehicle tracking of sediments;

(c) On-site waste management practices (waste piles, liquid wastes, dumpsters);

ii. The plan may include, but is not limited to, the following pollutant sources:

(a) Management of contaminated soils (contaminated soils may also occur from onsite spills or leaks), if known to be present, or if contaminated soils are found during construction;

(b) Loading and unloading operations;

(c) Outdoor storage activities (erodible building materials, fertilizers, chemicals, etc.);

(d) Vehicle and equipment maintenance and fueling;

(e) Significant dust or particulate generating processes (e.g., saw cutting material, including dust);

(f) Routine maintenance activities involving fertilizers, pesticides, herbicides, detergents, fuels, solvents, oils, etc.;

(g) Concrete/masonry truck/equipment washing, including washing of the concrete truck chute and associated fixtures and equipment;

(h) Dedicated asphalt, concrete batch plants and masonry mixing stations;

(i) Non-industrial waste sources such as worker trash and portable toilets; and

(j) Reclaimed water approved for use in construction dust suppression.

f. Materials Handling. The plan must describe handling procedures of all control measures implemented at the site to minimize impacts from handling significant materials that could contribute pollutants to runoff. These handling procedures can include control measures for pollutants and activities such as, exposed storage of building materials, paints and solvents, landscape materials, fertilizers or chemicals, sanitary waste material, trash and equipment maintenance or fueling procedures.

g. Spill Prevention and Response Plan. The plan must have a spill prevention and response plan. The plan may incorporate by reference any part of a Spill Prevention Control and Countermeasure (SPCC) plan under section 311 of the Clean Water Act (CWA) or a Spill Prevention Plan required by a separate CDPS permit. The relevant sections of any referenced plans must be available as part of the stormwater management plan consistent with Part I.C.4.

h. Implementation of Control Measures. The plan must include design specifications that contain information on the implementation of all the control measures in use on the site in accordance with good engineering, hydrologic and pollution control practices; including, as applicable, drawings, dimensions, installation information, materials, implementation processes, control measure-specific inspection expectations, and maintenance requirements.

i. The plan must include a documented use agreement between the permittee and the owner or operator of any control measures located outside of the permitted area that are utilized by the permittee's construction site for compliance with this permit, but not under the direct control of the permittee. The permittee is responsible for ensuring that all control measures located outside of their permitted area, that are being utilized by the permittee's construction site, are properly maintained and in compliance with all terms and conditions of the permit. The plan must include all information required of and relevant to any such control measures located outside the permitted area, including location, installation specifications, design specifications and maintenance requirements.

j. Temporary Stabilization, Final Stabilization and Long Term Stormwater Management.

   i. The plan must document the constraints necessitating an alternative temporary stabilization schedule, as referenced in Part I.B.1.a.iii(a), provide the alternate stabilization schedule, and identify all locations where the alternative schedule is applicable on the site map.

   ii. The plan must document all residential lots that utilize the Sale of Residence to Homeowner, as referenced in Part I.A.3.i, the lots that received temporary stabilization and meet all the requirements under Part I.A.3.i, and identify all the lot locations where Part I.A.3.i is applicable on the site map.

   iii. The plan must describe or locate where all final stabilization methods are used and what methods are used to achieve final stabilization of all disturbed areas at the site (e.g. pavement, vegetative cover, etc), as listed in Part I.B.1.a.iii(b).

   iv. The plan must describe how the permittee will establish final stabilization through vegetative cover or alternative stabilization method, as referenced in Part I.B.1.a.iii(c), and describe and locate any temporary control measures in place during the process of final stabilization (e.g. seed mix, soil amendments, final stabilization methods, return to cropland, etc.).

   v. The plan must describe and locate any planned permanent control measures to control pollutants in stormwater discharges that will occur after construction operations are completed, including but not limited to, detention/retention ponds, rain gardens, stormwater vaults, etc.

k. Inspection Reports. The plan must include documented inspection reports in accordance with Part I.D.5.c.

3. Stormwater Management Plan Review and Revisions

Permittees must keep the stormwater management plan current and maintain a record of changes made that includes the date and identification of the changes. The plan must be amended when the following occurs:

a. A change in design, construction, operation, or maintenance of the site requiring implementation of new or revised control measures;

b. The plan proves ineffective in controlling pollutants in stormwater runoff in compliance with the permit conditions;

c. Control measures identified in the plan are no longer necessary and are removed;

d. Corrective actions are taken onsite that result in a change to the plan; and

e. The site or areas of the site qualifying for reduced frequency inspections under Part I.D.4.

For stormwater management plan revisions made prior to or following a change(s) onsite, including revisions to sections addressing site conditions and control measures, a notation must be included in the plan that identifies the date of the site change, the control measure removed, or modified, the location(s) of those control measures, and any changes to the control measure(s). The methods for notation may include notations on site maps, a log of changes, redline changes in the, or other measures. The permittee must ensure the site changes are reflected in the plan. The permittee is noncompliant with the permit until the plan revisions have been made.

4. Stormwater Management Plan Availability

A copy of the stormwater management plan must be provided upon request to the division, EPA, and any local agency with authority for approving sediment and erosion plans, grading plans or stormwater management plans within the time frame specified in the request. If the plan is required to be submitted to any of these entities, the submission must include a signed certification in accordance with Part I.A.3.e, certifying that the plan is complete and compliant with all terms and conditions of the permit.

All stormwater management plans required under this permit are considered reports that must be available to the public under Section 308(b) of the CWA and Section 61.5(4) of the CDPS regulations. The permittee must make plans available to members of the public upon request. However, the permittee may claim any portion of a stormwater management plan as confidential in accordance with 40 CFR Part 2.

D. SITE INSPECTIONS

Site inspections must be conducted in accordance with the following requirements. The required inspection schedules are a minimum frequency and do not affect the permittee's responsibility to implement control measures in effective operating condition as prescribed in the stormwater management plan, Part I.C.2.a.vi, as proper maintenance of control measures may require more frequent inspections. Site inspections must start within 7 calendar days of the commencement of construction activities on site.

1. Person Responsible for Conducting Inspections

The person(s) inspecting the site may be on the permittee's staff or a third party hired to conduct stormwater inspections under the direction of the permittee(s). The permittee is responsible for ensuring that the inspector meets the definition of a Qualified Stormwater Manager. The inspector may be different than the individual(s) listed in Part I.C.2.a.

2. Inspection Frequency

Permittees must conduct site inspections in accordance with one of the following minimum frequencies, unless the site meets the requirements of Part I.D.3. All inspections must be recorded per Part I.D.5.c.

a. At least one inspection every 7 calendar days; or

b. At least one inspection every 14 calendar days, if post-storm event inspections are conducted within 24 hours after the end of any precipitation or snowmelt event that causes surface erosion. Post-storm inspections may be used to fulfill the 14-day routine inspection requirement.

c. When site conditions make the schedule required in this section impractical, the permittee may petition the division to grant an alternate inspection schedule. The alternative inspection schedule must not be implemented prior to written approval by the division and incorporation into the stormwater management plan.

3. **Inspection Frequency for Discharges to Outstanding Waters**

Permittees must conduct site inspections at least once every 7 calendar days for sites that discharge to a water body designated as an Outstanding Water by the Water Quality Control Commission. In order to determine if the immediate receiving water is to an Outstanding Water, the permittee can use this map of Outstanding Waters.

4. **Reduced Inspection Frequency**

The permittee may perform site inspections at the following reduced frequencies when one of the following conditions exists:

a. Post-Storm Inspections at Temporarily Idle Sites

For permittees choosing an inspection frequency pursuant to Part I.D.2.b and if no construction activities will occur following a storm event, post-storm event inspections must be conducted prior to re-commencing construction activities, and no later than 72 hours after the end of any precipitation or snowmelt event that causes surface erosion. If the post-storm event inspection qualifies under this section, the inspection delay must be documented in the inspection record per Part I.D.5.c. Routine inspections must still be conducted at least every 14 calendar days.

b. Inspections at Sites Awaiting Final Stabilization

When the site, or portions of a site, are awaiting establishment of a vegetative ground cover and final stabilization, the permittee must conduct a thorough inspection of the construction site and control measures at least once every 30 days. Post-storm event inspections are not required under this schedule. This reduced inspection schedule is allowed if all of the following criteria are met:

i. All construction activities resulting in ground disturbance are complete;

ii. All activities required for final stabilization, in accordance with Part I.B.1.a.iii(b) & (c) and with the stormwater management plan, have been completed, with the exception of the application of sod or seed that has not occurred due to seasonal conditions or the necessity for additional seed application to augment previous efforts; and

iii. The stormwater management plan has been amended to locate those areas to be inspected in accordance with the reduced schedule allowed for in this paragraph.

c. Winter Conditions Inspections Exclusion

Typically, this exclusion applies to elevations or locations where snow melt does not occur in the winter months. Inspections are not required for sites that meet all of the following conditions:

i. Construction activities are temporarily halted for the winter season (e.g. December – February due to site being inaccessible);

ii. Snow cover exists over the entire site for an extended period (i.e. high-elevation winter season); and

iii. Melting conditions posing a risk of surface erosion do not exist.

This inspection exception is applicable only during the period where melting conditions do not exist, and applies to the routine 7-day, 14-day and monthly inspections, as well as the post-storm-event inspections. When this inspection exclusion is implemented, the following information must be documented in accordance with the requirements in Part I.C.3 and Part I.D.5.c:

(a) Dates when snow cover existed;

(b) Date when construction activities ceased; and

(c) Date melting conditions began.

5. **Inspection Scope**

a. Areas to Be Inspected

When conducting a site inspection the following areas, if applicable, must be inspected for evidence of, or

the potential for, pollutants leaving the construction site boundaries, entering the stormwater drainage system, or discharging to state waters:

i. Construction site perimeter;

ii. All disturbed areas, including areas that are temporarily stabilized;

iii. Locations of installed control measures;

iv. Designated haul routes;

v. Material and waste storage areas exposed to precipitation;

vi. Locations of pumped stormwater;

vii. Locations where stormwater has the potential to discharge offsite, including visible erosion and sedimentation; and

viii. Locations where vehicles exit the site.

b. Inspection Requirements

Inspections must assess the following components:

i. Visually verify whether all implemented control measures are in effective operational condition and are working as designed in their specifications to minimize pollutant discharges.

(a) For pumped stormwater, assessment may include sediment plume, suspended solids, unusual color, decreased clarity, presence of odor or foam, etc.

ii. Determine if there are new potential sources of pollutants.

iii. Assess the adequacy of control measures at the site to identify areas requiring new or modified control measures to minimize pollutant discharges.

iv. Identify all areas of non-compliance with the permit requirements and, if necessary, implement corrective action(s) in accordance with Part I.B.1.c.

c. Inspection Reports

The permittee must keep a record of all inspections conducted for each permitted site. Inspection reports must identify any incidents of noncompliance with the terms and conditions of this permit. All inspection reports must be signed and dated in accordance with Part I.D.5.c.xiii and xiv below. Inspection records must be retained in accordance with Part II.J. At a minimum, the inspection report must include:

i. The inspection date;

ii. Name(s) and title(s) of personnel conducting the inspection;

iii. Weather conditions at the time of inspection;

iv. Phase of construction at the time of inspection;

v. Estimated acreage of disturbance at the time of inspection;

vi. Location(s) and identification of control measures requiring routine maintenance;

vii. Location(s) and identification of discharges of sediment or other pollutants from the site;

viii. Location(s) and identification of inadequate control measures;

ix. Location(s) and identification of additional control measures needed that were not in place at the time of inspection;

x. Description of corrective action(s) for items vii, viii, ix, above, dates corrective action(s) were completed, including requisite changes to the stormwater management plan, as necessary;

xi. Description of the minimum inspection frequency (either in accordance with Part I.D.2, Part I.D.3 or Part I.D.4.) utilized when conducting each inspection;

xii. Deviations from the minimum inspection schedule as required in Part I.D.2. This would include documentation of division approval for an alternate inspection schedule outlined in Part I.D.2.c;

xiii. After adequate corrective action(s) have been taken, or where a report does not identify any incidents requiring corrective action, the report must contain the following statement and provide the date of the statement:

"I verify that, to the best of my knowledge and belief, that if any corrective action items were identified during the inspection, those corrective actions are complete, and the site is currently in compliance with the permit."; and

xiv. Inspection reports must be signed by the individual(s) designated as a Qualified Stormwater Manager, as defined in Part I.E.

E. DEFINITIONS

For the purposes of this permit:

(1) Bypass the intentional diversion of waste streams from any portion of a treatment facility in accordance with 40 CFR 122.41(m)(1)(i) and Regulation 61.2(12).

(2) Common Plan of Development or Sale - A contiguous area where multiple separate and distinct construction activities may be taking place at different times on different schedules, but remain related. The division has determined that "contiguous" means construction activities located in close proximity to each other (within ¼ mile). Construction activities are considered to be "related" if they share the same development plan, builder or contractor, equipment, storage areas, etc. "Common plan of development or sale" includes construction activities that are associated with the construction of field wide oil and gas permits for facilities that are related.

(3) Construction Activity - Ground surface disturbing and associated activities (land disturbance), which include, but are not limited to, clearing, grading, excavation, demolition, installation of new or improved haul roads and access roads, staging areas, stockpiling of fill materials, and borrow areas. Construction does not include routine maintenance to maintain the original line and grade, hydraulic capacity, or original purpose of the facility. Activities to conduct repairs that are not part of routine maintenance or for replacement are construction activities and are not routine maintenance. Repaving activities where underlying and/or surrounding soil is exposed as part of the repaving operation are considered construction activities. Construction activity is from initial ground breaking to final stabilization regardless of ownership of the construction activities.

(4) Construction Site – The location where construction activity is occurring and associated discharges are covered by this permit, including offsite locations for storage, staging, etc. For use in this permit, the terms construction site, site, and facility are used interchangeably.

(5) Control Measure - Any best management practice or other method used to prevent or reduce the discharge of pollutants to state waters. Control measures include, but are not limited to, best management practices. Control measures can include other methods such as the installation, operation, and maintenance of structural controls and treatment devices.

(6) Control Measure Requiring Routine Maintenance - Any control measure that is still operating in accordance with its design and the requirements of this permit, but requires preventative maintenance to prevent a breach of the control measure in subsequent storms.

(7) Dedicated Asphalt, Concrete Batch Plants and Masonry Mixing Stations – Are batch plants or mixing stations located on, or within ¼ mile of, a construction site and that provide materials only to that specific construction site.

(8) Disturbed area – Any ground disturbance prior to final stabilization.

(9) Diversion – Discharges of state waters that are temporarily routed through channels or structures (e.g. in-stream, uncontaminated springs, non-pumped groundwater, temporary rerouting of surface waters, fords). For purposes of this permit, these diversions can also be referred to as clean water diversions.

(10) Final Stabilization - The condition reached when construction activities at the site have been completed, permanent stabilization methods are complete, and temporary control measures are removed. Areas being stabilized with a vegetative cover must have evenly distributed perennial vegetation. The vegetation coverage must be, at a minimum, equal to 70 percent of what would have been provided by native vegetation in a local, undisturbed area or adequate reference site.

(11) Good Engineering, Hydrologic and Pollution Control Practices: are methods, procedures, and practices that:

a. Are based on basic scientific fact(s).

b. Reflect best industry practices and standards.

c. Are appropriate for the conditions and pollutant sources.

d. Provide appropriate solutions to meet the associated permit requirements, including practice based effluent limits.

(12) Inadequate Control Measure - Any control measure that is not designed or implemented in accordance with the requirements of the permit and/or any control measure that is not implemented to operate in accordance with its design.

(13) Infeasible – Not technologically possible, or not economically practicable and achievable in light of best industry practices.

(14) Minimize - Reduce or eliminate to the extent achievable using control measures that are technologically available and economically practicable and achievable in light of best industry practice.

(15) Municipality - A city, town, county, district, association, or other public body created by, or under, State law and having jurisdiction over disposal of sewage, industrial wastes, or other wastes, or a designated and approved management agency under section 208 of CWA (1987).

(16) Municipal Separate Storm Sewer System (MS4) - A conveyance or system of conveyances (including roads with drainage systems, municipal streets, catch basins, curbs, gutters, ditches, man-made channels, or storm drains):

a. Owned or operated by a State, city, town, county, district, association, or other public body (created by or pursuant to State law) having jurisdiction over disposal of sewage, industrial wastes, stormwater, or other wastes, including special districts under State law such as a sewer district, flood control district or drainage district, or similar entity, or a designated and approved management agency under section 208 of the CWA that discharges to state waters;

b. Designed or used for collecting or conveying stormwater;

c. Are not a combined sewer; and

d. Are not part of a Publicly Owned Treatment Works (POTW). See 5 CCR 1002-61.2(62).

(17) Municipal Stormwater Management Program - A stormwater program operated by a municipality, typically to meet the requirements of the municipality's MS4 discharge certification.

(18) Native Vegetation – Plant species that are naturally occurring for the particular area (or region) and have adapted to and are well suited for the soil, temperature, nutrients, and precipitation of the particular area (region).

(19) Operator - The party that has operational control over day-to-day activities at a project site which are necessary to ensure compliance with the permit. This party is authorized to direct individuals at a site to carry out activities required by the permit (i.e. the general contractor).

(20) Outstanding Waters - Waters designated as outstanding waters pursuant to Regulation 31, Section 31.8(2)(a). The highest level of water quality protection applies to certain waters that constitute an outstanding state or national resource.

(21) Owner - The party that has overall control of the activities and that has funded the implementation of the construction plans and specifications. This is the party that may have ownership of, a long term lease of, or easements on the property on which the construction activity is occurring (e.g. the developer).

(22) Permittee(s) - The owner and operator named in the discharge certification issued under this general permit for the construction site specified in the certification.

(23) Point Source - Any discernible, confined, and discrete conveyance, including, but not limited to, any pipe, ditch, channel, tunnel, conduit, well, discrete fissure, container, rolling stock, concentrated animal feeding operation, or vessel or other floating craft, from which pollutants are or may be discharged. Point source does not include irrigation return flow. See 5 CCR 102-61.2(75).

(24) Pollutant - Dredged spoil, dirt, slurry, solid waste, incinerator residue, sewage, sewage sludge, garbage, trash, chemical waste, biological nutrient, biological material, radioactive material, heat, wrecked or discarded equipment, rock, sand, or any industrial, municipal or agricultural waste. See 5 CCR 1002-61.2(76).

(25) Presentation of credentials – A government issued form of identification, if in person; or (ii) providing name, position and purpose of inspection if request to enter is made via telephone, email or other form of electronic communication. A permittee's non-response to a request to enter upon presentation of credentials constitutes a denial to such request, and may result in violation of the permit.

(26) Process Water - Any water which, during manufacturing or processing, comes into contact with or results from the production of any raw material, intermediate product, finished product, by product or waste product.

(27) Public Emergency Related Site - A project initiated in response to an unanticipated emergency (e.g., mud slides, earthquake, extreme flooding conditions, disruption in essential public services), for which the related work requires immediate authorization to avoid imminent endangerment to human health or the environment, or to reestablish essential public services.

(28) Qualified Stormwater Manager - An individual knowledgeable in the principles and practices of erosion and sediment control and pollution prevention, and with the skills to assess conditions at construction sites that could impact stormwater quality and to assess the effectiveness of stormwater control measures implemented to meet the requirements of this permit.

(29) Qualifying Local Program - A municipal program for stormwater discharges associated with small construction activity that was formally approved by the division as a qualifying local program (Regulation 61.8(12).

(30) Receiving Water - Any surface state water into which stormwater associated with construction activities discharges. Examples include all water courses, even if they are usually dry, such as borrow ditches, arroyos, and other unnamed waterways.

(31) Severe Property Damage - Substantial physical damage to property, damage to the treatment facilities which causes them to become inoperable, or substantial and permanent loss of natural resources which can reasonably be expected to occur in the absence of a bypass. Severe property damage does not mean economic loss caused by delays in production. See 40 CFR 122.41(m)(1)(ii).

(32) Significant Materials - Include, but not limited to, raw materials; fuels; materials such as solvents, detergents, and plastic pellets; finished materials such as metallic products; raw materials used in food processing or production; hazardous substances designated under section 101(14) of CERCLA; any chemical the permittee is required to report under section 313 of Title III of the Superfund Amendments and Reauthorization Act (SARA); fertilizers; pesticides; and waste products such as ashes, slag and sludge that have the potential to be released with stormwater discharges.

(33) Small Construction Activity - The discharge of stormwater from construction activities that result in land disturbance of equal to, or greater than, one acre and less than five acres. Small construction activity also includes the disturbance of less than one acre of total land area that is part of a larger common plan of development or sale, if the larger common plan ultimately disturbs equal to, or greater than, one acre and less than five acres.

(34) Spill - An unintentional release of solid or liquid material which may pollute state waters.

(35) State Waters - Any and all surface and subsurface waters which are contained in or flow in or through this state, but does not include waters in sewage systems, waters in treatment works of disposal systems, waters in potable water distribution systems, and all water withdrawn for use until use and treatment have been

completed.

(36) Steep Slopes - Where a local government, or industry technical manual (e.g. stormwater BMP manual) has defined what is to be considered a “steep slope”, this permit’s definition automatically adopts that definition. Where no such definition exists, steep slopes are automatically defined as those that are 3:1 or greater.

(37) Stormwater - Precipitation runoff, snow melt runoff, and surface runoff and drainage. See 5 CCR 1002-61.2(103).

(38) Total Maximum Daily Loads (TMDLs) - The sum of the individual wasteload allocations (WLA) for point sources and load allocations (LA) for nonpoint sources and natural background. For the purposes of this permit, a TMDL is a calculation of the maximum amount of a pollutant that a waterbody can receive and still meet water quality standards, and an allocation of that amount to the pollutant's sources. A TMDL includes WLAs, LAs, and must include a margin of safety (MOS), and account for seasonal variations. See section 303(d) of the CWA and 40 C.F.R. 130.2 and 130.7.

(39) Upset - An exceptional incident in which there is unintentional and temporary noncompliance with permit effluent limitations because of factors beyond the reasonable control of the permittee. An upset does not include noncompliance to the extent caused by operational error, improperly designed treatment facilities, inadequate treatment facilities, lack of preventative maintenance, or careless or improper operation in accordance with 40 CFR 122.41(n) and Regulation 61.2(114).

F. MONITORING

The division may require sampling and testing, on a case-by-case basis. If the division requires sampling and testing, the division will send a notification to the permittee. Sampling and reporting procedures for any monitoring data collected will be included in the notification.

If monitoring is required, the following applies:

The thirty (30) day average must be determined by the arithmetic mean of all samples collected during a thirty (30) consecutive-day period; and

A grab sample, for monitoring requirements, is a single “dip and take” sample.

G. OIL AND GAS CONSTRUCTION

Stormwater discharges associated with construction activities directly related to oil and gas exploration, production, processing, and treatment operations or transmission facilities are regulated under the Colorado Discharge Permit System Regulations (5 CCR 1002-61), and require coverage under this permit in accordance with that regulation. However, references in this permit to specific authority under the CWA do not apply to stormwater discharges associated with these oil and gas related construction activities, to the extent that the references are limited by the federal Energy Policy Act of 2005.

PART II

Part II contains standard conditions required by federal regulation to be included in all NPDES permits (see 40 C.F.R. 122.41). Part I contains permit specific requirements.

A. DUTY TO COMPLY

1. The permittee must comply with all conditions of this permit. Any permit noncompliance constitutes a violation of the Colorado Water Quality Control Act and is grounds for: 1) enforcement action; 2) permit termination, revocation and reissuance, or modification; or 3) denial of a permit renewal application.
2. Federal Enforcement:
   a. The permittee shall comply with effluent standards or prohibitions established under section 307(a) of the Clean Water Act for toxic pollutants and with standards for sewage sludge use or disposal (see 40 CFR 122.2) established under section 405(d) of the CWA within the time provided in the regulations that establish these standards or prohibitions or standards for sewage sludge use or disposal, even if the permit has not yet been modified to incorporate the requirement.
   b. The Clean Water Act provides that any person who violates section 301, 302, 306, 307, 308, 318 or 405 of the Act, or any permit condition or limitation implementing any such sections in a permit issued under section 402, or any requirement imposed in a pretreatment program approved under sections 402(a)(3) or 402(b)(8) of the Act, is subject to a civil penalty not to exceed $25,000 per day for each violation. The Clean Water Act provides that any person who *negligently* violates sections 301, 302, 306, 307, 308, 318, or 405 of the Act, or any condition or limitation implementing any of such sections in a permit issued under section 402 of the Act, or any requirement imposed in a pretreatment program approved under section 402(a)(3) or 402(b)(8) of the Act, is subject to criminal penalties of $2,500 to $25,000 per day of violation, or imprisonment of not more than 1 year, or both. In the case of a second or subsequent conviction for a negligent violation, a person shall be subject to criminal penalties of not more than $50,000 per day of violation, or by imprisonment of not more than 2 years, or both. Any person who *knowingly* violates such sections, or such conditions or limitations is subject to criminal penalties of $5,000 to $50,000 per day of violation, or imprisonment for not more than 3 years, or both. In the case of a second or subsequent conviction for a knowing violation, a person shall be subject to criminal penalties of not more than $100,000 per day of violation, or imprisonment of not more than 6 years, or both. Any person who knowingly violates section 301, 302, 303, 306, 307, 308, 318 or 405 of the Act, or any permit condition or limitation implementing any of such sections in a permit issued under section 402 of the Act, and who knows at that time that he thereby places another person in imminent danger of death or serious bodily injury, shall, upon conviction, be subject to a fine of not more than $250,000 or imprisonment of not more than 15 years, or both. In the case of a second or subsequent conviction for a knowing endangerment violation, a person shall be subject to a fine of not more than $500,000 or by imprisonment of not more than 30 years, or both. An organization, as defined in section 309(c)(3)(B)(iii) of the CWA, shall, upon conviction of violating the imminent danger provision, be subject to a fine of not more than $1,000,000 and can be fined up to $2,000,000 for second or subsequent convictions.
   c. Any person may be assessed an administrative penalty by the Administrator for violating section 301, 302, 306, 307, 308, 318 or 405 of this Act, or any permit condition or limitation implementing any of such sections in a permit issued under section 402 of this Act. Administrative penalties for Class I violations are not to exceed $10,000 per violation, with the maximum amount of any Class I penalty assessed not to exceed $25,000. Penalties for Class II violations are not to exceed $10,000 per day for each day during which the violation continues, with the maximum amount of any Class II penalty not to exceed $125,000.

B. DUTY TO REAPPLY

If the permittee plans to continue an activity regulated by this permit after the expiration date of this permit, the permittee must submit a permit application at least 180 days before this permit expires as required by Regulations 61.4 and 61.10.

C. NEED TO HALT OR REDUCE ACTIVITY NOT A DEFENSE

It shall not be a defense for a permittee in an enforcement action that it would have been necessary to halt or

reduce the permitted activity in order to maintain compliance with the conditions of this permit.

D. DUTY TO MITIGATE

The permittee must take all reasonable steps to minimize or prevent any discharge or sludge use or disposal in violation of this permit which has a reasonable likelihood of adversely affecting human health or the environment.

E. PROPER OPERATION AND MAINTENANCE

The permittee must at all times properly operate and maintain all facilities and systems of treatment and control (and related appurtenances) that are installed or used by the permittee to achieve compliance with the conditions of this permit. Proper operation and maintenance also includes adequate laboratory controls and appropriate quality assurance procedures. This provision requires the operation of backup or auxiliary facilities or similar systems which are installed by a permittee only when the operation is necessary to achieve compliance with the conditions of this permit. See 40 C.F.R. §122.41(e).

F. PERMIT ACTIONS

This permit may be modified, revoked and reissued, or terminated for cause. The filing of a request for a permit modification, revocation and reissuance, or termination, or a notification of planned changes or anticipated noncompliance does not stay any permit condition. Any request for modification, revocation, reissuance, or termination under this permit must comply with all terms and conditions of Regulation 61.8(8). See also 40 C.F.R. § 122.41(f).

G. PROPERTY RIGHTS

In accordance with 40 CFR §122.41(g) and Regulation 61.8(9): The issuance of a permit does not convey any property or water rights in either real or personal property, or stream flows or any exclusive privilege.

1. The issuance of a permit does not authorize any injury to person or property or any invasion of personal rights, nor does it authorize the infringement of federal, state, or local laws or regulations.
2. Except for any toxic effluent standard or prohibition imposed under Section 307 of the Clean Water Act or any standard for sewage sludge use or disposal under Section 405(d) of the Federal act, compliance with a permit during its term constitutes compliance, for purposes of enforcement, with Sections 301, 302, 306, 318, 403, and 405(a) and (b) of the Clean Water Act. However, a permit may be modified, revoked and reissued, or terminated during its term for cause as set forth in Section 61.8(8) of the Colorado Discharge Permit System Regulations. See 61.8(9)(c).

H. DUTY TO PROVIDE INFORMATION

The permittee shall furnish to the Division, within a reasonable time, any information which the Division may request to determine whether cause exists for modifying, revoking and reissuing, or terminating this permit, or to determine compliance with this permit. The permittee shall also furnish to the Division, upon request, copies of records required to be kept by this permit in accordance with 40 C.F.R. §122.41(h) and/or Regulation 61.8(3)(q).

I. INSPECTION AND ENTRY

The permittee shall allow the Division and the authorized representative, including U.S. EPA, and/or their authorized representatives (including an authorized contractor acting as their representative), upon the presentation of credentials as required by law, to conduct inspections in accordance with 40 C.F.R. §122.41(i), Regulation 61.8(3), and Regulation 61.8(4):

1. To enter upon the permittee's premises where a regulated facility or activity is located or conducted in which any records are required to be kept under the terms and conditions of this permit;
2. At reasonable times to have access to and copy any records required to be kept under the terms and conditions of this permit and to inspect any facilities, equipment (including monitoring and control equipment), practices, operations or monitoring method regulated or required in the permit;
3. To enter upon the permittee's premises in a reasonable manner and at a reasonable time to inspect or investigate, any actual, suspected, or potential source of water pollution, or to ascertain compliance or noncompliance with the Colorado Water Quality Control Act or any other applicable state or federal statute or regulation or any order promulgated by the Division, and;

4. Sample or monitor at reasonable times, for the purposes of assuring permit compliance or as otherwise authorized by the Clean Water Act, any substances or parameters at any location.

J. MONITORING AND RECORDS

1. Samples and measurements taken for the purpose of monitoring must be representative of the volume and nature of the monitored activity. See 40 C.F.R. § 122.41(j)(1).

2. Monitoring must be conducted according to test procedures approved under 40 C.F.R. part 136 for the analyses of pollutants unless another method is required under 40 C.F.R. subchapters N or O. In the case of pollutants for which there are no approved methods under 40 C.F.R. part 136 or otherwise required under 40 C.F.R. subchapters N or O, monitoring must be conducted according to a test procedure specified in this permit for such pollutants. See 40 C.F.R. § 122.41(j)(4); 122.44(i)(1)(iv)(A).

3. Except for records of monitoring information required by this permit related to the permittee's sewage sludge use and disposal activities, which shall be retained for a period of at least five years (or longer as required by 40 CFR part 503), the permittee shall retain records of all monitoring information, including all calibration and maintenance records and all original strip chart recordings for continuous monitoring instrumentation, copies of all reports required by this permit, and records of all data used to complete the application for this permit, for a period of at least 3 years from the date of the sample, measurement, report or application. This period of retention shall be extended during the course of any unresolved litigation regarding the discharge of pollutants by the permittee or when requested by the Division or Regional Administrator.

4. Records of monitoring information must include:

   a. The date, exact place, and time of sampling or measurements;
   b. The individual(s) who performed the sampling or measurements;
   c. The date(s) analyses were performed
   d. The individual(s) who performed the analyses;
   e. The analytical techniques or methods used; and
   f. The results of such analyses.

5. The permittee shall install, calibrate, use and maintain monitoring methods and equipment, including biological and indicated pollutant monitoring methods. See Regulation 61.8(4)(b)(iii). All sampling shall be performed by the permittee according to sufficiently sensitive test procedures required by 40 C.F.R. 122.44(i)(1)(iv) or methods approved by the Division, in the absence of a method specified in or approved pursuant to 40 C.F.R. Part 136.

6. The CWA provides that any person who falsifies, tampers with, or knowingly renders inaccurate any monitoring device or method required to be maintained under this permit shall, upon conviction, be punished by a fine of not more than $10,000, or by imprisonment for not more than 2 years, or both. If a conviction of a person is for a violation committed after a first conviction of such person under this paragraph, punishment is a fine of not more than $20,000 per day of violation, or by imprisonment of not more than 4 years, or both.

7. Documentation required by this permit, including records of all data used to complete the application for permit coverage to be covered by this permit, stormwater management plans, inspection reports, etc., must be retained for at least three years from the date that permit coverage expires or is terminated. This period may be extended by request of EPA or the division at any time.

K. SIGNATORY REQUIREMENTS

1. Authorization to Sign: All documents required to be submitted to the Division by the permit must be signed in accordance with 40 CFR §122.22, Regulation 61.4, and the following criteria:

   a. For a corporation: By a responsible corporate officer. For the purpose of this subsection, a responsible corporate officer means: (i) a president, treasurer, or vice president of the corporation in charge of a principal business function, or any other person who performs similar policy- or decision-making functions for the corporation, or (ii) the manager of one or more manufacturing, production, or operating facilities, provided, the manager is authorized to make management decisions which govern the operation of the regulated facility including having the explicit or implicit duty of making major capital investment recommendations, and initiating and directing other comprehensive measures to assure long term

environmental compliance with environmental laws and regulations; the manager can ensure that the necessary systems are established or actions taken to gather complete and accurate information for permit application requirements; and where authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures. The responsible official may be a project manager if the project manager has level of control at a corporation as required in this subpart a.

b. For a partnership or sole proprietorship: By a general partner or the proprietor, respectively; or
c. For a municipality, state, federal, or other public agency: By either a principal executive officer or ranking elected official. For purposes of this subsection, a principal executive officer of a federal agency includes (i) the chief or principal executive officer of the agency, or (ii) a senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency. (e.g., Regional Administrator of EPA), and at the city, municipal, state or other government entity it typically will include a program director (e.g. Director of Public Works, Director of Transportation, Director of Parks and Recreation, etc.). For purposes of this section, a principal executive officer has responsibility for the overall operation of the facility from which the discharge originates.
d. By a duly authorized representative in accordance with 40 C.F.R. 122.22(b), only if:

   i. the authorization is made in writing by a person described in Part II.K.1.a, b, or c above;
   ii. The authorization specifies either an individual or a position having responsibility for the overall operation of the regulated facility or activity such as the position of plant manager, operator of a well or a well field, superintendent, position of equivalent responsibility, or an individual or position having overall responsibility for environmental matters for the company. (A duly authorized representative may thus be either a named individual or any individual occupying a named position); and,
   iii. The written authorization is submitted to the Division.

2. Any person(s) signing documents required for submittal to the Division must make the following certification:

   "I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

3. The CWA provides that any person who knowingly makes any false statement, representation, or certification in any record or other document submitted or required to be maintained under this permit, including monitoring reports or reports of compliance or non-compliance shall, upon conviction, be punished by a fine of not more than $10,000 per violation, or by imprisonment for not more than 6 months per violation, or by both. See 40 C.F.R. §122.41(k)(2).

L. REPORTING REQUIREMENTS

1. Planned Changes: The permittee shall give advance notice to the Division, in writing, of any planned physical alterations or additions to the permitted facility in accordance with 40 CFR §122.41(l) and Regulation 61.8(5)(a) and Part II.O. of this permit. Notice is required only when:

   a. The alteration or addition to a permitted facility may meet one of the criteria for determining whether a facility is a new source in 40 CFR §122.29(b); or
   b. The alteration or addition could significantly change the nature or increase the quantity of pollutants discharged. This notification applies to pollutants which are subject neither to effluent limitations in the permit, nor to notification requirements under 40 CFR §122.41(a)(1).
   c. The alteration or addition results in a significant change in the permittee's sludge use or disposal practices, and such alteration, addition, or change may justify the application of permit conditions that are different from or absent in the existing permit, including notification of additional use or disposal sites not reported during the permit application process or not reported pursuant to an approved land application plan. See 40 C.F.R. §122.41(l)(1)(iii).

2. Anticipated Non-Compliance: The permittee shall give advance notice to the Division, in writing, of any planned changes in the permitted facility or activity that may result in noncompliance with permit requirements. The timing of notification requirements differs based on the type of non-compliance as described below.

3. Transfer of Ownership or Control: The permittee shall notify the Division, in writing, ten (10) calendar days in advance of a proposed transfer of the permit. The notice must include a written agreement between the existing and new permittee(s) containing a specific date for transfer of permit responsibility, coverage and liability between them. This permit is not transferable to any person except after notice to the Division. The Division may require modification or revocation and reissuance of the permit to change the name of the permittee and incorporate such other requirements as may be necessary under the Clean Water Act. See Regulation 61.8(6); 40 C.F.R. §§ 122.41(l)(iii) and 122.61.

4. Monitoring reports: Monitoring results must be reported at the intervals specified in this permit.

   a. If the permittee monitors any pollutant at the approved monitoring locations listed in Part I more frequently than that required by this permit using test procedures approved under 40 CFR Part 136, or another method required for an industry-specific waste stream under 40 CFR subchapters N or O, the results of such monitoring shall be included in the calculation and reporting of the data submitted in the DMR or sludge reporting form specified by the Division. See 40 CFR 122.41(l)(4).
   b. Calculations for all limitations which require averaging of measurements shall utilize an arithmetic mean unless otherwise specified by the Division in the permit.

5. Submission of Discharge Monitoring Reports (DMRs): DMRs shall be submitted electronically through NetDMR system unless the permittee requests and is granted a waiver of the electronic reporting requirement by the Division pursuant to Regulation 61.8(4)(d).

6. Compliance Schedules: Reports of compliance or noncompliance with, or any progress reports on, interim and final requirements contained in any compliance schedule in the permit, shall be submitted on or before the date listed in the compliance schedule section. The fourteen (14) calendar day provision in Regulation 61.8(4)(n)(i) has been incorporated into the due date.

7. Twenty-four hour reporting:

   a. In addition to the reports required elsewhere in this permit, the permittee shall report the following circumstances on the Division's submission form within twenty-four (24) hours from the time the permittee becomes aware of the circumstances, and shall submit to the Division a written report containing the information requested within five (5) working days after becoming aware of the following circumstances:
      i. Circumstances leading to any noncompliance which may endanger health or the environment regardless of the cause of the incident;
      ii. Circumstances leading to any unanticipated bypass which exceeds any effluent limitations in the permit;
      iii. Circumstances leading to any upset which causes an exceedance of any effluent limitation in the permit; or
      iv. Daily maximum violations for any of the pollutants limited by Part I.A of this permit as specified in Part III of this permit. This includes any toxic pollutant or hazardous substance or any pollutant specifically identified as the method to control any toxic pollutant or hazardous substance.
   b. The report shall contain a description of the noncompliance and its cause; the period of noncompliance, including exact dates and times, and if the noncompliance has not been corrected, the anticipated time it is expected to continue; and steps taken or planned to reduce, eliminate, and prevent reoccurrence of the noncompliance.
   c. For noncompliance events related to combined sewer overflows, sanitary sewer overflows, or bypass events, these reports must include the data described above (with the exception of time of discovery) as well as the type of event (combined sewer overflows, sanitary sewer overflows, or bypass events), type of sewer overflow structure (e.g., manhole, combine sewer overflow outfall), discharge volumes untreated by the treatment works treating domestic sewage, types of human health and environmental impacts of the sewer overflow event, and whether the noncompliance was related to wet weather. See 40 CFR 122.41(l)(6)(i).

i. As of December 21, 2020 all reports related to combined sewer overflows, sanitary sewer overflows, or bypass events submitted in compliance with this section must be submitted electronically by the permittee to the Division.

8. Other non-compliance: A permittee must report all instances of noncompliance at the time monitoring reports are due. These reports may be submitted annually in accordance with Regulation 61.8(4)(p) and/or 61.8(5)(f), but may be submitted at a more frequent interval.

M. BYPASS

1. Definitions:

   a. "Bypass" means the intentional diversion of waste streams from any portion of a treatment facility in accordance with 40 CFR §122.41(m)(1)(i) and/or Regulation 61.2(12).
   b. Severe property damage means substantial physical damage to property, damage to the treatment facilities which causes them to become inoperable, or substantial and permanent loss of natural resources which can reasonably be expected to occur in the absence of a bypass. Severe property damage does not mean economic loss caused by delays in production. See 40 CFR §122.41(m)(1)(ii).

2. Bypass not exceeding limitations. The permittee may allow any bypass to occur which does not cause effluent limitations to be exceeded, but only if it also is for essential maintenance to assure efficient operation. These bypasses are not subject to the provisions of 40 CFR 122.41(m)(3) and (m)(4). See 40 CFR §122.41(m)(2).

3. Notice of bypass:

   a. Anticipated bypass. If the permittee knows in advance of the need for a bypass, the permittee shall submit prior notice, if possible, at least ten (10) days before the date of the bypass. See 40 CFR §122.41(m)(3)(i) and/or Regulation 61.9(5)(c).
   b. Unanticipated bypass. You must submit notice of an unanticipated bypass as required in Part II.L.7. See also 40 CFR §122.41(m)(3)(ii).

4. Prohibition of Bypass: Bypasses are prohibited and the Division may take enforcement action against the permittee for bypass, unless:

   a. the bypass is unavoidable to prevent loss of life, personal injury, or severe property damage;
   b. There were no feasible alternatives to the bypass, such as the use of auxiliary treatment facilities, retention of untreated wastes, or maintenance during normal periods of equipment downtime. This condition is not satisfied if adequate backup equipment should have been installed in the exercise of reasonable engineering judgment to prevent a bypass which occurred during normal periods of equipment downtime or preventive maintenance; and
   c. Proper notices were submitted to the Division.
      i. The Division may approve an anticipated bypass, after considering its adverse effects, if the Division determines that it will meet the three conditions listed.

N. UPSET

1. Definition: "Upset" means an exceptional incident in which there is unintentional and temporary noncompliance with technology based permit effluent limitations because of factors beyond the reasonable control of the permittee. An upset does not include noncompliance to the extent caused by operational error, improperly designed treatment facilities, inadequate treatment facilities, lack of preventative maintenance, or careless or improper operation. See 40 CFR §122.41(n) and Regulation 61.2(113).

2. Effect of an upset: An upset constitutes an affirmative defense to an action brought for noncompliance with permit effluent limitations if the requirements of section 3 are met. A determination made during administrative review of claims that noncompliance was caused by upset is final administrative action subject to judicial review in accordance with Regulation 61.8(3)(j).

   ***special note:** this provision is consistent with the definition of "Upset" as codified in Regulation 61.2(113). However, the Colorado regulatory definition of upset is less stringent than the federal code of regulations, which restricts the use of an upset defense to noncompliance with technology-based permit effluent limitations only.*

3. Conditions necessary for demonstration of an Upset: A permittee who wishes to establish the affirmative defense of upset shall demonstrate through properly signed contemporaneous operating logs, or other relevant evidence that:

   a. an upset occurred and the permittee can identify the cause(s) of the upset;
   b. the permitted facility was at the time being properly maintained; and
   c. the permittee submitted notice of the upset as required in Part II.L.7 (24-hour notice); and
   d. The permittee complied with any remedial measure necessary to minimize or prevent any discharge or sludge use or disposal in violation of this permit which has a reasonable likelihood of adversely affecting human health or the environment. See also 40 C.F.R. 122.41(n)(3)(i)-(iv).

   **special note:* this provision is consistent with the definition of "Conditions necessary for demonstration of upset" as codified in Regulation 61.8(3)(j)(ii). However, the Colorado regulatory definition of upset is less stringent than the federal code of regulations, which restricts the use of an upset defense to demonstrate that a facility was properly operated and maintained. Colorado's regulatory definition of "Conditions necessary for demonstration of upset" is less stringent than the requirements of the federal Clean Water Act.*

4. In addition to the demonstration required above, a permittee who wishes to establish the affirmative defense of upset for a violation of effluent limitations based upon water quality standards shall also demonstrate through monitoring, modeling or other methods that the relevant standards were achieved in the receiving water.

5. Burden of Proof: In any enforcement proceeding, the permittee seeking to establish the occurrence of an upset has the burden of proof.

O. REOPENER CLAUSE

Procedures for modification or revocation. Permit modification or revocation of this permit or coverage under this permit will be conducted according to Regulation 61.8(8). This permit may be reopened and modified (following proper administrative procedures) to include the appropriate effluent limitations (and compliance schedule, if necessary), or other appropriate requirements if one of the following events occurs, including but not limited to:

1. Water Quality Standards: The water quality standards of the receiving water(s) to which the permittee discharges are modified in such a manner as to require different effluent limits than contained in this permit.

2. Wasteload Allocation: A wasteload allocation is developed and approved by the State of Colorado and/or EPA for incorporation in this permit.

3. Discharger-specific variance: A variance is adopted by the Water Quality Control Commission.

P. OTHER INFORMATION

When the permittee becomes aware that it failed to submit any relevant facts in a permit application, or submitted incorrect information in a permit application or in any report to the Division or U.S. EPA, the Discharger shall promptly submit such facts or information. See 40 C.F.R. § 122.41(l)(8).

Q. SEVERABILITY

The provisions of this permit are severable. If any provisions or the application of any provision of this permit to any circumstances, is held invalid, the application of such provision to other circumstances and the application of the remainder of this permit shall not be affected.

R. NOTIFICATION REQUIREMENTS

1. Notification to Parties: All notification requirements, excluding application information submitted using the CEOS portal or twenty-four hour reporting via the submission form, shall be directed as follows:

   a. Oral Notifications, during normal business hours shall be to:

      CDPHE-Emergency Reporting Line: 1-877-518-5608; or

      Water Quality Protection Section – Compliance Program
      Water Quality Control Division

Telephone: (303) 692-3500
After hours notifications should be made to the CDPHE-Emergency Reporting Line: 1-877-518-5608.

b. Written notification shall be to:
Water Quality Protection Section – Compliance Program
Water Quality Control Division
Colorado Department of Public Health and Environment
WQCD-WQP-B2
4300 Cherry Creek Drive South
Denver, CO 80246-1530

S. RESPONSIBILITIES

Reduction, Loss, or Failure of Treatment Facility: The permittee has the duty to halt or reduce any activity if necessary to maintain compliance with the effluent limitations of the permit. It shall not be a defense for a permittee in an enforcement action that it would be necessary to halt or reduce the permitted activity in order to maintain compliance with the conditions of this permit.

T. OIL AND HAZARDOUS SUBSTANCES LIABILITY

Nothing in this permit shall be construed to preclude the institution of any legal action or relieve the permittee from any responsibilities, liabilities, or penalties to which the permittee is or may be subject to under Section 311 (Oil and Hazardous Substance Liability) of the Clean Water Act.

U. EMERGENCY POWERS

Nothing in this permit shall be construed to preclude the institution of any legal action or relieve the permittee from any responsibilities, liabilities, or penalties established pursuant to any applicable State law or regulation under authority granted by Section 510 of the Clean Water Act. Nothing in this permit shall be construed to prevent or limit application of any emergency power of the Division.

V. CONFIDENTIALITY

Any information relating to any secret process, method of manufacture or production, or sales or marketing data which has been declared confidential by the permittee, and which may be acquired, ascertained, or discovered, whether in any sampling investigation, emergency investigation, Colorado Open Records Act (CORA) request, or otherwise, shall not be publicly disclosed by any member, officer, or employee of the Water Quality Control Commission or the Division, but shall be kept confidential. Any person seeking to invoke the protection of this section shall bear the burden of proving its applicability. This section shall never be interpreted as preventing full disclosure of effluent data.

W. FEES

The permittee is required to submit payment of an annual fee as set forth in the 2016 amendments to the Water Quality Control Act. Section 25-8-502 (1.1) (b), and the Regulation 61.15 as amended. Failure to submit the required fee when due and payable is a violation of the permit and will result in enforcement action pursuant to Section 25-8-601 et. seq., C.R.S.1973 as amended.

X. DURATION OF PERMIT

The duration of a permit shall be for a fixed term and shall not exceed five (5) years. If the permittee desires to continue to discharge, a permit renewal application shall be submitted at least one hundred eighty (180) calendar days before this permit expires. Filing of a timely and complete application shall cause the expired permit to continue in force to the effective date of the new permit. The permit's duration may be extended only through administrative extensions and not through interim modifications. If the permittee anticipates there will be no discharge after the expiration date of this permit, the Division should be promptly notified so that it can terminate the permit in accordance with Regulation 61.

Y. SECTION 307 TOXICS

If a toxic effluent standard or prohibition, including any applicable schedule of compliance specified, is established

by regulation pursuant to Section 307 of the Clean Water Act for a toxic pollutant which is present in the permittee's discharge and such standard or prohibition is more stringent than any limitation upon such pollutant in the discharge permit, the Division shall institute proceedings to modify or revoke and reissue the permit to conform to the toxic effluent standard or prohibition.

APPENDIX F – CDPHE LOW RISK DISCHARGE GUIDANCE DOCUMENTS

LOW RISK DISCHARGES

Background:

In accordance with the Colorado Water Quality Control Act, and consistent with the federal Clean Water Act, no person shall discharge any pollutant into any state water from a point source without first having obtained a permit from the Water Quality Control Division (Division). The issuance of an individual permit to the operator of each point source, including the enormous number of small point sources, would create a situation of administrative infeasibility for the Division given its limited resources. To streamline the permitting process, the Division has the authority to issue general permits for categories of discharges that involve the same or substantially similar types of operations, discharge the same types of wastes, require the same effluent limits or operating conditions, and require the same monitoring conditions. Once a general permit is issued, operators can apply for certification of coverage and obtain authorization to discharge under the general permit. This approach is particularly useful for categories that have large numbers of discharges across the state.

The Division has used this general permitting approach to cover a wide variety of industrial discharges under the minimal industrial discharge permit, or MINDI. This general permit was specifically designed to cover discharges that are not expected to contain pollutants in toxic concentrations, are small volume, and/or will occur over a very short-term. Both numeric and practice-based regulatory approaches have been used for these types of discharges.

During the MINDI permit renewal process in 2007-2008, the Division attempted to further define and subcategorize the types of industrial discharges that would qualify for coverage. This was to address concerns that the permit covered industry types that were too broad to fit under one permit, meaning that additional general permits would need to be created to address the various categories of discharges previously covered under the MINDI permit. The Division's priority for permitting and compliance is to focus resources on discharges that have the greatest potential to cause water quality impacts. Based on a review of industry types and pollutants expected, the Division has begun to develop new general permits specifically geared to those industrial types, addressing the discharges of most concern first. Through this review, the Division has identified some discharges as low risk discharges, and has also found that few requests for coverage under the MINDI permit have been received for these types of discharges. The Division does not believe it is an efficient use of its limited resources to continue to issue general permits for these discharges.

Policy:

The Division has decided not to issue general permits for minimal industrial discharges with the lowest potential risk to water quality. The Division will develop guidance for these low risk categories of discharges including best management practices (BMPs) intended to be protective of water quality. While regulations do require that operators of point source discharges obtain a CDPS permit, the Division will not take enforcement action for those operators which have not obtained CDPS permit coverage for these discharges, providing that the operator can prove that all appropriate BMPs identified in the guidance have been fully implemented. This approach to enforcement will not apply to criminal violations or in situations where there are egregious circumstances, such as those resulting in serious environmental harm, adverse impacts to the quality of state waters, or which pose an imminent or substantial endangerment to public health and/or the environment.

It should be noted that unpermitted surface water discharges could be subject to third-party or federal enforcement even where BMPs are implemented. Operators wishing to obtain the additional legal protection provided by permit coverage can submit an individual permit application for these discharges to the Division for processing.

Colorado Water Quality Control Division

WATER QUALITY CONTROL DIVISION

Policy No: WQE-10
Initiated By: Dave Akers
Approved By:
Effective Date: 3/1/08
Revision No.:
Revision Date:

Guidance for Reporting Spills under the Colorado Water Quality Control Act and Colorado Discharge Permits

I. Purpose

To provide guidance on applicable Colorado reporting requirements pursuant to § 25-8-601(2), C.R.S., that pertains to spills or discharges that may cause pollution of State waters. This guidance does not relieve an entity of any other statutory or regulatory requirements applicable to a spill. Facilities possessing a Colorado Discharge Permit System (CDPS) permit should follow applicable permit terms and conditions regarding spill reporting and response. This guidance is not intended to supersede or modify such permit terms and conditions or the applicable statute and regulations. This guidance does not limit the existing rights or responsibilities of persons with respect to spill reporting. For example, persons retain the right and responsibility to determine in the first instance whether a particular spill is covered by an existing permit or may cause pollution to State waters (i.e., surface or ground waters).

II. Statutory Requirement Addressed

Colorado Water Quality Control Act - Spill Reporting Requirements - § 25-8-601(2), C.R.S.

> "Any person engaged in any operation or activity which results in a spill or discharge of oil or other substance which may cause pollution of the waters of the state contrary to the provisions of this article as soon as he has knowledge thereof, shall notify the division of such discharge."

State waters means any and all surface and subsurface waters which are contained in or flow in or through this state, but does not include waters in sewage systems, waters in treatment works of disposal systems, waters in potable water distribution systems, and all water withdrawn for use until use and treatment have been completed (§ 25-8-103 (19), C.R.S.).

Examples of State waters include, but are not limited to, perennial streams, intermittent or ephemeral gulches and arroyos, ponds, lakes, reservoirs, irrigation canals or ditches, wetlands, stormwater conveyances (when they discharge to a surface water), and groundwater.

III. Policy/Applicability

The Division distinguishes between reporting requirements for spills that occur with respect to activities that result in a discharge that is authorized under a CDPS permit and those that are not. For non-permitted activities, or in the case of an activity where a permit does not address reporting of or response to a given spill, the Division recommends that the responsible person(s) take the following actions:

1. Immediately report spills that may result in a non-permitted discharge of pollutants to State waters to the Environmental Release and Incident Reporting Line at 1-877-518-5608;
2. Include the following information, if available, when notifying the Division of a spill:
   a. The name of the responsible person and, if not reported by that person, the name of the person reporting the spill and the name of the responsible person if known;
   b. An estimate of the date and time that the spill began or the actual date and time, if known;

c. The location of the spill, its source (e.g., manhole, tanker truck), and identification of the type of material spilled (e.g., untreated wastewater, biosolids, specific chemical);

d. The estimated volume of the spill and, if known, the actual date and time the spill was fully controlled/stopped.

e. Whether the spill is ongoing and, if it is, the rate of flow and an estimate of the time that the spill will be fully controlled, if known;

f. Measures that are being or have been taken to contain, reduce, and/or clean up the spill;

g. A list of any potentially affected area and any known downstream water uses (e.g., public water supplies, irrigation diversions, public use areas such as parks or swim beaches) that will be or have been notified; and

h. A phone number and e-mail to contact a representative of the responsible person that is in charge of the response. Where a non-responsible person is reporting the spill, they are encouraged, but not required, to provide contact information.

Reporting and management of spills that occur with respect to activities resulting in a discharge authorized under a permit should be performed in accordance with the specific requirements of that permit. If the permit does not provide specific reporting or management response requirements for a given spill that may pollute State waters, the Division recommends that the responsible person report the spill in accordance with the procedures listed above.

This guidance only addresses reporting requirements under the Division's authority. The person or entity engaged in any operation or activity that results in a spill is responsible for any other applicable reporting requirements associated with the spill to other regulatory agencies.

Section 25-8-601(2), C.R.S. only addresses spill reporting to the Division. Section 25-8-202(7), C.R.S. provides certain water quality responsibilities to other state "implementing agencies." The Division's position is that, where a spill to the ground that may impact ground water only is fully and timely reported to an implementing agency having jurisdiction over that spill, the intent of section 601(2) has been fulfilled, and the spill need not also be reported to the Division. The Division suggests that the responsible person confirm with the implementing agency that a spill falls under the jurisdiction of the implementing agency at the time it is reported in order to avoid possible legal liability should it fall under the Division's jurisdiction.

IV. Division Examples of Non-Reportable Spills

The Division has identified the following examples of types of spills that are considered "non-reportable" under § 25-8-601(2), C.R.S. Documentation of such spills, including the information listed in section III.2.a – III.2.f above, should be maintained by the responsible person for Division review for a period of three years.

1. A spill to a generally impervious surface or structure (e.g., paved street/parking lot, storm sewer, warehouse floor, manhole, vault, concrete basement), or onto soils, that is fully contained in/on the impervious surface/structure or soils, or that is managed in a manner so that it will not reach State waters at the time of the spill or in the future. Such spills that are cleaned up within 24 hours will be considered by the Division to have no potential to reach State waters. However, even if such spills are not cleaned up within 24 hours, the responsible person may be able to "fully contain" or otherwise manage a spill such that it will not reach State waters. Where there is a sump pump present in a basement to which a spill occurred, the responsible person must establish that the pump did not discharge to State waters during the time between the start of the spill and the completion of clean-up in accordance with best management practices.
2. A spill or discharge that is managed consistent with best management practices that are established in accordance with a CDPS discharge permit or any Water Quality Control Commission-adopted control regulation related to spill management or reporting.
3. A spill of potable water from a public water system that does not reach surface waters.

APPENDIX G – SELF-INSPECTION FORM AND SPILL PREVENTION DOCUMENT

SWMP REPORT REVISION LOG

REVISION #	DATE	BY	COMMENTS

Spill Prevention, Control and Countermeasure (SPCC) Plan

Facility Name: _____
Address: _____
_____

Contact Name: _____
Phone: _____
Fax: _____
Email: _____

Certification: I hereby certify that I have examined the facility, and, being familiar with the provisions of 40 CFR part 112, attest that this SPCC plan has been prepared, or updated within 5 years, in accordance with good engineering practices and meets the requirements listed in 40 CFR part 112.

This plan has been certified by:

Date of certification: _____ *Engineer's Seal*

Copies of this plan are located at the facility and are available to all employees.

Location(s) of plan(s): _____

I. FACILITY INFORMATION

a. Facility Name: _____

b. Mailing Address: _____
_____

c. Physical address if different: _____
_____
_____

d. Owner Name: _____

e. Owner Address: _____
_____

f. Primary Contact Name: _____
Work Phone Number: _____
Home Phone Number: _____
Mobile Phone Number: _____

g. Secondary Contact Name:
Work Phone Number: _____
Home Phone Number: _____
Mobile Phone Number: _____

h. Date of Initial Operation: _____

II. SITE ASSESSMENT

a. Location:
Describe where facility is located. For example, "This site is located along Broad Creek about 2 miles north of its confluence with the Choptank River at Holland Point. Road access is from. . . . The site is located on Talbot County ADC map 22 (H5). Latitude is ___ and longitude is ___ ."

_____
_____
_____
_____
_____
_____
_____
_____
_____
_____
_____

III. FACILITY DESCRIPTION

a. Acres of land: ____

b. Facilities and Equipment:
Place an X beside all that apply.

____ Garage for vehicle processing
____ Parts store
____ On-site crushcr
_____Impervious crush pad for crusher
____ Impervious pad for outside vehicle processing
____ Spill kit/emergency equipment
____ Refrigerant (Freon) extractor
____ Parts washer
____ Other structures and major equipment:

Please list: _____
_____
_____
_____
_____

c. Services:
Place an X beside all that apply.

____ Dismantler/Recycler
____ Sell used parts
____ Sell vehicles for scrap
_____Crushing
____ Auto body/repair shop
____ Sell used cars
____ Other services:

Please list: _____
_____
_____
_____

d. Fixed Storage:
List capacity and contents of each storage container. For example, "One 6,000 gallon above ground tank containing diesel fuel." Be sure to include diesel, gasoline, waste oil, heating oil, kerosene, paint thinner and other solvents. Also describe the construction of the containers, secondary containment for each, liquid level indicators, alarms and method of corrosion protection for each container._____

e. Non-Fixed Storage:
List capacity and contents of each storage container. For example, "One 55 gallon drum for recycled oil." Be sure to indicate what each container is used for, its condition and construction and how secondary containment is provided. _____

f. Total quantity of stored materials:
The combined quantity of the materials listed above: _____ gallons

IV. OIL SPILL HISTORY

Place an X on the appropriate line and proceed accordingly.

___ There has never been a significant spill at the above named facility.

___ There have been one or more significant spills at the above named facility. Details of such spill(s) are described below.

For each spill that occurred, supply the following information:

- Type and amount of oil spilled
- Location, date and time of spill(s)
- Watercourse affected
- Description of physical damage
- Cost of damage
- Cost of clean-up
- Cause of spill
- Action taken to prevent recurrence

V. POTENTIAL SPILL VOLUMES AND RATES

Fill in all applicable blanks. Be prepared to show the engineer documentation of flow rates. Your fuel vendor and the manufacturer of your storage and dispensing equipment should be able to provide this documentation.

Potential Event	Volume Released	Spill Rate
Complete failure of a full tank*	____ gallons	instantaneous
Partial failure of a full tank*	1 to ____ gallons	gradual to instantaneous
Tank overflow**	1 to ____ gallons	up to ____ gallons per minute
Leaking during unloading***	up to ____ gallons	up to ____ gallons per minute
Pipe failure****	up to ____ gallons	up to ____ gallons per minute
Leaking pipe or valve****	several ounces to gallons	up to ____ gallons per minute
Fueling operations****	several ounces to gallons	up to ____ gallons per minute
Oil and grease	several ounces to quarts	spotting

* Volume of largest tank
** Calculate using the rate at which fuel is dispensed from the delivery truck into your tank(s).
*** Calculate using the rate at which petroleum would be withdrawn from the tank if it should have to be emptied (*e.g.*, if it was being taken out of service).
**** Calculate based on the specifications of your equipment.

VI. SPILL PREVENTION AND CONTROL

a. Spill Prevention:
Provide specific descriptions of containment facilities and practices. Include description of items such as double-walled tanks, containment berms, emergency shut-offs, drip pans, fueling procedures and spill response kits. Also, describe how and when employees are trained in proper handling procedures and spill prevention and response procedures.

b. Spill discharge and flow:
For each potential spill source, describe where petroleum would flow in the event of a spill. For example, "The 6,000 gallon diesel tank has a pre-manufactured secondary containment system capable of holding 110 percent of the total volume of the tank" and, "A spill from engine repair would be contained inside the shop building and quickly cleaned up with oil absorbents." Incorporate site map by reference (see instructions under *Appendices*).

c. Spill response:
Identify what equipment would be deployed by whom and in what situation. Also, include phone numbers for response agencies, *e.g.*, U.S. Coast Guard, fire department, spill response contractors, etc. A copy of your spill response plan may be attached as an appendix to this SPCC plan in lieu of completing this section.

d. Security
Provide a description of how all containers are protected when the facility is not in operation or unattended. Include a description of fencing, access control, gates, locks, etc. that prevent access by unauthorized individuals.

VII. FACILITY INSPECTIONS

a. Routine Inspections

Name facilities and the frequency with which they are inspected. For example, "The fuel pumps are inspected daily. The materials storage area is inspected monthly." Describe all facility containers, piping, etc. that is to be inspected. Name the person who has responsibility to implement preventative maintenance programs, oversee on-site inspections, coordinate employee training, maintain records, update the plan as necessary, and ensure that reports are submitted to the proper authorities.

b. Annual Inspections

Include a description of annual comprehensive inspections. For example, "A site inspection is also conducted annually by appropriate responsible personnel to verify that the description of potential pollutant sources are accurate, that the map reflects current site conditions, and that the controls to reduce the pollutants identified in this plan are being implemented and are adequate. This annual inspection will be conducted above and beyond the routine inspections done focusing on designated equipment and areas where potential sources are located."

VIII. RECORD KEEPING

Describe record keeping procedures. For example, "Record keeping procedures consist of maintaining all records a minimum of three years. The following items will be kept on file: current SPCC plan, internal site reviews, training records, and documentation of any spills or maintenance conducted in regards to these sites." *Maintenance Inspection*, *Employee Training*, and *Record Keeping* logs are included in this template for your use.

IX. MAINTENANCE INSPECTIONS

Maintenance Coordinator: _____. Maintenance Coordinator responsibilities include implementation of preventative maintenance programs and oversight of on-site inspections.

Use this table to record inspections:

Facility Inspected	Date of Inspection	Name of Inspector	Result Pass/Fail	Comments

X. RECORD KEEPING OF INCIDENTAL SPILLS

Record Keeper: _____. Record Keeper responsibilities include maintaining records of incidents, updating the SPCC plan as necessary and ensuring reports are submitted to the proper authorities when necessary.

Incident No.	Type of Incident	Date of Occurrence	How it was Cleaned Up

APPENDIX H – OTHER DOCUMENTS AND CREDENTIALS
